


Overall Project Schedule_Level 2																							
ID	Task Name	Duration	Start	Finish	Critical	Baseline Start	Baseline Finish	Baseline1 Start	Baseline1 Finish	Actual Start	Actual Finish	% Complete	2025	H1	H2	2026	H1	H2	2027	H1	H2	2028	H1
1	1 Industrial waste-to-energy power plant (PWW1)	836 days	8/1/25	11/14/27	Yes	9/15/25	11/14/27	8/1/25	11/14/27	8/1/25		NA	20%										
2	1.1 Project Milestone	820 days	8/17/25	11/14/27	Yes	9/15/25	11/14/27	8/17/25	11/14/27	8/17/25		NA	0%										
3	1.1.1 LNTP	0 days	9/15/25	9/15/25	No	9/15/25	9/15/25	9/15/25	9/15/25	9/15/25	9/15/25	100%											
4	1.1.2 Incinerator Procurement Order	0 days	8/17/25	8/17/25	No	10/25/25	10/25/25	8/17/25	8/17/25	8/17/25	8/17/25	100%											
5	1.1.3 Boiler Procurement Order	0 days	8/17/25	8/17/25	No	10/24/25	10/24/25	8/17/25	8/17/25	8/17/25	8/17/25	100%											
6	1.1.4 Steam turbine Procurement Order	0 days	9/28/25	9/28/25	No	12/2/25	12/2/25	9/28/25	9/28/25	9/28/25	9/28/25	100%											
7	1.1.5 Flue gas treatment Procurement Order	0 days	9/28/25	9/28/25	No	12/2/25	9/28/25	9/28/25	9/28/25	9/28/25	9/28/25	100%											
8	1.1.6 1st batch of the Boiler Structure EXW	0 days	3/7/26	3/7/26	No	4/17/26	4/17/26	4/11/26	4/11/26	NA		0%											
9	1.1.7 Incinerator EXW	0 days	4/22/26	4/22/26	No	5/20/26	5/20/26	4/30/26	4/30/26	NA		0%											
10	1.1.8 Flue Gas Treatment EXW	0 days	8/10/26	8/10/26	No	6/18/26	6/18/26	8/10/26	8/10/26	NA		0%											
11	1.1.9 Incinerator Arrival at site	0 days	6/20/26	6/20/26	No	6/17/26	6/17/26	5/28/26	5/28/26	NA		0%											
12	1.1.10 Boiler EXW	0 days	5/30/26	5/30/26	No	5/20/26	5/20/26	5/30/26	5/30/26	NA		0%											
13	1.1.11 Steam turbine EXW	0 days	10/23/26	10/23/26	No	11/17/26	11/17/26	10/30/26	10/30/26	NA		0%											
14	1.1.12 Boiler Arrival at site	0 days	6/27/26	6/27/26	No	6/17/26	6/17/26	6/27/26	6/27/26	NA		0%											
15	1.1.13 Steam turbine Arrival at site	0 days	11/21/26	11/21/26	No	12/16/26	12/16/26	11/28/26	11/28/26	NA		0%											
16	1.1.14 Main building underground foundation completion	0 days	5/25/26	5/25/26	No	6/15/26	6/15/26	5/25/26	5/25/26	NA		0%											
17	1.1.15 Boiler foundation clearance for equipment installation	0 days	7/4/26	7/4/26	Yes	5/21/26	5/21/26	7/4/26	7/4/26	NA		0%											
18	1.1.16 Turbine building clearance for equipment installation	0 days	12/15/26	12/15/26	No	10/29/26	10/29/26	12/15/26	12/15/26	NA		0%											
19	1.1.17 Flue gas treatment system foundation clearance for equipment installation	0 days	6/18/26	6/18/26	No	6/27/26	6/18/26	6/27/26	6/18/26	NA		0%											
20	1.1.18 Refuse crane clearance for installation	0 days	12/15/26	12/15/26	No	1/9/27	1/9/27	12/15/26	12/15/26	NA		0%											
21	1.1.19 Boiler Hydrostatic pressure test start	0 days	1/18/27	1/18/27	No	1/18/27	1/18/27	1/18/27	1/18/27	NA		0%											
22	1.1.20 Steam turbine body installation completion	0 days	2/5/27	2/5/27	No	2/6/27	2/5/27	2/5/27	2/5/27	NA		0%											
23	1.1.21 Grid power energization	0 days	2/18																				

Overall Project Schedule_Level 2																								
ID	Task Name	Duration	Start	Finish	Critical	Baseline Start	Baseline Finish	Baselinel Start	Baselinel Finish	Actual Start	Actual Finish	% Complete	2025	H1	H2	2026	H1	H2	2027	H1	H2	2028	H1	
165	1.4.1.11.6 Instrument Enclosure,Rack and Stanchion	26 days	5/1/26	5/30/26	No	3/26/26	4/29/26	5/1/26	5/30/26	5/1/26		NA	70%											
166	1.4.1.11.7 Cable and raceway system (C&I)	39 days	4/16/26	5/30/26	No	3/18/26	4/27/26	4/16/26	5/30/26	NA		NA	0%											
167	1.4.2 Manufacture design Submission and approval	96 days	8/18/25	12/7/25	No	10/25/25	2/10/26	8/18/25	12/7/25	8/18/25	12/7/25	100%												
168	1.4.2.1 Incinerator	30 days	8/18/25	9/20/25	No	10/27/25	11/29/25	8/18/25	9/20/25	8/18/25	9/20/25	100%												
169	1.4.2.2 Boiler	30 days	8/18/25	9/20/25	No	10/25/25	11/28/25	8/18/25	9/20/25	8/18/25	9/20/25	100%												
170	1.4.2.3 Turbine generator unit (Include Turbine Control System, Generator)	54 days	10/5/25	12/7/25	No	12/3/25	2/10/26	10/5/25	12/7/25	10/5/25	12/7/25	100%												
171	1.4.2.4 Flue gas treatment	30 days	10/5/25	11/9/25	No	12/3/25	1/17/26	10/5/25	11/9/25	10/5/25	11/9/25	100%												
172	1.4.3 Manufacturing	375 days	9/22/25	12/2/26	No	11/29/25	11/17/26	9/28/25	12/2/26	9/22/25		NA	3%											
173	1.4.3.1 Incinerator (Include Boiler Control System)	183 days	5/22/25	4/22/26	No	12/1/25	5/20/26	9/30/25	4/30/26	NA		NA	0%											
174	1.4.3.2 Boiler foundation anchor bolts	80 days	9/28/25	12/30/25	No	11/29/25	3/2/26	9/28/25	12/30/25	9/28/25	12/30/25	100%												
175	1.4.3.3 Boiler structure	144 days	9/22/25	3/7/26	No	11/29/25	4/17/26	10/26/25	4/11/26	NA		NA	0%											
176	1.4.3.4 Boiler equipment	186 days	10/26/25	5/30/26	No	11/29/25	5/20/26	10/26/25	5/30/26	10/26/25		NA	5%											
177	1.4.3.5 STG foundation anchor bolts, condenser metal sheet	216 days	12/8/25	8/15/26	No	2/11/26	6/30/26	12/8/25	8/15/26	NA		NA	0%											
178	1.4.3.6 Turbine generator unit (Include Turbine Control System, Generator)	275 days	12/8/25	10/23/26	No	2/11/26	11/17/26	12/14/25	10/30/26	NA		NA	0%											
179	1.4.3.7 Flue gas treatment system anchor bolts	22 days	11/16/25	12/11/25	No	1/19/26	2/11/26	11/16/25	12/11/25	11/16/25	12/11/25	100%												
180	1.4.3.8 Flue gas treatment system	229 days	11/16/25	8/10/26	No	1/19/26	6/18/26	11/16/25	8/10/26	11/16/25		NA	3%											
181	1.4.3.9 Refuse crane	262 days	12/19/25	10/20/26	No	2/19/26	9/16/26	12/19/25	10/20/26	12/19/25		NA	2%											
182	1.4.3.10 STG crane	184 days	12/19/25	7/21/26	No	2/19/26	9/16/26	12/19/25	7/21/26	12/19/25		NA	3%											
183	1.4.3.11 Compressed air system	153 days	3/17/26	9/10/26	No	2/19/26	9/16/26	3/17/26	9/10/26	NA		NA	0%											
184	1.4.3.12 Boiler Auxiliary system	167 days	12/28/25	7/10/26	No	4/13/26	8/29/26	12/28/25	7/10/26	12/28/25		NA	4%											
185	1.4.3.12.1 Primary fan (Including Motor System)	167 days	12/28/25	7/10/26	No	4/13/26	8/29/26	12/28/25	7/10/26	12/28/25		NA	4%											
186	1.4.3.12.2 Secondary fan (Including Motor System)	167 days	12/28/25	7/10/26	No	4/13/26	8/29/26	12/28/25	7/10/26	12/28/25		NA	4%											
187	1.4.3.12.3 Induced Draft fan (Including Motor System)	167 days	12/28/25	7/10/26	No	4/13/26	8/29/26	12/28/25	7/10/26	12/28/25		NA	4%											
188	1.4.3.12.4 Flue gas recirculation fan (Including Motor System)	167 days	12/28/25	7/10/26	No	4/13/26	8/29/26	12/28/25	7/10/26	12/28/25		NA	4%											
189	1.4.3.12.5 Furnace cooling fan system (Including Motor System)	167 days	12/28/25	7/10/26	No	4/13/26	8/29/26	12/28/25	7/10/26	12/28/25		NA	4%											
190	1.4.3.13 STG Auxiliary Systems	170 days	2/21/26	9/7/26	No	4/24/26	9/10/26	2/21/26	9/7/26	2/21/26		NA	4%											
191	1.4.3.14 Electric system	282 days	1/8/26	12/2/26	No	3/23/26	9/26/26	1/8/26	12/2/26	NA		NA	0%											
192	1.4.3.14.1 Step-up Transformer	227 days	3/13/26	12/2/26	No	3/24/26	9/25/26	3/13/26	12/2/26	NA		NA	0%											
193	1.4.3.14.2 Generator outlet cabinet	155 days	4/16/26	10/13/26	No	4/6/26	8/22/26	4/16/26	10/13/26	NA		NA	0%											
194	1.4.3.14.3 22 kV switchgear and distribution system	155 days	4/16/26	10/13/26	No	4/6/26	8/22/26	4/16/26	10/13/26	NA		NA	0%											
195	1.4.3.14.4 11kV Switchgear	155 days	4/16/26	10/13/26	No	4/6/26	8/22/26	4/16/26	10/13/26	NA		NA	0%											
196	1.4.3.14.5 11kV VFD	155 days	4/16/26	10/13/26	No	4/13/26	8/29/26	4/16/26	10/13/26	NA		NA	0%											
197	1.4.3.14.6 Auxiliary transformer	160 days	5/1/26	11/3/26	No	3/25/26	9/26/26	5/1/26	11/3/26	NA		NA	0%											
198	1.4.3.14.7 Emergency Diesel Generator	148 days	4/16/26	10/5/26	No	4/25/26	8/31/26	4/16/26	10/5/26	NA		NA	0%											
199	1.4.3.14.8 Batteries/DC/UPS	166 days	5/1/26	11/10/26	No	4/18/26	8/29/26	5/1/26	11/10/26	NA		NA	0%											
200	1.4.3.14.9 Relay and protection panel	142 days	5/1/26	10/13/26	No	4/8/26	8/31/26	5/1/26	10/13/26	NA		NA	0%											
201	1.4.3.14.10 Revenue meter and synchronization	124 days	5/22/26	10/13/26	No	4/13/26	9/4/26	5/22/26	10/13/26	NA		NA	0%											
202	1.4.3.14.11 LV Switchgear/Distribution board	131 days	5/1/26	9/30/26	No	4/18/26	9/4/26	5/1/26	9/30/26	NA		NA	0%											
203	1.4.3.14.12 Cable and raceway system (EE)	131 days	6/1/26	10/30/26	No	4/28/26	9/14/26	6/1/26	10/30/26	NA		NA	0%											
204	1.4.3.14.13 Grounding and Lightning Protection System	203 days	1/8/26	9/1/26	No	4/4/26	8/21/26	1/8/26	9/1/26	NA		NA	0%											
205	1.4.3.14.14 Lighting and Small Power	176 days	1/12/26	8/4/26	No	3/23/26	8/8/26	1/12/26	8/4/26	NA		NA	0%											
206	1.4.3.14.15 Communication system (telephone, paging, intercom, LAN)	142 days	5/22/26	11/3/26	No	4/18/26	8/12/26	6/1/26	11/12/26	NA		NA	0%											
207	1.4.3.15 C&I system	200 days	4/11/26	11/30/26	No	4/24/26	9/16/26	4/11/26	11/30/26	NA		NA	0%											
208	1.4.3.15.1 DCS (Include Boiler Control System)	200 days	4/11/26	11/30/26	No	4/30/26	9/16/26	4/11/26	11/30/26	NA		NA	0%											
209	1.4.3.15.2 CEMS	170 days	4/11/26	10/26/26	No	4/24/26	9/10/26	4/11/26	10/26/26	NA		NA	0%											
210	1.4.3.15.3 CCTV system	131 days	6/1/26	10/30/26	No	4/24/26	7/25/26	6/1/26	10/30/26	NA		NA	0%											
211	1.4.3.15.4 Fire Alarm and detection system	90 days	6/1/26	9/12/26	No	4/30/26	6/3/26	6/1/26	9/12/26	NA		NA	0%											
212	1.4.3.15.5 Instrument and Analyzer	131 days	6/1/26	10/30/26	No	4/30/26	8/12/26	6/1/26	10/30/26	NA		NA	0%											
213	1.4.3.15.6 Instrument Enclosure,Rack and Stanchion	131 days	6/1/26	10/30/26	No	4/30/26	8/12/26	6/1/26	10/30/26	NA		NA	0%											
214	1.4.3.15.7 Cable and raceway system (C&I)	118 days	6/1/26	10/15/26	No	4/28/26	9/14/26	6/1/26	10/15/26	NA		NA	0%											
215	1.4.4 Shipment	276 days	1/11/26	11/28/26	No	2/12/26	12/8/26	1/11/26	11/28/26	1/11/26		NA	8%											
216	1.4.4.1 Incinerator equipment (Include Boiler Control System)	17 days	4/23/26	5/12/26	No	5/21/26	6/9/26	5/1/26	5/20/26	4/23/26	5/12/26	100%												
217	1.4.4.2 Boiler foundation anchor bolts	8 days	1/11/26	1/20/26	No	3/3/26	3/23/26	1/11/26	1/20/26	1/11/26	1/20/26	100%												
218	1.4.4.3 Boiler structure	17 days	3/9/26	3/27/26	No	4/18/26	5/8/26	4/13/26	5/1/26	NA		NA	0%											
219	1.4.4.4 Boiler equipment	18 days	6/1/26	6/20/26	No	5/21/26	6/10/26	6/1/26	6/20/26	NA		NA	0%											
220	1.4.4.5 STG foundation anchor bolts	18 days	8/17/26	9/5/26	No	7/1/26	7/21/26	8/17/26	9/5/26	NA		NA	0%											
221	1.4.4.6 Turbine generator unit (Include Turbine Control System, Generator)	18 days	10/24/26	11/13/26	No	11/18/26	12/8/26	10/31/26	11/20/26	NA		NA	0%											
222	1.4.4.7 Flue gas treatment system anchor bolts	8 days	1/11/26	1/20/26	No	2/12/26	3/4/26	1/11/26	1/20/26	1/11/26	1/20/26	100%												
223	1.4.4.8 Flue gas treatment system	15 days	8/11/26	8/27/26	No	6/19/26	7/6/26	8/11/26	8/27/26	NA		NA	0%											
224	1.4.4.9 Refuse crane	15 days	10/21/26	11/6/26	No	9/17/26	10/3/26	10/21/26	11/6/26	NA		NA	0%											
225	1.4.4.10 STG crane	15 days	7/22/26	8/7/26	No	9/17/26	10/3/26	7/22/26	8/7/26	NA		NA	0%											
226	1.4.4.11 Compressed air system	15 days	9/11/26	9/28/26	No	9/17/26	10/3/26	9/11/26	9/28/26	NA		NA	0%											
227	1.4.4.12 Boiler Auxiliary system	7 days	7/11/26	7/18/26	No	8/31/26	9/7/26	7/11/26	7/18/26	NA		NA	0%											
228	1.4.4.12.1 Primary fan (Including Motor System)	7 days	7/11/26	7/18/26	No	8/31/26	9/7/26	7/11/26	7/18/26	NA		NA	0%											
229	1.4.4.12.2 Secondary fan (Including Motor System)	7 days	7/11/26	7/18/26	No	8/31/26	9/7/26	7/11/26	7/18/26	NA		NA	0%											
230	1.4.4.12.3 Induced Draft fan (Including Motor System)	7 days	7/11/26	7/18/26	No	8/31/26	9/7/26	7/11																

Overall Project Schedule_Level 2																									
ID	Task Name	Duration	Start	Finish	Critical	Baseline Start	Baseline Finish	Baseline1 Start	Baseline1 Finish	Actual Start	Actual Finish	% Complete	2025	H1		H2	2026	H1	H2	2027	H1	H2	2028	H1	
247	1.4.5.2 Boiler foundation anchor bolts (Supplied by boiler supplier)	7 days	2/3/26	2/10/26	No	3/24/26	4/3/26	2/3/26	2/10/26	2/3/26	2/10/26	100%													
248	1.4.5.3 Boiler structure	7 days	3/28/26	4/4/26	No	5/9/26	5/16/26	5/2/26	5/9/26	NA	NA	0%													
249	1.4.5.4 Boiler equipment	6 days	6/22/26	6/27/26	No	6/11/26	6/17/26	6/22/26	6/27/26	NA	NA	0%													
250	1.4.5.5 STG foundation anchor bolts	30 days	9/7/26	10/10/26	No	7/22/26	8/25/26	9/7/26	10/10/26	NA	NA	0%													
251	1.4.5.6 Turbine generator unit (Include Turbine Control System, Generator)	7 days	11/14/26	11/21/26	No	12/9/26	12/16/26	11/21/26	11/28/26	NA	NA	0%													
252	1.4.5.7 Flue gas treatment system anchor bolts	7 days	2/3/26	2/10/26	No	3/5/26	3/12/26	2/3/26	2/10/26	2/3/26	2/10/26	100%													
253	1.4.5.8 Flue gas treatment system	7 days	8/28/26	9/4/26	No	7/7/26	7/14/26	8/28/26	9/4/26	NA	NA	0%													
254	1.4.5.9 Refuse crane	15 days	11/7/26	11/24/26	No	10/5/26	10/21/26	11/7/26	11/24/26	NA	NA	0%													
255	1.4.5.10 STG crane	15 days	8/8/26	8/25/26	No	10/5/26	10/21/26	8/8/26	8/25/26	NA	NA	0%													
256	1.4.5.11 Compressed air system	15 days	9/29/26	10/15/26	No	10/5/26	10/21/26	9/29/26	10/15/26	NA	NA	0%													
257	1.4.5.12 Boiler Auxiliary system	7 days	7/20/26	7/27/26	No	9/8/26	9/15/26	7/20/26	7/27/26	NA	NA	0%													
258	1.4.5.12.1 Primary fan (Including Motor System)	7 days	7/20/26	7/27/26	No	9/8/26	9/15/26	7/20/26	7/27/26	NA	NA	0%													
259	1.4.5.12.2 Secondary fan (Including Motor System)	7 days	7/20/26	7/27/26	No	9/8/26	9/15/26	7/20/26	7/27/26	NA	NA	0%													
260	1.4.5.12.3 Induced Draft fan (Including Motor System)	7 days	7/20/26	7/27/26	No	9/8/26	9/15/26	7/20/26	7/27/26	NA	NA	0%													
261	1.4.5.12.4 Flue gas recirculation fan (Including Motor System)	7 days	7/20/26	7/27/26	No	9/8/26	9/15/26	7/20/26	7/27/26	NA	NA	0%													
262	1.4.5.12.5 Furnace cooling fan system (Including Motor System)	7 days	7/20/26	7/27/26	No	9/8/26	9/15/26	7/20/26	7/27/26	NA	NA	0%													
263	1.4.5.13 STG Auxiliary Systems	10 days	9/25/26	10/6/26	No	9/29/26	10/9/26	9/25/26	10/6/26	NA	NA	0%													
264	1.4.5.14 Electrical system	113 days	8/5/26	12/14/26	No	8/10/26	10/13/26	8/5/26	12/14/26	NA	NA	0%													
265	1.4.5.14.1 Step-up Transformer	10 days	12/3/26	12/14/26	No	9/26/26	10/7/26	12/3/26	12/14/26	NA	NA	0%													
266	1.4.5.14.2 Generator outlet cabinet	10 days	11/6/26	11/17/26	No	9/16/26	9/26/26	11/6/26	11/17/26	NA	NA	0%													
267	1.4.5.14.3 22 kV switchgear and distribution system	10 days	11/6/26	11/17/26	No	9/16/26	9/26/26	11/6/26	11/17/26	NA	NA	0%													
268	1.4.5.14.4 11kV Switchgear	10 days	11/6/26	11/17/26	No	9/16/26	9/26/26	11/6/26	11/17/26	NA	NA	0%													
269	1.4.5.14.5 11kV VFD	10 days	11/6/26	11/17/26	No	9/23/26	10/3/26	11/6/26	11/17/26	NA	NA	0%													
270	1.4.5.14.6 Auxiliary transformer	10 days	11/4/26	11/14/26	No	9/28/26	10/8/26	11/4/26	11/14/26	NA	NA	0%													
271	1.4.5.14.7 Emergency Diesel Generator	10 days	10/6/26	10/16/26	No	9/1/26	9/11/26	10/6/26	10/16/26	NA	NA	0%													
272	1.4.5.14.8 Batteries/DC/UPS	7 days	11/11/26	11/18/26	No	8/31/26	9/7/26	11/11/26	11/18/26	NA	NA	0%													
273	1.4.5.14.9 Relay and protection panel	10 days	11/6/26	11/17/26	No	9/24/26	10/5/26	11/6/26	11/17/26	NA	NA	0%													
274	1.4.5.14.10 Revenue meter and synchronization	10 days	11/6/26	11/17/26	No	9/29/26	10/9/26	11/6/26	11/17/26	NA	NA	0%													
275	1.4.5.14.11 LV Switchgear/Distribution board	10 days	10/24/26	11/4/26	No	9/29/26	10/9/26	10/24/26	11/4/26	NA	NA	0%													
276	1.4.5.14.12 Cable and raceway system (EE)	10 days	11/18/26	11/28/26	No	10/2/26	10/13/26	11/18/26	11/28/26	NA	NA	0%													
277	1.4.5.14.13 Grounding and Lightning Protection System	10 days	9/2/26	9/12/26	No	8/22/26	9/2/26	9/2/26	9/12/26	NA	NA	0%													
278	1.4.5.14.14 Lighting and Small Power	10 days	8/5/26	8/15/26	No	8/10/26	8/20/26	8/5/26	8/15/26	NA	NA	0%													
279	1.4.5.14.15 Communication system (telephone, paging, intercom, LAN)	10 days	11/4/26	11/14/26	No	8/13/26	8/24/26	11/13/26	11/24/26	NA	NA	0%													
280	1.4.5.15 C&I	82 days	9/14/26	12/17/26	No	6/4/26	10/13/26	9/14/26	12/17/26	NA	NA	0%													
281	1.4.5.15.1 DCS (Include Boiler Control System)	15 days	12/1/26	12/17/26	No	9/17/26	10/3/26	12/1/26	12/17/26	NA	NA	0%													
282	1.4.5.15.2 CCTV system	10 days	11/30/26	12/10/26	No	8/25/26	9/4/26	11/30/26	12/10/26	NA	NA	0%													
283	1.4.5.15.3 Fire Alarm and detection system	5 days	9/14/26	9/18/26	No	6/4/26	6/9/26	9/14/26	9/18/26	NA	NA	0%													
284	1.4.5.15.4 CEMS	20 days	10/27/26	11/18/26	No	9/11/26	10/3/26	10/27/26	11/18/26	NA	NA	0%													
285	1.4.5.15.5 Instrument and Analyzer	20 days	11/18/26	12/10/26	No	8/31/26	9/22/26	11/18/26	12/10/26	NA	NA	0%													
286	1.4.5.15.6 Instrument Enclosure,Rack and Stanchion	20 days	11/18/26	12/10/26	No	8/31/26	9/22/26	11/18/26	12/10/26	NA	NA	0%													
287	1.4.5.15.7 Cable and raceway system (C&I)	10 days	11/18/26	11/28/26	No	10/2/26	10/13/26	11/18/26	11/28/26	NA	NA	0%													
288	1.5 Construction	508 days	10/10/25	5/25/27	No	12/11/25	5/17/27	10/10/25	5/25/27	10/10/25	NA	7%													
289	1.5.1 Temporary Construction	56 days	12/29/25	3/3/26	No	12/29/25	3/23/26	12/29/25	3/3/26	12/29/25	3/3/26	100%													
290	1.5.1.1 Temporary site office	56 days	12/29/25	3/3/26	No	12/29/25	3/3/26	12/29/25	3/3/26	12/29/25	3/3/26	100%													
291	1.5.1.2 Temporary fence																								

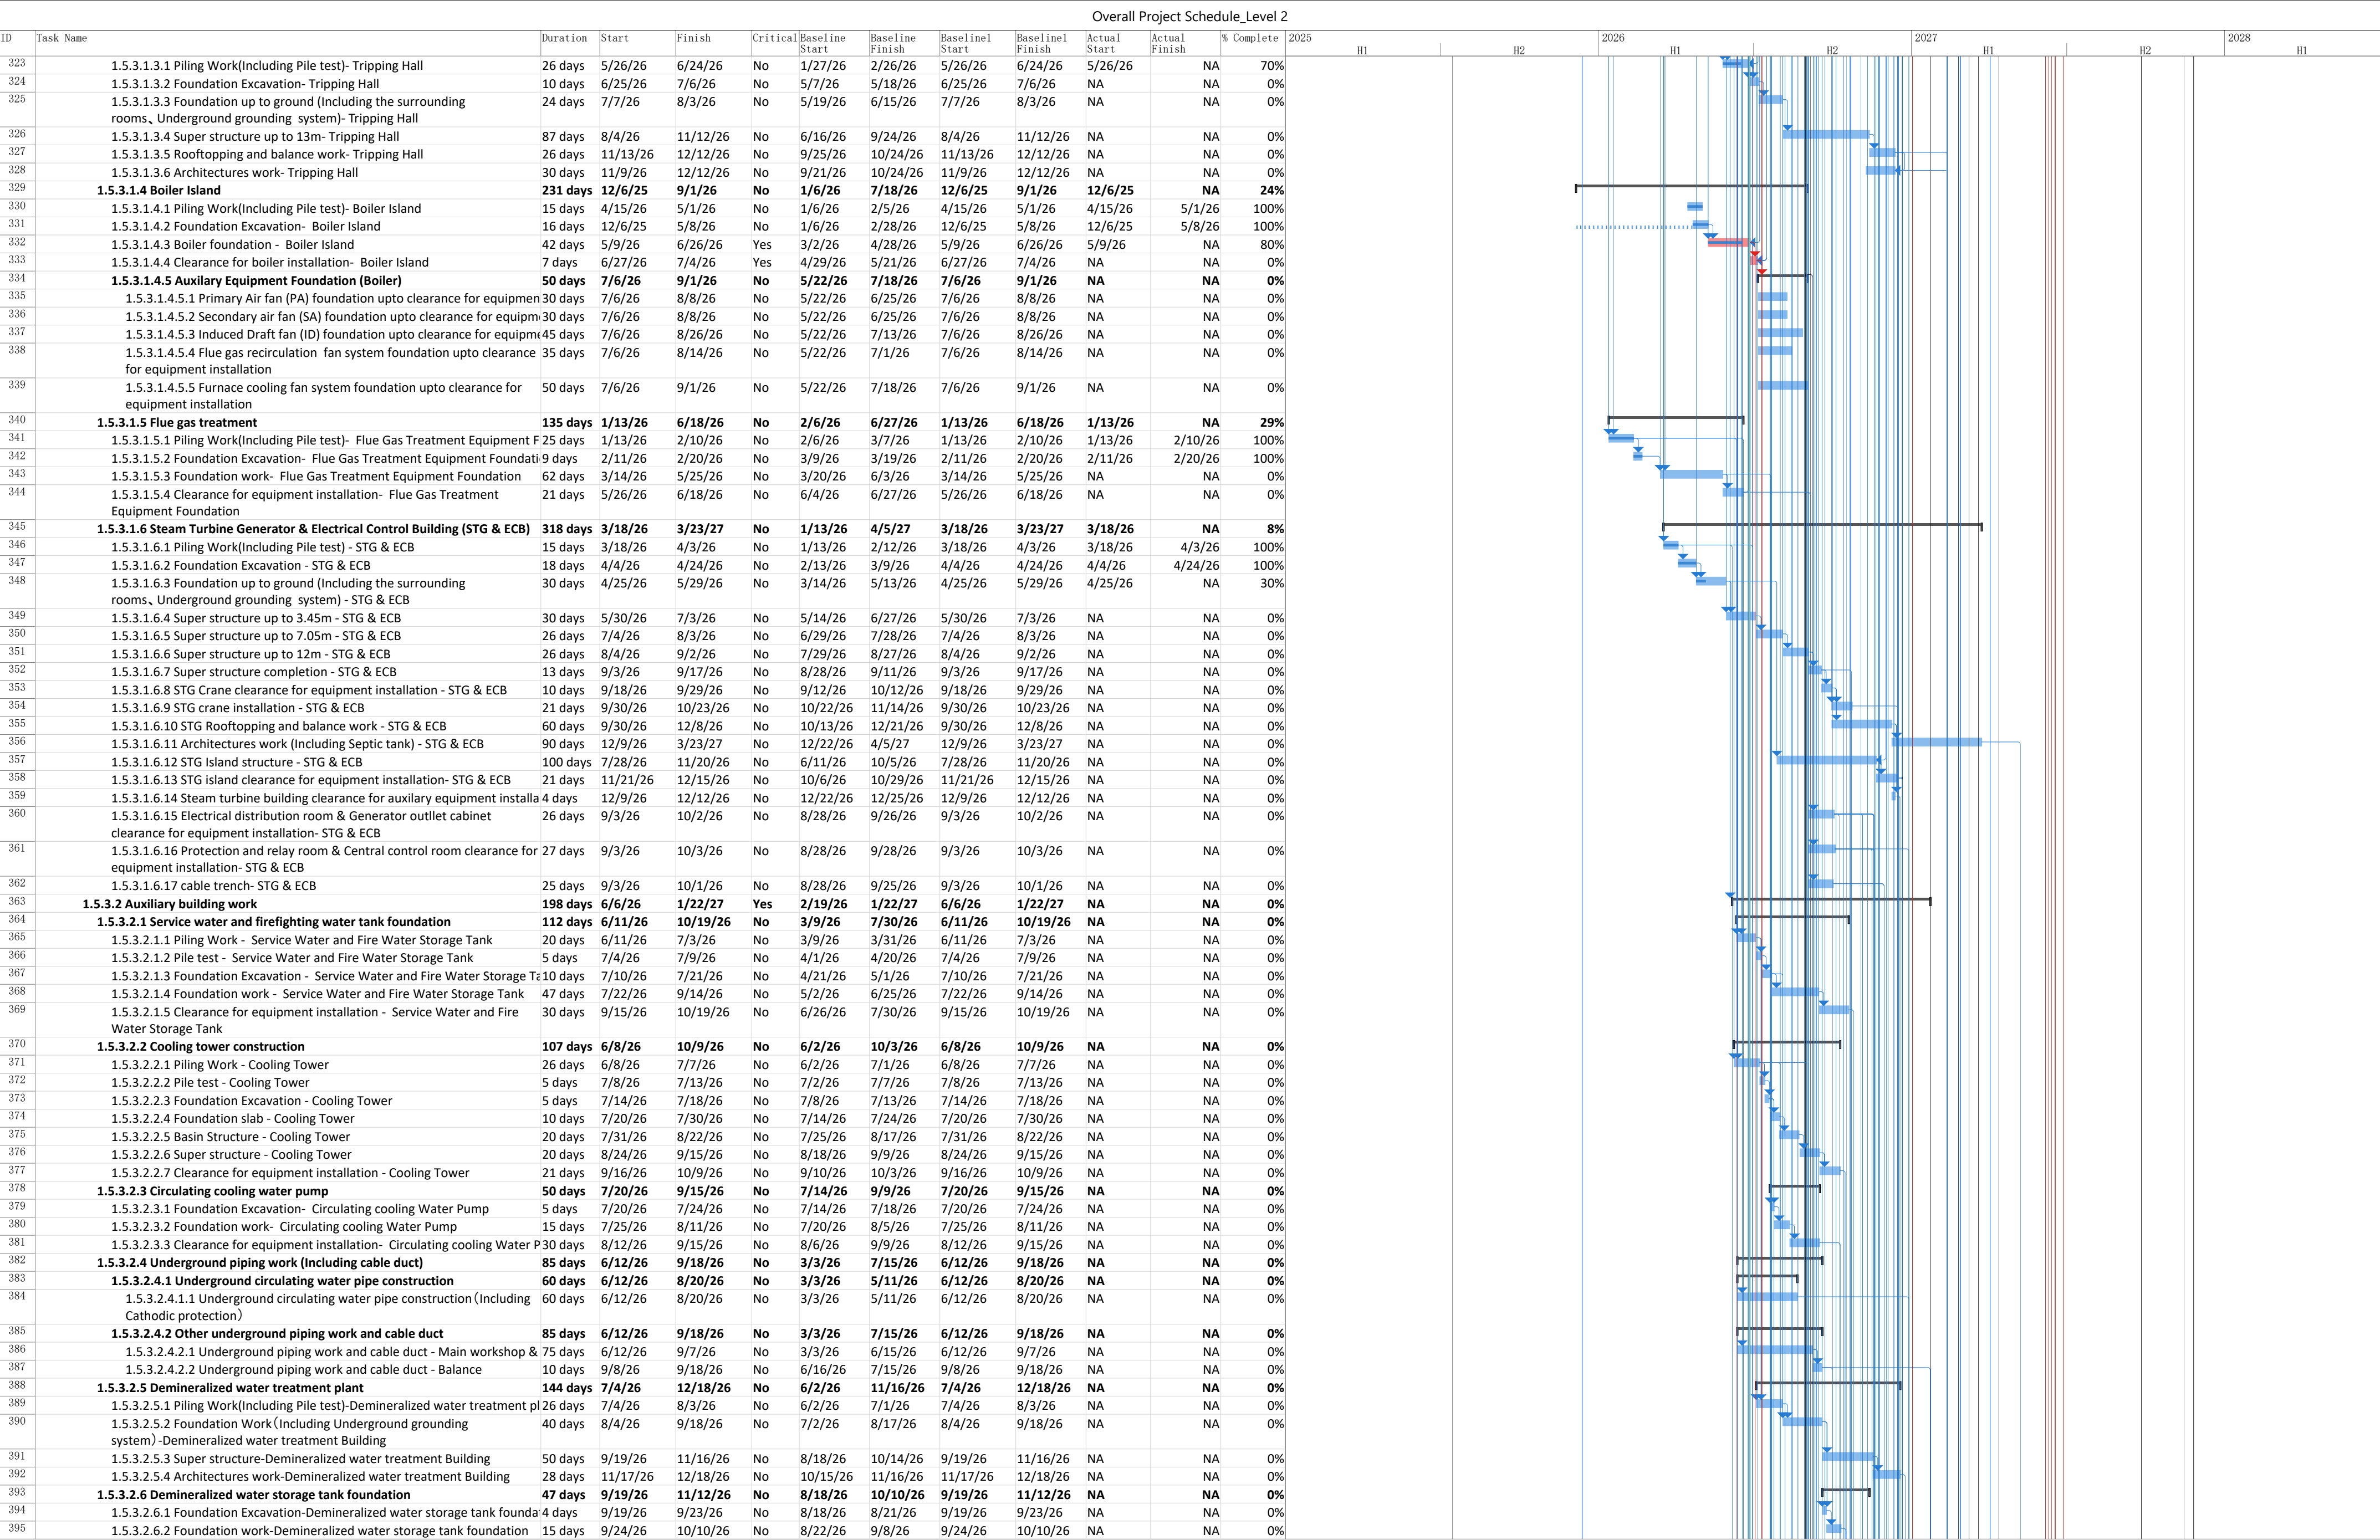

Project:Industrial waste-to-energy power plant (PWW1)
Date:May 16th 2026
Revision:D

Task

Split

Milestone

Summary

Project Summary

Not Active

Non-Active Milestone

Non-Active Summary

Manual Task

Duration Only

Manual Summary Roll-up

Manual Summary

Start Time Only

Finish Time Only

External Task

External Milestone

Deadline

Critical

Critical Split

Scheduled

Manually Scheduled

Overall Project Schedule_Level 2																							
ID	Task Name	Duration	Start	Finish	Critical	Baseline Start	Baseline Finish	Baselinel Start	Baselinel Finish	Actual Start	Actual Finish	% Complete	2025	H1	H2	2026	H1	H2	2027	H1	H2	2028	H1
396	1.5.3.2.6.3 Clearance for equipment installation-Demineralized water storage tank foundation	28 days	10/12/26	11/12/26	No	9/9/26	10/10/26	10/12/26	11/12/26	NA		NA	0%										
397	1.5.3.2.7 Chemical Storage Building	89 days	7/20/26	10/30/26	No	7/14/26	10/24/26	7/20/26	10/30/26	NA		NA	0%										
398	1.5.3.2.7.1 Foundation Work (Including Underground grounding system) -Chemical Storage Building	49 days	7/20/26	9/14/26	No	7/14/26	9/8/26	7/20/26	9/14/26	NA		NA	0%										
399	1.5.3.2.7.2 Super structure-Chemical Storage Building	20 days	9/15/26	10/7/26	No	9/9/26	10/1/26	9/15/26	10/7/26	NA		NA	0%										
400	1.5.3.2.7.3 Architectures work-Chemical Storage Building	20 days	10/8/26	10/30/26	No	10/2/26	10/24/26	10/8/26	10/30/26	NA		NA	0%										
401	1.5.3.2.8 Cooling water chemical feed building	113 days	8/1/26	12/10/26	No	9/1/26	1/9/27	8/1/26	12/10/26	NA		NA	0%										
402	1.5.3.2.8.1 Piling Work(Including Pile test)-Cooling water chemical feed build	26 days	8/1/26	8/31/26	No	9/1/26	9/30/26	8/1/26	8/31/26	NA		NA	0%										
403	1.5.3.2.8.2 Foundation Work (Including Underground grounding system) -Cooling water chemical feed building	30 days	9/1/26	10/5/26	No	10/1/26	11/4/26	9/1/26	10/5/26	NA		NA	0%										
404	1.5.3.2.8.3 Super structure-Cooling water chemical feed building	20 days	10/6/26	10/28/26	No	11/5/26	11/27/26	10/6/26	10/28/26	NA		NA	0%										
405	1.5.3.2.8.4 Architectures work-Cooling water chemical feed building	37 days	10/29/26	12/10/26	No	11/28/26	1/9/27	10/29/26	12/10/26	NA		NA	0%										
406	1.5.3.2.9 Storm Water Retention Pond (Including Sump pit)	124 days	9/1/26	1/22/27	No	9/1/26	1/22/27	9/1/26	1/22/27	NA		NA	0%										
407	1.5.3.2.10 Holding Pond and Emergency Pond	156 days	6/12/26	12/10/26	No	6/2/26	11/24/26	6/12/26	12/10/26	NA		NA	0%										
408	1.5.3.2.10.1 Foundation Excavation- Holding Pond and Emergency Pond	10 days	6/12/26	6/23/26	No	6/2/26	6/12/26	6/12/26	6/23/26	NA		NA	0%										
409	1.5.3.2.10.2 Foundation slab- Holding Pond and Emergency Pond	45 days	6/24/26	8/14/26	No	6/13/26	8/4/26	6/24/26	8/14/26	NA		NA	0%										
410	1.5.3.2.10.3 Pond wall- Holding Pond and Emergency Pond	45 days	8/15/26	10/6/26	No	8/5/26	9/25/26	8/15/26	10/6/26	NA		NA	0%										
411	1.5.3.2.10.4 Top slab- Holding Pond and Emergency Pond	51 days	10/7/26	12/4/26	No	9/26/26	11/24/26	10/7/26	12/4/26	NA		NA	0%										
412	1.5.3.2.10.5 Oil/Water Separator- Holding Pond and Emergency Pond	150 days	6/19/26	12/10/26	No	6/3/26	11/24/26	6/19/26	12/10/26	NA		NA	0%										
413	1.5.3.2.11 Wastewater Monitoring Room (WMR)	96 days	8/15/26	12/4/26	No	9/1/26	12/21/26	8/15/26	12/4/26	NA		NA	0%										
414	1.5.3.2.11.1 Piling Work(Including Pile test)-WMR	26 days	8/15/26	9/14/26	No	9/1/26	9/30/26	8/15/26	9/14/26	NA		NA	0%										
415	1.5.3.2.11.2 Foundation Work (Including Underground grounding system) -	10 days	9/15/26	9/25/26	No	10/1/26	10/12/26	9/15/26	9/25/26	NA		NA	0%										
416	1.5.3.2.11.3 Super structure-WMR	35 days	9/26/26	11/5/26	No	10/13/26	11/21/26	9/26/26	11/5/26	NA		NA	0%										
417	1.5.3.2.11.4 Architectures work-WMR	25 days	11/6/26	12/4/26	No	11/23/26	12/21/26	11/6/26	12/4/26	NA		NA	0%										
418	1.5.3.2.11.5 Final Inspection pit-WMR	28 days	11/3/26	12/4/26	No	11/19/26	12/21/26	11/3/26	12/4/26	NA		NA	0%										
419	1.5.3.2.12 Fire water pump shelter	100 days	6/6/26	9/30/26	Yes	2/19/26	5/22/26	6/6/26	9/30/26	NA		NA	0%										
420	1.5.3.2.12.1 Piling Work- Fire Water Pump Shelter	10 days	6/6/26	6/17/26	Yes	2/19/26	3/2/26	6/6/26	6/17/26	NA		NA	0%										
421	1.5.3.2.12.2 Pile test- Fire Water Pump Shelter	10 days	6/18/26	6/29/26	Yes	3/3/26	3/13/26	6/18/26	6/29/26	NA		NA	0%										
422	1.5.3.2.12.3 Foundation Work (Including Underground grounding system) - Fire Water Pump Shelter	50 days	6/30/26	8/26/26	Yes	3/14/26	4/17/26	6/30/26	8/26/26	NA		NA	0%										
423	1.5.3.2.12.4 Super structure- Fire Water Pump Shelter	30 days	8/27/26	9/30/26	Yes	4/18/26	5/22/26	8/27/26	9/30/26	NA		NA	0%										
424	1.5.3.2.13 Chimney foundation (Stack)	123 days	6/19/26	11/9/26	No	3/9/26	6/19/26	6/19/26	11/9/26	NA		NA	0%										
425	1.5.3.2.13.1 Piling Work- Chimney foundation (Stack)	26 days	6/19/26	7/18/26	No	3/9/26	4/7/26	6/19/26	7/18/26	NA		NA	0%										
426	1.5.3.2.13.2 Pile test- Chimney foundation (Stack)	15 days	7/4/26	7/21/26	No	4/8/26	4/24/26	7/4/26	7/21/26	NA		NA	0%										
427	1.5.3.2.13.3 Foundation Excavation- Chimney foundation (Stack)	20 days	7/22/26	8/13/26	No	4/25/26	5/18/26	7/22/26	8/13/26	NA		NA	0%										
428	1.5.3.2.13.4 Foundation basement casting- Chimney foundation (Stack)	30 days	8/14/26	9/17/26	No	5/19/26	6/22/26	8/14/26	9/17/26	NA		NA	0%										
429	1.5.3.2.13.5 Foundation casting- Chimney foundation (Stack)	30 days	9/18/26	10/22/26	No	6/23/26	8/31/26	9/18/26	10/22/26	NA		NA	0%										
430	1.5.3.2.13.6 Clearance for installation- Chimney foundation (Stack)	15 days	10/23/26	11/9/26	No	9/1/26	11/9/26	10/23/26	11/9/26	NA		NA	0%										
431	1.5.3.2.14 Diesel oil tank and diesel oil pump foundation and clearance for equipment installation	53 days	9/3/26	11/3/26	No	9/29/26	11/28/26	9/3/26	11/3/26	NA		NA	0%										
432	1.5.3.2.15 CEMS control room	70 days	8/14/26	11/3/26	No	5/19/26	8/7/26	8/14/26	11/3/26	NA		NA	0%										
433	1.5.3.2.15.1 Foundation Work (Including Underground grounding system) -CEMS control room	30 days	8/14/26	9/17/26	No	5/19/26	6/22/26	8/14/26	9/17/26	NA		NA	0%										
434	1.5.3.2.15.2 Super structure-CEMS control room	20 days	9/18/26	10/10/26	No	6/23/26	7/15/26	9/18/26	10/10/26	NA		NA	0%										
435	1.5.3.2.15.3 Architectures work-CEMS control room	20 days	10/12/26	11/3/26	No	7/16/26	8/7/26	10/12/26	11/3/26	NA		NA	0%										
436	1.5.3.2.16 Transformer Foundation	60 days	6/24/26	9/1/26	No	6/2/26	8/10/26	6/24/26	9/1/26	NA		NA	0%										
437	1.5.3.2.16.1 Piling Work- Unit Auxiliary and Step-up Transformer Foundation	10 days	6/24/26	7/4/26	No	6/2/26	6/12/26	6/24/26	7/4/26	NA		NA	0%										
438	1.5.3.2.16.2 Pile test- Transformer Foundation	5 days	7/6/26	7/10/26	No	6/13/26	6/18/26	7/6/26	7/10/26	NA		NA	0%										
439	1.5.3.2.16.3 Foundation Excavation- Transformer Foundation	10 days	7/11/26	7/22/26	No	6/19/26	6/30/26	7/11/26	7/22/26	NA		NA	0%										
440	1.5.3.2.16.4 Foundation work- Transformer Foundation	25 days	7/23/26	8/20/26	No	7/1/26	7/29/26	7/23/26	8/20/26	NA		NA	0%										
441	1.5.3.2.16.5 Clearance for equipment installation- Transformer Foundation	10 days	8/21/26	9/1/26	No	7/30/26	8/10/26	8/21/26	9/1/26	NA		NA	0%										
442	1.5.3.2.17 Bottom Ash Conveyer Foundation	20 days	6/27/26	7/20/26	No	4/29/26	6/2/26	6/27/26	7/20/26	NA		NA	0%										
443	1.5.3.2.18 Fly Ash Silo Foundation	29 days	7/21/26	8/22/26	No	6/4/26	7/8/26	7/21/26	8/22/26	NA		NA	0%										
444	1.5.3.2.19 Pipe Rack Foundation and Installation (Incl.Pipe bridge and Pipe Su	52 days	10/23/26	12/22/26	No	10/17/26	12/16/26	10/23/26	12/22/26	NA		NA	0%										
445	1.5.3.3 Other building work	266 days	7/20/26	5/25/27	No	3/14/26	5/1/27	7/20/26	5/25/27	NA		NA	0%										
446	1.5.3.3.1 Administration building	154 days	9/1/26	2/26/27	No	9/1/26	2/26/27	9/1/26	2/26/27	NA		NA	0%										
447	1.5.3.3.1.1 Piling Work- Administration Building	10 days	9/1/26	9/11/26	No	9/1/26	9/11/26	9/1/26	9/11/26	NA		NA	0%										
448	1.5.3.3.1.2 Pile test- Administration Building	10 days	9/12/26	9/23/26	No	9/12/26	9/23/26	9/12/26	9/23/26	NA		NA	0%										
449	1.5.3.3.1.3 Foundation Work (Including Underground grounding system) - Administration Building	30 days	9/24/26	10/28/26	No	9/24/26	10/28/26	9/24/26	10/28/26	NA		NA	0%										
450	1.5.3.3.1.4 Super structure- Administration Building	52 days	10/29/26	12/28/26	No	10/29/26	12/28/26	10/29/26	12/28/26	NA		NA	0%										
451	1.5.3.3.1.5 Architectures work (Include decoration, Septic tank) - Administra	52 days	12/29/26	2/26/27	No	12/29/26	2/26/27	12/29/26	2/26/27	NA		NA	0%										
452	1.5.3.3.2 Warehouse and Maintenance Workshop(WH & WS)	218 days	5/12/26	5/24/27	No	9/12/26	5/1/27	9/12/26	5/24/27	NA		NA	0%										
453	1.5.3.3.2.1 Piling Work - WH & WS	10 days	9/12/26	9/23/26	No	9/12/26	9/23/26	9/12/26	9/23/26	NA		NA	0%										
454	1.5.3.3.2.2 Pile test - WH & WS	9 days	9/24/26	10/3/26	No	9/24/26	10/3/26	9/24/26	10/3/26	NA		NA	0%										
455	1.5.3.3.2.3 Foundation Work (Including Underground grounding system) - W	49 days	10/5/26	11/30/26	No	10/5/26	11/7/26	10/5/26	11/30/26	NA		NA	0%										
456	1.5.3.3.2.4 Super structure - WH & WS	45 days	12/1/26	1/21/27	No	11/9/26	12/30/26	12/1/26	1/21/27	NA		NA	0%										
457	1.5.3.3.2.5 Overhead Crane clearance for equipment installation - WH & WS	45 days	1/22/27	3/15/27	No	12/31/26	2/20/27	1/22/27	3/15/27	NA		NA	0%										
458	1.5.3.3.2.6 Architectures work (Including Septic tank) - WH & WS	60 days	3/16/27	5/24/27	No	2/22/27	5/1/27	3/16/27	5/24/27	NA		NA	0%										
459	1.5.3.3.3 Truck Weighing Scale & Control Building	147 days	9/1/26	2/18/27	No	9/1/26	2/18/27	9/1/26	2/18/27	NA		NA	0%										
460	1.5.3.3.3.1 Piling Work(Including Pile test)-Truck Weighing Scale & Control Bu	26 days	9/1/26	9/30/26	No	9/1/26	9/30/26	9/1/26	9/30/26	NA		NA	0%										
461	1.5.3.3.3.2 Foundation Work (Including We																						

Overall Project Schedule_Level 2														
ID	Task Name	Duration	Start	Finish	Critical	Baseline Start	Baseline Finish	Baseline1 Start	Baseline1 Finish	Actual Start	Actual Finish	% Complete	2025	
471	1.5.3.3.5.1 Piling Work	30 days	7/20/26	8/22/26	No	4/8/26	5/12/26	7/20/26	8/22/26	NA		NA	0%	H1
472	1.5.3.3.5.2 Pile test	10 days	8/24/26	9/3/26	No	5/13/26	5/23/26	8/24/26	9/3/26	NA		NA	0%	
473	1.5.3.3.5.3 Foundation Excavation	20 days	9/4/26	9/26/26	No	5/25/26	6/16/26	9/4/26	9/26/26	NA		NA	0%	H2
474	1.5.3.3.5.4 Foundation	50 days	9/28/26	11/24/26	No	6/17/26	8/13/26	9/28/26	11/24/26	NA		NA	0%	
475	1.5.3.3.5.5 Retaining Wall	60 days	11/25/26	2/2/27	No	8/14/26	10/22/26	11/25/26	2/2/27	NA		NA	0%	
476	1.5.3.3.6 Plant internal road	45 days	2/27/27	4/20/27	No	3/14/26	5/5/26	2/27/27	4/20/27	NA		NA	0%	
477	1.5.3.3.7 Plant Virescence	60 days	2/27/27	5/7/27	No	3/14/26	5/22/26	2/27/27	5/7/27	NA		NA	0%	
478	1.5.3.3.8 Site Grading (Backfilling)	30 days	2/27/27	4/2/27	No	3/14/26	9/4/26	2/27/27	4/2/27	NA		NA	0%	
479	1.5.3.3.9 Road Lighting	30 days	4/21/27	5/25/27	No	5/6/26	6/9/26	4/21/27	5/25/27	NA		NA	0%	
480	1.5.3.3.10 Parking area foundation	20 days	4/3/27	4/26/27	No	9/5/26	10/27/26	4/3/27	4/26/27	NA		NA	0%	
481	1.5.4 Mechanical Work	271 days	7/6/26	5/17/27	Yes	5/22/26	5/17/27	7/6/26	5/17/27	NA		NA	0%	
482	1.5.4.1 Main equipment installation	271 days	7/6/26	5/17/27	Yes	5/22/26	5/17/27	7/6/26	5/17/27	NA		NA	0%	
483	1.5.4.1.1 Incinerator installation	90 days	7/6/26	10/17/26	Yes	5/22/26	11/11/26	7/6/26	10/17/26	NA		NA	0%	
484	1.5.4.1.1.1 Grate steel structure (Supplied by boiler supplier)-Incinerator	14 days	7/6/26	7/21/26	Yes	5/22/26	6/23/26	7/6/26	7/21/26	NA		NA	0%	
485	1.5.4.1.1.2 Bottom ash remover-Incinerator	5 days	7/22/26	7/27/26	Yes	6/24/26	6/29/26	7/22/26	7/27/26	NA		NA	0%	
486	1.5.4.1.1.3 Bottom ash conveyor-Incinerator	5 days	7/28/26	8/1/26	Yes	6/30/26	7/4/26	7/28/26	8/1/26	NA		NA	0%	
487	1.5.4.1.1.4 Incinerator ash hopper-Incinerator	5 days	8/3/26	8/7/26	Yes	7/6/26	7/10/26	8/3/26	8/7/26	NA		NA	0%	
488	1.5.4.1.1.5 Grate installation-Incinerator	18 days	8/8/26	8/28/26	Yes	7/11/26	7/31/26	8/8/26	8/28/26	NA		NA	0%	
489	1.5.4.1.1.6 Feeder installation-Incinerator	5 days	8/29/26	9/3/26	No	8/7/26	8/12/26	8/29/26	9/3/26	NA		NA	0%	
490	1.5.4.1.1.7 Chute installation-Incinerator	3 days	9/4/26	9/7/26	No	9/29/26	10/1/26	9/4/26	9/7/26	NA		NA	0%	
491	1.5.4.1.1.8 Fuel hopper installation-Incinerator	5 days	9/8/26	9/12/26	No	10/2/26	10/7/26	9/8/26	9/12/26	NA		NA	0%	
492	1.5.4.1.1.9 Hydrostatic oil station-Incinerator	30 days	9/14/26	10/17/26	No	10/8/26	11/11/26	9/14/26	10/17/26	NA		NA	0%	
493	1.5.4.1.2 Boiler installation	224 days	8/29/26	5/17/27	Yes	8/1/26	5/17/27	8/29/26	5/17/27	NA		NA	0%	
494	1.5.4.1.2.1 Boiler steel structure-Boiler	20 days	8/29/26	9/21/26	Yes	8/1/26	8/24/26	8/29/26	9/21/26	NA		NA	0%	
495	1.5.4.1.2.2 Board girder and Drum lifting-Boiler	3 days	9/22/26	9/24/26	Yes	8/25/26	8/27/26	9/22/26	9/24/26	NA		NA	0%	
496	1.5.4.1.2.3 Water wall installation-Boiler	20 days	9/25/26	10/17/26	Yes	8/28/26	9/19/26	9/25/26	10/17/26	NA		NA	0%	
497	1.5.4.1.2.4 Superheater-Boiler	15 days	10/19/26	11/4/26	Yes	9/21/26	10/17/26	10/19/26	11/4/26	NA		NA	0%	
498	1.5.4.1.2.5 Economizer-Boiler	24 days	11/5/26	12/2/26	Yes	10/19/26	11/14/26	11/5/26	12/2/26	NA		NA	0%	
499	1.5.4.1.2.6 Heating surface sealing-Boiler	40 days	12/3/26	1/18/27	No	11/16/26	1/6/27	12/3/26	1/18/27	NA		NA	0%	
500	1.5.4.1.2.7 Main body pipeline-Boiler	30 days	12/3/26	1/6/27	Yes	11/16/26	1/6/27	12/3/26	1/6/27	NA		NA	0%	
501	1.5.4.1.2.8 Boiler ash hopper-Boiler	10 days	12/3/26	12/14/26	No	11/16/26	11/26/26	12/3/26	12/14/26	NA		NA	0%	
502	1.5.4.1.2.9 Boiler ash conveyor-Boiler	10 days	12/15/26	12/25/26	No	11/27/26	12/8/26	12/15/26	12/25/26	NA		NA	0%	
503	1.5.4.1.2.10 Tail flue gas duct-Boiler	10 days	12/3/26	12/14/26	No	11/16/26	11/26/26	12/3/26	12/14/26	NA		NA	0%	
504	1.5.4.1.2.11 Temporary pipeline (For Hydrostatic test)-Boiler	9 days	1/7/27	1/16/27	Yes	1/7/27	1/16/27	1/7/27	1/16/27	NA		NA	0%	
505	1.5.4.1.2.12 Hydrostatic test-Boiler	3 days	1/18/27	1/20/27	Yes	1/18/27	1/20/27	1/18/27	1/20/27	NA		NA	0%	
506	1.5.4.1.2.13 Fire brick-Boiler	50 days	1/21/27	3/19/27	Yes	1/21/27	3/19/27	1/21/27	3/19/27	NA		NA	0%	
507	1.5.4.1.2.14 Insulation-Boiler	50 days	3/20/27	5/17/27	Yes	3/20/27	5/17/27	3/20/27	5/17/27	NA		NA	0%	
508	1.5.4.1.3 Steam turbine and generator (STG)	123 days	12/16/26	5/7/27	No	12/17/26	5/8/27	12/16/26	5/7/27	NA		NA	0%	
509	1.5.4.1.3.1 Condenser installation - STG	5 days	12/16/26	12/21/26	No	12/17/26	12/22/26	12/16/26	12/21/26	NA		NA	0%	
510	1.5.4.1.3.2 STG installation - STG	30 days	12/22/26	1/25/27	No	12/23/26	1/26/27	12/22/26	1/25/27	NA		NA	0%	
511	1.5.4.1.3.3 Gear casing installation - STG	7 days	12/22/26	12/29/26	No	12/23/26	12/30/26	12/22/26	12/29/26	NA		NA	0%	
512	1.5.4.1.3.4 Generator installation - STG	10 days	12/22/26	1/1/27	No	12/23/26	1/2/27	12/22/26	1/1/27	NA		NA	0%	
513	1.5.4.1.3.5 Shafting alignment - STG	10 days	1/26/27	2/5/27	No	1/27/27	2/6/27	1/26/27	2/5/27	NA		NA	0%	
514	1.5.4.1.3.6 Secondary grouting - STG	3 days	2/6/27	2/9/27	No	2/8/27	2/10/27	2/6/27	2/9/27	NA		NA	0%	
515	1.5.4.1.3.7 Insulation - STG	15 days	2/10/27	2/26/27	No	2/11/27	2/27/27	2/10/27	2/26/27	NA		NA	0%	
516	1.5.4.1.3.8 EH control oil system - STG	30 days	1/23/27	2/26/27	No	1/25/27	2/27/27	1/23/27	2/26/27	NA		NA	0%	
517	1.5.4.1.3.9 Lubricated oil system installation - STG	30 days	1/23/27	2/26/27	No	1/25/27	2/27/27	1/23/27	2/26/27	NA		NA	0%	
518	1.5.4.1.3.10 Lube oil flushing - STG	60 days	2/27/27	5/7/27	No	3/1/27	5/8/27	2/27/27	5/					

Overall Project Schedule_Level 2																							
ID	Task Name	Duration	Start	Finish	Critical	Baseline Start	Baseline Finish	Baseline Start	Baseline Finish	Actual Start	Actual Finish	% Complete	2025	H1	H2	2026	H1	H2	2027	H1	H2	2028	H1
551	1.5.4.2.9.1.2 Piping Installation-Primary fan system	50 days	9/14/26	11/10/26	No	9/28/26	11/24/26	9/14/26	11/10/26	NA	NA	0%											
552	1.5.4.2.9.2 Secondary fan system (Including Motor System)	60 days	9/2/26	11/10/26	No	9/16/26	11/24/26	9/2/26	11/10/26	NA	NA	0%											
553	1.5.4.2.9.2.1 fan Installation-Secondary fan system	10 days	9/2/26	9/12/26	No	9/16/26	9/26/26	9/2/26	9/12/26	NA	NA	0%											
554	1.5.4.2.9.2.2 Piping Installation-Secondary fan system	50 days	9/14/26	11/10/26	No	9/28/26	11/24/26	9/14/26	11/10/26	NA	NA	0%											
555	1.5.4.2.9.3 Induced Draft fan system (Including Motor System)	60 days	9/2/26	11/10/26	No	9/16/26	11/24/26	9/2/26	11/10/26	NA	NA	0%											
556	1.5.4.2.9.3.1 fan Installation-Induced Draft fan system	10 days	9/2/26	9/12/26	No	9/16/26	9/26/26	9/2/26	9/12/26	NA	NA	0%											
557	1.5.4.2.9.3.2 Piping Installation-Induced Draft fan system	50 days	9/14/26	11/10/26	No	9/28/26	11/24/26	9/14/26	11/10/26	NA	NA	0%											
558	1.5.4.2.9.4 Flue gas recirculation fan system installation	60 days	9/2/26	11/10/26	No	9/16/26	11/24/26	9/2/26	11/10/26	NA	NA	0%											
559	1.5.4.2.9.4.1 fan Installation-Flue gas recirculation fan system	10 days	9/2/26	9/12/26	No	9/16/26	9/26/26	9/2/26	9/12/26	NA	NA	0%											
560	1.5.4.2.9.4.2 Piping Installation-Flue gas recirculation fan system	50 days	9/14/26	11/10/26	No	9/28/26	11/24/26	9/14/26	11/10/26	NA	NA	0%											
561	1.5.4.2.9.5 Furnace cooling fan system (Including Motor System)	60 days	9/2/26	11/10/26	No	9/16/26	11/24/26	9/2/26	11/10/26	NA	NA	0%											
562	1.5.4.2.9.5.1 fan Installation-Furnace cooling fan system	10 days	9/2/26	9/12/26	No	9/16/26	9/26/26	9/2/26	9/12/26	NA	NA	0%											
563	1.5.4.2.9.5.2 Piping Installation-Furnace cooling fan system	50 days	9/14/26	11/10/26	No	9/28/26	11/24/26	9/14/26	11/10/26	NA	NA	0%											
564	1.5.4.2.9.6 Insulation	60 days	9/2/26	11/10/26	No	9/16/26	11/24/26	9/2/26	11/10/26	NA	NA	0%											
565	1.5.4.2.10 STG Auxiliary systems	60 days	12/14/26	2/20/27	No	12/26/26	3/5/27	12/14/26	2/20/27	NA	NA	0%											
566	1.5.4.2.10.1 Vacuum pumping system	30 days	12/14/26	1/16/27	No	12/26/26	1/29/27	12/14/26	1/16/27	NA	NA	0%											
567	1.5.4.2.10.1.1 Mechanical Installation - Vacuum Pumping System	5 days	12/14/26	12/18/26	No	12/26/26	12/31/26	12/14/26	12/18/26	NA	NA	0%											
568	1.5.4.2.10.1.2 Piping Installation (Incl. Painting & Insulation) - Vacuum Pumping System	25 days	12/19/26	1/16/27	No	1/1/27	1/29/27	12/19/26	1/16/27	NA	NA	0%											
569	1.5.4.2.10.2 Condensate water system	45 days	12/14/26	2/3/27	No	12/26/26	2/16/27	12/14/26	2/3/27	NA	NA	0%											
570	1.5.4.2.10.2.1 Mechanical Installation - Condensate Water System	5 days	12/14/26	12/18/26	No	12/26/26	12/31/26	12/14/26	12/18/26	NA	NA	0%											
571	1.5.4.2.10.2.2 Piping Installation (Incl. Painting & Insulation) - Condensate Water System	40 days	12/19/26	2/3/27	No	1/1/27	2/16/27	12/19/26	2/3/27	NA	NA	0%											
572	1.5.4.2.10.3 Feed water system (Including Deaerator and feed water tank)	45 days	12/14/26	2/3/27	No	12/26/26	2/16/27	12/14/26	2/3/27	NA	NA	0%											
573	1.5.4.2.10.3.1 Mechanical Installation - Feed Water System	5 days	12/14/26	12/18/26	No	12/26/26	12/31/26	12/14/26	12/18/26	NA	NA	0%											
574	1.5.4.2.10.3.2 Piping Installation (Incl. Painting & Insulation) - Feed Water System	40 days	12/19/26	2/3/27	No	1/1/27	2/16/27	12/19/26	2/3/27	NA	NA	0%											
575	1.5.4.2.10.4 Main steam system (Piping Installation)	30 days	12/23/26	1/26/27	No	12/26/26	1/29/27	12/23/26	1/26/27	NA	NA	0%											
576	1.5.4.2.10.5 Turbine bypass system (Piping Installation)	30 days	12/14/26	1/16/27	No	12/26/26	1/29/27	12/14/26	1/16/27	NA	NA	0%											
577	1.5.4.2.10.6 Turbine extraction steam system	60 days	12/14/26	2/20/27	No	12/26/26	3/5/27	12/14/26	2/20/27	NA	NA	0%											
578	1.5.4.2.10.6.1 Mechanical Installation - Turbine Extraction Steam System	10 days	12/14/26	12/24/26	No	12/26/26	1/6/27	12/14/26	12/24/26	NA	NA	0%											
579	1.5.4.2.10.6.2 Piping Installation (Incl. Painting & Insulation) - Turbine Extraction Steam System	50 days	12/25/26	2/20/27	No	1/7/27	3/5/27	12/25/26	2/20/27	NA	NA	0%											
580	1.5.4.2.10.7 Insulation	60 days	12/14/26	2/20/27	No	12/26/26	3/5/27	12/14/26	2/20/27	NA	NA	0%											
581	1.5.5 Electrical Work	150 days	8/17/26	2/6/27	No	8/21/26	12/22/26	8/17/26	2/6/27	NA	NA	0%											
582	1.5.5.1 22kV system	33 days	11/18/26	12/25/26	No	9/28/26	10/19/26	11/18/26	12/25/26	NA	NA	0%											
583	1.5.5.1.1 11kV/22kV Transformer installation	10 days	12/15/26	12/25/26	No	10/8/26	10/19/26	12/15/26	12/25/26	NA	NA	0%											
584	1.5.5.1.2 22kV Switchgear and Distribution system	10 days	11/18/26	11/28/26	No	9/28/26	10/8/26	11/18/26	11/28/26	NA	NA	0%											
585	1.5.5.2 Relay and protection system	22 days	11/16/26	12/10/26	No	9/28/26	11/2/26	11/18/26	12/17/26	NA	NA	0%											
586	1.5.5.2.1 Relay and protection panel	20 days	11/18/26	12/10/26	No	10/6/26	10/28/26	11/18/26	12/10/26	NA	NA	0%											
587	1.5.5.2.2 Revenue meter and synchronization	20 days	11/18/26	12/10/26	No	10/10/26	11/2/26	11/18/26	12/10/26	NA	NA	0%											
588	1.5.5.2.3 Battery system	10 days	11/19/26	11/30/26	No	9/28/26	10/8/26	11/19/26	11/30/26	NA	NA	0%											
589	1.5.5.2.4 DC, UPS system	10 days	11/19/26	11/30/26	No	9/29/26	10/9/26	11/19/26	11/30/26	NA	NA	0%											
590	1.5.5.2.5 Communication system (telephone, paging, intercom, LAN)	20 days	11/16/26	12/8/26	No	9/29/26	10/21/26	11/25/26	12/17/26	NA	NA	0%											
591	1.5.5.3 11kV system	20 days	11/18/26	12/10/26	No	9/28/26	10/27/26	11/18/26	12/10/26	NA	NA	0%											
592	1.5.5.3.1 Generator outlet cabinet	20 days	11/18/26	12/10/26	No	9/28/26	10/20/26	11/18/26	12/10/26	NA	NA	0%											
593	1.5.5.3.2 11kV Switchgear	20 days	11/18/26	12/10/26	No	9/28/26	10/20/26	11/18/26	12/10/26	NA	NA	0%											
594	1.5.5.3.3 11kV VFD	20 days	11/18/26	12/10/26	No	10/5/26	10/27/26	11/18/26	12/10/26	NA	NA	0%											
595	1.5.5.4 400V system	36 days	10/17/26	11/27/26	No	10/9/26	11/13/26	10/17/26	11/27/26	NA	NA	0%											
596	1.5.5.4.1 11kV/400V Transformer installation	5 days	11/16/26	11/20/26	No	10/9/26	10/14/26	11/16/26	11/20/26	NA	NA	0%											
597	1.5.5.4.2 Low voltage cabinet installation	20 days	11/5/26	11/27/26	No	10/10/26	11/2/26	11/5/26	11/27/26	NA	NA	0%											
598	1.5.5.4.3 LV frequency converter cabinet	10 days	11/5/26	11/16/26	No	10/10/26	10/21/26	11/5/26	11/16/26	NA	NA	0%											
599	1.5.5.4.4 Emergency Diesel Generator	10 days	10/17/26	10/28/26	No	11/3/26	11/13/26	10/17/26	10/28/26	NA	NA	0%											
600	1.5.5.5 Cable and raceway system installation	55 days	11/30/26	2/1/27	No	10/14/26	12/16/26	11/30/26	2/1/27	NA	NA	0%											
601	1.5.5.6 Cable laying and wiring (Electric system)	45 days	12/11/26	2/1/27	No	10/26/26	12/16/26	12/11/26	2/1/27	NA	NA	0%											
602	1.5.5.7 Cable laying and wiring (Mechanical equipment power supply system)	50 days	12/11/26	2/6/27	No	10/26/26	12/22/26	12/11/26	2/6/27	NA	NA	0%											
603	1.5.5.8 Grounding and Lightning Protection System	45 days	9/14/26	11/4/26	No	9/3/26	10/24/26	9/14/26	11/4/26	NA	NA	0%											
604	1.5.5.9 Lighting and Small Power	30 days	8/17/26	9/19/26	No	8/21/26	9/24/26	8/17/26	9/19/26	NA	NA	0%											
605	1.5.6 C&I Work	172 days	10/1/26	4/19/27	Yes	7/16/26	2/10/27	10/1/26	4/19/27	NA	NA	0%											
606	1.5.6.1 DCS system installation	45 days	12/29/26	2/18/27	No	10/31/26	12/22/26	12/29/26	2/18/27	NA	NA	0%											
607	1.5.6.2 CCTV system	111 days	12/11/26	4/19/27	No	9/5/26	1/12/27	12/11/26	4/19/27	NA	NA	0%											
608	1.5.6.3 Fire fighting and fire alarm system	150 days	10/1/26	3/24/27	Yes	7/16/26	1/6/27	10/1/26	3/24/27	NA	NA	0%											
609	1.5.6.4 CEMS system and Emission Panel at entrance gate	60 days	12/3/26	2/10/27	No	12/3/26	2/10/27	12/3/26	2/10/27	NA	NA	0%											
610	1.5.6.5 HVAC system (Control room and electric distribution room)	32 days	10/3/26	11/9/26	No	9/28/26	11/3/26	10/3/26	11/9/26	NA	NA	0%											
611	1.5.6.6 Source component installation	60 days	12/11/26	2/18/27	No	9/23/26	12/1/26	12/11/26	2/18/27	NA	NA	0%											
612	1.5.6.7 Instrument equipment installation	60 days	12/11/26	2/18/27	No	9/23/26	12/1/26	12/11/26	2/18/27	NA	NA	0%											
613	1.5.6.8 Cable and raceway system installation	40 days	11/30/26	1/14/27	No	10/14/26	11/30/26	1/14/27	1/14/27	NA	NA	0%											
614	1.5.6.9 Cable laying and wiring	50 days	12/11/26	2/6/27	No	10/26/26	12/22/26	12/11/26	2/6/27	NA	NA	0%											
615	1.6 Testing/Commissioning	318 days	11/10/26	11/14/27	Yes	11/4/26	11/14/27	11/10/26	11/14/27	NA	NA	0%											
616	1.6.1 System testing and commissioning	213 days	11/10/26	7/15/27	Yes	11/4/26	7/15/27	11/10/26	7/15/27	NA	NA	0%											
617	1.6.1.1 Wastewater treatment system	10 days	1/23/27	2/3/27	No	1/23/27	2/3/27	1/23/27	2/3/27	NA	NA	0%											
618	1.6.1.2 Testing and commissioning for electrical system	7 days	2/8/27	2/15/27	No	12/23/26	12/30/26	2/8/27	2/15/27	NA	NA	0%											
619																							

