


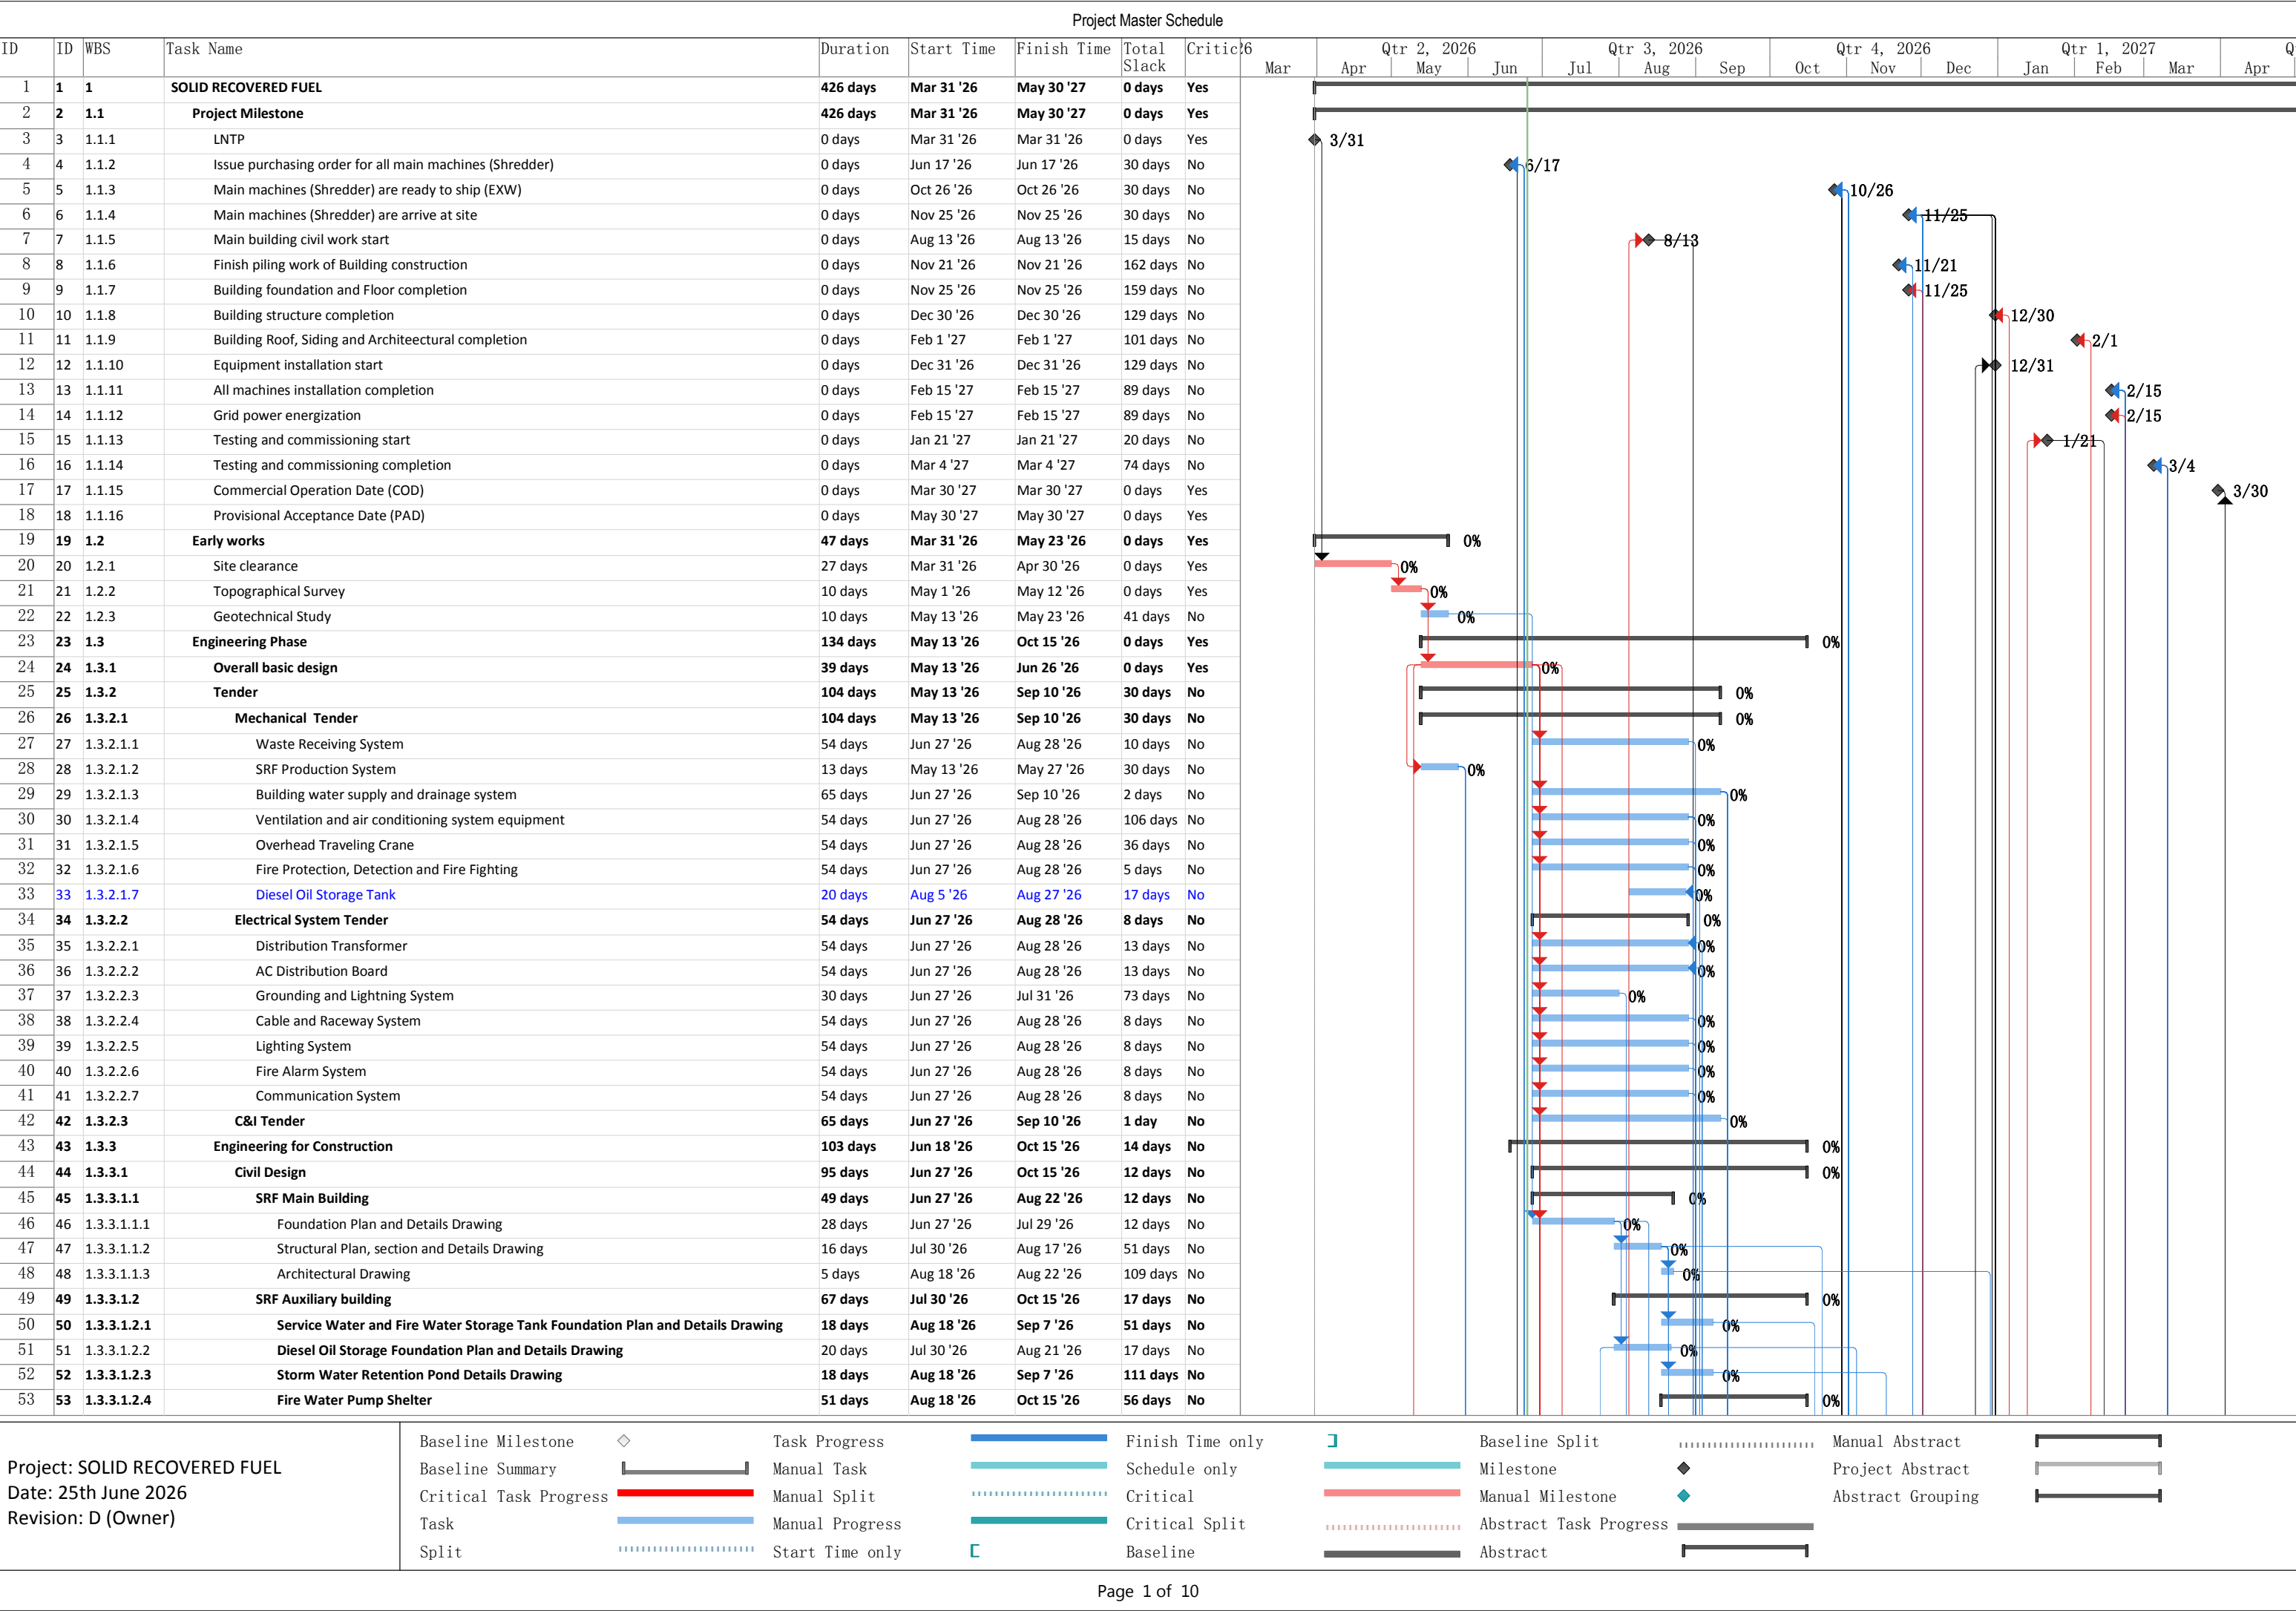

Project Master Schedule																							
ID	ID	WBS	Task Name	Duration	Start Time	Finish Time	Total Slack	Critical	6	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
54	54	1.3.3.1.2.4.1	Fire Water Pump Shelter Foundation Plan and Details Drawing	18 days	Aug 18 '26	Sep 7 '26	56 days	No								0%							
55	55	1.3.3.1.2.4.2	Structural Plan, section and Details Drawing	18 days	Sep 8 '26	Sep 28 '26	89 days	No								0%							
56	56	1.3.3.1.2.4.3	Fire Water Pump Shelter Architectural Drawing	15 days	Sep 29 '26	Oct 15 '26	89 days	No									0%						
57	57	1.3.3.1.2.5	Transformer Foundation Plan and Details Drawing	18 days	Aug 18 '26	Sep 7 '26	61 days	No								0%							
58	58	1.3.3.1.2.6	Pipe Trench, Duct Bank, Lighting pole support Structural Details Drawing	25 days	Aug 18 '26	Sep 15 '26	81 days	No								0%							
59	59	1.3.3.1.2.7	Drainage system and Sump pit Structural Details drawing	25 days	Aug 18 '26	Sep 15 '26	81 days	No								0%							
60	60	1.3.3.1.2.8	Truck Weighing Scale Control Building	36 days	Aug 18 '26	Sep 28 '26	75 days	No								0%							
61	61	1.3.3.1.2.8.1	Foundation Plan and Details drawing	12 days	Aug 18 '26	Aug 31 '26	75 days	No								0%							
62	62	1.3.3.1.2.8.2	Structural Plan, section and Details Drawing	12 days	Sep 1 '26	Sep 14 '26	105 days	No								0%							
63	63	1.3.3.1.2.8.3	Architectural Drawing	12 days	Sep 15 '26	Sep 28 '26	113 days	No								0%							
64	64	1.3.3.1.2.9	Truck Weighing Scale Foundation Plan and Details drawing	12 days	Aug 18 '26	Aug 31 '26	82 days	No								0%							
65	65	1.3.3.1.3	SRF Other building	32 days	Aug 18 '26	Sep 23 '26	56 days	No								0%							
66	66	1.3.3.1.3.1	Administration building	32 days	Aug 18 '26	Sep 23 '26	85 days	No								0%							
67	67	1.3.3.1.3.1.1	Administration building Foundation Plan and Details drawing	12 days	Aug 18 '26	Aug 31 '26	85 days	No								0%							
68	68	1.3.3.1.3.1.2	Administration building Structural Plan, section and Details drawing	10 days	Sep 1 '26	Sep 11 '26	104 days	No								0%							
69	69	1.3.3.1.3.1.3	Administration building Architectural Drawing	10 days	Sep 12 '26	Sep 23 '26	114 days	No								0%							
70	70	1.3.3.1.3.2	Warehouse & Maintenance Workshop Building	32 days	Aug 18 '26	Sep 23 '26	77 days	No								0%							
71	71	1.3.3.1.3.2.1	Warehouse & Maintenance Workshop Building Foundation Plan and Details Drawing	12 days	Aug 18 '26	Aug 31 '26	77 days	No								0%							
72	72	1.3.3.1.3.2.2	Warehouse & Maintenance Workshop Building Structural Plan, section and Details Dr	10 days	Sep 1 '26	Sep 11 '26	99 days	No								0%							
73	73	1.3.3.1.3.2.3	Warehouse & Maintenance Workshop Building Architectural Drawing	10 days	Sep 12 '26	Sep 23 '26	114 days	No								0%							
74	74	1.3.3.1.3.3	Guard House	32 days	Aug 18 '26	Sep 23 '26	117 days	No								0%							
75	75	1.3.3.1.3.3.1	Foundation Plan and Details drawing	12 days	Aug 18 '26	Aug 31 '26	117 days	No								0%							
76	76	1.3.3.1.3.3.2	Structural Plan section and Details drawing	10 days	Sep 1 '26	Sep 11 '26	117 days	No								0%							
77	77	1.3.3.1.3.3.3	Architectural Drawing	10 days	Sep 12 '26	Sep 23 '26	122 days	No								0%							
78	78	1.3.3.1.3.4	Road, Parking area, Paving area Plan and Details drawing	25 days	Aug 18 '26	Sep 15 '26	56 days	No								0%							
79	79	1.3.3.1.3.5	Boundary fence and Gate, Retaining wall Plan and Details drawing	25 days	Aug 18 '26	Sep 15 '26	56 days	No								0%							
80	80	1.3.3.2	Mechanical Design	88 days	Jun 18 '26	Sep 28 '26	53 days	No								0%							
81	81	1.3.3.2.1	Overall Piping General Arrangement (Yard Pipe Routing)	70 days	Jun 27 '26	Sep 16 '26	100 days	No								0%							
82	82	1.3.3.2.2	SRF Main Building	88 days	Jun 18 '26	Sep 28 '26	95 days	No								0%							
83	83	1.3.3.2.2.1	Service Water Distribution System	15 days	Sep 11 '26	Sep 28 '26	95 days	No								0%							
84	84	1.3.3.2.2.2	Waste Water Treatment System	15 days	Sep 11 '26	Sep 28 '26	95 days	No								0%							
85	85	1.3.3.2.2.3	Fire Protection, Detection and Fire Fighting	15 days	Aug 29 '26	Sep 15 '26	97 days	No								0%							
86	86	1.3.3.2.2.4	SRF Production System	51 days	Jun 18 '26	Aug 15 '26	117 days	No								0%							
87	87	1.3.3.2.2.5	Ventilation and air conditioning system equipment	15 days	Aug 29 '26	Sep 15 '26	106 days	No								0%							
88	88	1.3.3.2.3	SRF Auxiliary building	52 days	Jul 30 '26	Sep 28 '26	17 days	No								0%							
89	89	1.3.3.2.3.1	Diesel Storage System Design (Incl. Calculation)	20 days	Jul 30 '26	Aug 21 '26	17 days	No								0%							
90	90	1.3.3.2.3.2	Truck Weighing Scale & Control Building	26 days	Aug 29 '26	Sep 28 '26	118 days	No								0%							
91	91	1.3.3.2.3.2.1	Service Water Distribution System	15 days	Sep 11 '26	Sep 28 '26	118 days	No								0%							
92	92	1.3.3.2.3.2.2	Waste Water Treatment System	15 days	Sep 11 '26	Sep 28 '26	118 days	No								0%							
93	93	1.3.3.2.3.2.3	Fire Protection, Detection and Fire Fighting	15 days	Aug 29 '26	Sep 15 '26	129 days	No								0%							
94	94	1.3.3.2.3.2.4	Ventilation and air conditioning system equipment	15 days	Aug 29 '26	Sep 15 '26	129 days	No								0%							
95	95	1.3.3.2.3.3	Fire Water Pump Shelter	26 days	Aug 29 '26	Sep 28 '26	112 days	No								0%							
96	96	1.3.3.2.3.3.1	Service Water Distribution System	15 days	Sep 11 '26	Sep 28 '26	118 days	No								0%							
97	97	1.3.3.2.3.3.2	Waste Water Treatment System	15 days	Sep 11 '26	Sep 28 '26	118 days	No								0%							
98	98	1.3.3.2.3.3.3	Fire Protection, Detection and Fire Fighting	15 days	Aug 29 '26	Sep 15 '26	112 days	No								0%							
99	99	1.3.3.2.3.3.4	Ventilation and air conditioning system equipment	15 days	Aug 29 '26	Sep 15 '26	129 days	No								0%							
100	100	1.3.3.2.4	SRF Other building	26 days	Aug 29 '26	Sep 28 '26	120 days	No								0%							
101	101	1.3.3.2.4.1	Administration Building	26 days	Aug 29 '26	Sep 28 '26	115 days	No								0%							
102	102	1.3.3.2.4.1.1	Service Water Distribution System	15 days	Sep 11 '26	Sep 28 '26	115 days	No								0%							
103	103	1.3.3.2.4.1.2	Waste Water Treatment System	15 days	Sep 11 '26	Sep 28 '26	115 days	No								0%							
104	104	1.3.3.2.4.1.3	Fire Protection, Detection and Fire Fighting	15 days	Aug 29 '26	Sep 15 '26	126 days	No								0%							
105	105	1.3.3.2.4.1.4	Ventilation and air conditioning system equipment	15 days	Aug 29 '26	Sep 15 '26	126 days	No								0%							
106	106	1.3.3.2.4.2	Warehouse & Maintenance Workshop Building	26 days	Aug 29 '26	Sep 28 '26	115 days	No								0%							
Project: SOLID RECOVERED FUEL Date: 25th June 2026 Revision: D (Owner)			Baseline Milestone Baseline Summary Critical Task Progress Task Split Task Progress Manual Task Manual Split Manual Progress Start Time only Finish Time only Schedule only Critical Critical Split Baseline Baseline Split Milestone Manual Milestone Abstract Task Progress Abstract Manual Abstract Project Abstract Abstract Grouping																				
Page 2 of 10																							

Project Master Schedule																							
ID	ID	WBS	Task Name	Duration	Start Time	Finish Time	Total Slack	Critical	6	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
107	107	1.3.3.2.4.2.1	Service Water Distribution System	15 days	Sep 11 '26	Sep 28 '26	115 days	No															
108	108	1.3.3.2.4.2.2	Waste Water Treatment System	15 days	Sep 11 '26	Sep 28 '26	115 days	No															
109	109	1.3.3.2.4.2.3	Fire Protection, Detection and Fire Fighting	15 days	Aug 29 '26	Sep 15 '26	126 days	No															
110	110	1.3.3.2.4.2.4	Ventilation and air conditioning system equipment	15 days	Aug 29 '26	Sep 15 '26	126 days	No															
111	111	1.3.3.2.4.3	Guard House	26 days	Aug 29 '26	Sep 28 '26	120 days	No															
112	112	1.3.3.2.4.3.1	Service Water Distribution System	15 days	Sep 11 '26	Sep 28 '26	120 days	No															
113	113	1.3.3.2.4.3.2	Waste Water Treatment System	15 days	Sep 11 '26	Sep 28 '26	120 days	No															
114	114	1.3.3.2.4.3.3	Fire Protection, Detection and Fire Fighting	15 days	Aug 29 '26	Sep 15 '26	131 days	No															
115	115	1.3.3.2.4.3.4	Ventilation and air conditioning system equipment	15 days	Aug 29 '26	Sep 15 '26	131 days	No															
116	116	1.3.3.3	Electrical System Design	70 days	Jun 27 '26	Sep 16 '26	35 days	No															
117	117	1.3.3.3.1	Overall Single Line Diagram	20 days	Jul 9 '26	Jul 31 '26	25 days	No															
118	118	1.3.3.3.2	SRF Main Building	70 days	Jun 27 '26	Sep 16 '26	98 days	No															
119	119	1.3.3.3.2.1	Outside Building	70 days	Jun 27 '26	Sep 16 '26	103 days	No															
120	120	1.3.3.3.2.1.1	Electrical Equipment Layout and Arrangement	70 days	Jun 27 '26	Sep 16 '26	103 days	No															
121	121	1.3.3.3.2.1.2	Grounding and Lightning Protection System	70 days	Jun 27 '26	Sep 16 '26	108 days	No															
122	122	1.3.3.3.2.1.3	Raceway, Conduit, Ductbank, and Trench System Routing Layout Outside Building	70 days	Jun 27 '26	Sep 16 '26	108 days	No															
123	123	1.3.3.3.2.1.4	Road and Area Lighting System	70 days	Jun 27 '26	Sep 16 '26	103 days	No															
124	124	1.3.3.3.2.1.5	Fire Alarm and Detection System	70 days	Jun 27 '26	Sep 16 '26	103 days	No															
125	125	1.3.3.3.2.1.6	CCTV, LAN, Telephone and Paging System	70 days	Jun 27 '26	Sep 16 '26	103 days	No															
126	126	1.3.3.3.2.2	Main Building	70 days	Jun 27 '26	Sep 16 '26	98 days	No															
127	127	1.3.3.3.2.2.1	Grounding and Lightning System	70 days	Jun 27 '26	Sep 16 '26	98 days	No															
128	128	1.3.3.3.2.2.2	Cable and Raceway System	70 days	Jun 27 '26	Sep 16 '26	98 days	No															
129	129	1.3.3.3.2.2.3	Lighting System	70 days	Jun 27 '26	Sep 16 '26	98 days	No															
130	130	1.3.3.3.2.2.4	Fire Alarm System	70 days	Jun 27 '26	Sep 16 '26	98 days	No															
131	131	1.3.3.3.2.2.5	Communication System	70 days	Jun 27 '26	Sep 16 '26	98 days	No															
132	132	1.3.3.3.3	SRF Auxiliary building	70 days	Jun 27 '26	Sep 16 '26	123 days	No															
133	133	1.3.3.3.3.1	Truck Weighing Scale & Control Building	70 days	Jun 27 '26	Sep 16 '26	123 days	No															
134	134	1.3.3.3.3.1.1	Grounding and Lightning System	70 days	Jun 27 '26	Sep 16 '26	123 days	No															
135	135	1.3.3.3.3.1.2	Cable and Raceway System	70 days	Jun 27 '26	Sep 16 '26	123 days	No															
136	136	1.3.3.3.3.1.3	Lighting System	70 days	Jun 27 '26	Sep 16 '26	123 days	No															
137	137	1.3.3.3.3.1.4	Fire Alarm System	70 days	Jun 27 '26	Sep 16 '26	123 days	No															
138	138	1.3.3.3.3.1.5	Communication System	70 days	Jun 27 '26	Sep 16 '26	123 days	No															
139	139	1.3.3.3.3.2	Fire Water Pump Shelter	70 days	Jun 27 '26	Sep 16 '26	123 days	No															
140	140	1.3.3.3.3.2.1	Grounding and Lightning System	70 days	Jun 27 '26	Sep 16 '26	123 days	No															
141	141	1.3.3.3.3.2.2	Cable and Raceway System	70 days	Jun 27 '26	Sep 16 '26	123 days	No															
142	142	1.3.3.3.3.2.3	Lighting System	70 days	Jun 27 '26	Sep 16 '26	123 days	No															
143	143	1.3.3.3.3.2.4	Fire Alarm System	70 days	Jun 27 '26	Sep 16 '26	123 days	No															
144	144	1.3.3.3.3.2.5	Communication System	70 days	Jun 27 '26	Sep 16 '26	123 days	No															
145	145	1.3.3.3.4	SRF Other building	70 days	Jun 27 '26	Sep 16 '26	115 days	No															
146	146	1.3.3.3.4.1	Administration Building	70 days	Jun 27 '26	Sep 16 '26	115 days	No															
147	147	1.3.3.3.4.1.1	Grounding and Lightning System	70 days	Jun 27 '26	Sep 16 '26	115 days	No															
148	148	1.3.3.3.4.1.2	Cable and Raceway System	70 days	Jun 27 '26	Sep 16 '26	115 days	No															
149	149	1.3.3.3.4.1.3	Lighting System	70 days	Jun 27 '26	Sep 16 '26	115 days	No															
150	150	1.3.3.3.4.1.4	Fire Alarm System	70 days	Jun 27 '26	Sep 16 '26	115 days	No															
151	151	1.3.3.3.4.1.5	Communication System	70 days	Jun 27 '26	Sep 16 '26	115 days	No															
152	152	1.3.3.3.4.2	Warehouse & Maintenance Workshop Building	70 days	Jun 27 '26	Sep 16 '26	115 days	No															
153	153	1.3.3.3.4.2.1	Grounding and Lightning System	70 days	Jun 27 '26	Sep 16 '26	115 days	No															
154	154	1.3.3.3.4.2.2	Cable and Raceway System	70 days	Jun 27 '26	Sep 16 '26	115 days	No															
155	155	1.3.3.3.4.2.3	Lighting System	70 days	Jun 27 '26	Sep 16 '26	115 days	No															
156	156	1.3.3.3.4.2.4	Fire Alarm System	70 days	Jun 27 '26	Sep 16 '26	115 days	No															
157	157	1.3.3.3.4.2.5	Communication System	70 days	Jun 27 '26	Sep 16 '26	115 days	No															
158	158	1.3.3.3.4.3	Guard House	70 days	Jun 27 '26	Sep 16 '26	115 days	No															
159	159	1.3.3.3.4.3.1	Grounding and Lightning System	70 days	Jun 27 '26	Sep 16 '26	115 days	No															
Project: SOLID RECOVERED FUEL Date: 25th June 2026 Revision: D (Owner)			Baseline Milestone Baseline Summary Critical Task Progress Task Split Task Progress Manual Task Manual Split Manual Progress Start Time only Finish Time only Schedule only Critical Critical Split Baseline Baseline Split Milestone Manual Milestone Abstract Task Progress Abstract Manual Abstract Project Abstract Abstract Grouping																				
Page 3 of 10																							

Project Master Schedule																												
ID	ID	WBS	Task Name	Duration	Start Time	Finish Time	Total Slack	Critical	6	Mar	Apr	Qtr 2, 2026	May	Jun	Jul	Qtr 3, 2026	Aug	Sep	Oct	Qtr 4, 2026	Nov	Dec	Jan	Qtr 1, 2027	Feb	Mar	Apr	Qtr 2, 2027
160	160	1.3.3.3.4.3.2	Cable and Raceway System	70 days	Jun 27 '26	Sep 16 '26	115 days	No										0%										
161	161	1.3.3.3.4.3.3	Lighting System	70 days	Jun 27 '26	Sep 16 '26	115 days	No										0%										
162	162	1.3.3.3.4.3.4	Fire Alarm System	70 days	Jun 27 '26	Sep 16 '26	115 days	No										0%										
163	163	1.3.3.3.4.3.5	Communication System	70 days	Jun 27 '26	Sep 16 '26	115 days	No										0%										
164	164	1.3.3.4	C&I Design	70 days	Jun 27 '26	Sep 16 '26	6 days	No										0%										
165	165	1.4	Procurement, Manufacturing and Transportation	194 days	May 28 '26	Jan 8 '27	27 days	No																				
166	166	1.4.1	Purchase Order (LOA/PO)	110 days	May 28 '26	Oct 2 '26	30 days	No											0%									
167	167	1.4.1.1	Mechanical (LOA/PO)	110 days	May 28 '26	Oct 2 '26	23 days	No											0%									
168	168	1.4.1.1.1	Waste Receiving System (Weighbridge)	18 days	Aug 29 '26	Sep 18 '26	10 days	No										0%										
169	169	1.4.1.1.2	SRF Production System	18 days	May 28 '26	Jun 17 '26	30 days	No																				
170	170	1.4.1.1.2.1	Grab Bucket System	18 days	May 28 '26	Jun 17 '26	30 days	No																				
171	171	1.4.1.1.2.1.1	Stationary Grab Loader	18 days	May 28 '26	Jun 17 '26	30 days	No																				
172	172	1.4.1.1.2.1.2	Feeding hopper	18 days	May 28 '26	Jun 17 '26	30 days	No																				
173	173	1.4.1.1.2.2	Shredder (Pre-Shredder)	18 days	May 28 '26	Jun 17 '26	30 days	No																				
174	174	1.4.1.1.2.3	Conveyor Equipment	18 days	May 28 '26	Jun 17 '26	30 days	No																				
175	175	1.4.1.1.2.3.1	Chain Conveyor	18 days	May 28 '26	Jun 17 '26	30 days	No																				
176	176	1.4.1.1.2.3.2	Belt Conveyor (Transfer conveyor)	18 days	May 28 '26	Jun 17 '26	30 days	No																				
177	177	1.4.1.1.2.4	Magnetic Separator	18 days	May 28 '26	Jun 17 '26	30 days	No																				
178	178	1.4.1.1.2.5	Trommel Screen	18 days	May 28 '26	Jun 17 '26	30 days	No																				
179	179	1.4.1.1.2.6	Fully Automatic Hydraulic Baler	18 days	May 28 '26	Jun 17 '26	30 days	No																				
180	180	1.4.1.1.2.7	Air Treatment System	18 days	May 28 '26	Jun 17 '26	30 days	No																				
181	181	1.4.1.1.2.8	Electrical Control System	18 days	May 28 '26	Jun 17 '26	30 days	No																				
182	182	1.4.1.1.3	Building water supply and drainage system	19 days	Sep 11 '26	Oct 2 '26	2 days	No											0%									
183	183	1.4.1.1.3.1	Service Water Distribution System	19 days	Sep 11 '26	Oct 2 '26	2 days	No											0%									
184	184	1.4.1.1.3.2	Waste Water Treatment System	19 days	Sep 11 '26	Oct 2 '26	2 days	No											0%									
185	185	1.4.1.1.4	Fire Protection, Detection and Fire Fighting	19 days	Aug 29 '26	Sep 19 '26	5 days	No											0%									
186	186	1.4.1.1.5	Ventilation and air conditioning system equipment	17 days	Aug 29 '26	Sep 17 '26	16 days	No											0%									
187	187	1.4.1.1.6	Overhead Traveling Crane	17 days	Aug 29 '26	Sep 17 '26	36 days	No											0%									
188	188	1.4.1.1.7	Diesel Oil Storage Tank	17 days	Aug 28 '26	Sep 16 '26	17 days	No											0%									
189	189	1.4.1.2	Electrical System (LOA/PO)	41 days	Aug 1 '26	Sep 17 '26	32 days	No											0%									
190	190	1.4.1.2.1	Distribution Transformer	17 days	Aug 29 '26	Sep 17 '26	13 days	No											0%									
191	191	1.4.1.2.2	AC Distribution Board	17 days	Aug 29 '26	Sep 17 '26	13 days	No											0%									
192	192	1.4.1.2.3	Grounding and Lightning System	17 days	Aug 1 '26	Aug 20 '26	73 days	No											0%									
193	193	1.4.1.2.4	Cable and Raceway System	17 days	Aug 29 '26	Sep 17 '26	8 days	No											0%									
194	194	1.4.1.2.5	Lighting System and Small Power	17 days	Aug 29 '26	Sep 17 '26	8 days	No											0%									
195	195	1.4.1.2.6	Fire Alarm System	17 days	Aug 29 '26	Sep 17 '26	8 days	No											0%									
196	196	1.4.1.2.7	Communication System	17 days	Aug 29 '26	Sep 17 '26	8 days	No											0%									
197	197	1.4.1.3	C&I (LOA/PO)	15 days	Sep 11 '26	Sep 28 '26	1 day	No											0%									
198	198	1.4.2	Manufacturing	158 days	Jun 18 '26	Dec 18 '26	28 days	No																				
199	199	1.4.2.1	Mechanical Manufacturing	158 days	Jun 18 '26	Dec 18 '26	28 days	No																				
200	200	1.4.2.1.1	Waste Receiving System (Weighbridge)	71 days	Sep 19 '26	Dec 10 '26	10 days	No																				
201	201	1.4.2.1.2	SRF Production System	112 days	Jun 18 '26	Oct 26 '26	30 days	No																				
202	202	1.4.2.1.2.1	Grab Bucket System	97 days	Jun 18 '26	Oct 8 '26	45 days	No																				
203	203	1.4.2.1.2.1.1	Stationary Grab Loader	97 days	Jun 18 '26	Oct 8 '26	45 days	No																				
204	204	1.4.2.1.2.1.2	Feeding hopper	97 days	Jun 18 '26	Oct 8 '26	45 days	No																				
205	205	1.4.2.1.2.2	Shredder (Pre-Shredder)	97 days	Jun 18 '26	Oct 8 '26	45 days	No																				
206	206	1.4.2.1.2.3	Conveyor Equipment	97 days	Jun 18 '26	Oct 8 '26	45 days	No																				
207	207	1.4.2.1.2.3.1	Chain Conveyor	97 days	Jun 18 '26	Oct 8 '26	45 days	No																				
208	208	1.4.2.1.2.3.2	Belt Conveyor (Transfer conveyor)	97 days	Jun 18 '26	Oct 8 '26	45 days	No																				
209	209	1.4.2.1.2.4	Magnetic Separator	112 days	Jun 18 '26	Oct 26 '26	30 days	No																				
210	210	1.4.2.1.2.5	Trommel Screen	97 days	Jun 18 '26	Oct 8 '26	45 days	No																				
211	211	1.4.2.1.2.6	Fully Automatic Hydraulic Baler	97 days	Jun 18 '26	Oct 8 '26	45 days	No																				
212	212	1.4.2.1.2.7	Air Treatment System	109 days	Jun 18 '26	Oct 22 '26	33 days	No																				
Project: SOLID RECOVERED FUEL Date: 25th June 2026 Revision: D (Owner)			Baseline Milestone	◆	Task Progress	▬	Finish Time only	┐	Baseline Split	⋯⋯⋯⋯⋯⋯	Manual Abstract	▬																
			Baseline Summary	▬	Manual Task	▬	Schedule only	▬	Milestone	◆	Project Abstract	▬																
			Critical Task Progress	▬	Manual Split	⋯⋯⋯⋯⋯⋯	Critical	▬	Manual Milestone	◆	Abstract Grouping	▬																
			Task	▬	Manual Progress	▬	Critical Split	⋯⋯⋯⋯⋯⋯	Abstract Task Progress	▬																		
			Split	⋯⋯⋯⋯⋯⋯	Start Time only	┐	Baseline	▬	Abstract	▬																		
Page 4 of 10																												

Project Master Schedule																			
ID	ID	WBS	Task Name	Duration	Start Time	Finish Time	Total Slack	Critical	Qtr 1, 2026	Qtr 2, 2026	Qtr 3, 2026	Qtr 4, 2026	Qtr 1, 2027	Qtr 2, 2027	Qtr 3, 2027	Qtr 4, 2027			
					Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	
213	213	1.4.2.1.2.8	Electrical Control System	109 days	Jun 18 '26	Oct 22 '26	33 days	No											
214	214	1.4.2.1.3	Building water supply and drainage system	66 days	Oct 3 '26	Dec 18 '26	2 days	No											
215	215	1.4.2.1.3.1	Service Water Distribution System	66 days	Oct 3 '26	Dec 18 '26	2 days	No											
216	216	1.4.2.1.3.2	Waste Water Treatment System	66 days	Oct 3 '26	Dec 18 '26	2 days	No											
217	217	1.4.2.1.4	Fire Protection, Detection and Fire Fighting	70 days	Sep 21 '26	Dec 10 '26	5 days	No											
218	218	1.4.2.1.5	Ventilation and air conditioning system equipment	71 days	Sep 18 '26	Dec 9 '26	16 days	No											
219	219	1.4.2.1.6	Overhead Traveling Crane	71 days	Sep 18 '26	Dec 9 '26	36 days	No											
220	220	1.4.2.1.7	Diesel Oil Storage Tank	69 days	Sep 17 '26	Dec 5 '26	17 days	No											
221	221	1.4.2.2	Electrical System Manufacturing	95 days	Aug 21 '26	Dec 9 '26	13 days	No											
222	222	1.4.2.2.1	Distribution Transformer	71 days	Sep 18 '26	Dec 9 '26	13 days	No											
223	223	1.4.2.2.2	AC Distribution Board	71 days	Sep 18 '26	Dec 9 '26	13 days	No											
224	224	1.4.2.2.3	Grounding and Lightning System	30 days	Aug 21 '26	Sep 24 '26	73 days	No											
225	225	1.4.2.2.4	Cable and Raceway System	71 days	Sep 18 '26	Dec 9 '26	8 days	No											
226	226	1.4.2.2.5	Lighting System and Small Power	71 days	Sep 18 '26	Dec 9 '26	8 days	No											
227	227	1.4.2.2.6	Fire Alarm System	71 days	Sep 18 '26	Dec 9 '26	8 days	No											
228	228	1.4.2.2.7	Communication System	71 days	Sep 18 '26	Dec 9 '26	8 days	No											
229	229	1.4.2.3	C&I Manufacturing	69 days	Sep 29 '26	Dec 17 '26	1 day	No											
230	230	1.4.3	Shipment	87 days	Sep 25 '26	Jan 4 '27	27 days	No											
231	231	1.4.3.1	Mechanical Shipment	60 days	Oct 27 '26	Jan 4 '27	27 days	No											
232	232	1.4.3.1.1	Waste Receiving System (Weighbridge)	13 days	Dec 11 '26	Dec 25 '26	10 days	No											
233	233	1.4.3.1.2	SRF Production System	53 days	Oct 27 '26	Dec 26 '26	17 days	No											
234	234	1.4.3.1.2.1	Grab Bucket System	18 days	Oct 27 '26	Nov 16 '26	30 days	No											
235	235	1.4.3.1.2.1.1	Stationary Grab Loader	18 days	Oct 27 '26	Nov 16 '26	30 days	No											
236	236	1.4.3.1.2.1.2	Feeding hopper	18 days	Oct 27 '26	Nov 16 '26	30 days	No											
237	237	1.4.3.1.2.2	Shredder (Pre-Shredder)	18 days	Oct 27 '26	Nov 16 '26	30 days	No											
238	238	1.4.3.1.2.3	Conveyor Equipment	18 days	Oct 27 '26	Nov 16 '26	30 days	No											
239	239	1.4.3.1.2.3.1	Chain Conveyor	18 days	Oct 27 '26	Nov 16 '26	30 days	No											
240	240	1.4.3.1.2.3.2	Belt Conveyor (Transfer conveyor)	18 days	Oct 27 '26	Nov 16 '26	30 days	No											
241	241	1.4.3.1.2.4	Magnetic Separator	18 days	Oct 27 '26	Nov 16 '26	30 days	No											
242	242	1.4.3.1.2.5	Trommel Screen	18 days	Oct 27 '26	Nov 16 '26	30 days	No											
243	243	1.4.3.1.2.6	Fully Automatic Hydraulic Baler	18 days	Oct 27 '26	Nov 16 '26	30 days	No											
244	244	1.4.3.1.2.7	Air Treatment System	18 days	Oct 27 '26	Nov 16 '26	30 days	No											
245	245	1.4.3.1.2.8	Electrical Control System	18 days	Oct 27 '26	Nov 16 '26	30 days	No											
246	246	1.4.3.1.2.9	Diesel Oil Storage Tank	18 days	Dec 7 '26	Dec 26 '26	17 days	No											
247	247	1.4.3.1.3	Building water supply and drainage system	14 days	Dec 19 '26	Jan 4 '27	2 days	No											
248	248	1.4.3.1.3.1	Service Water Distribution System	14 days	Dec 19 '26	Jan 4 '27	2 days	No											
249	249	1.4.3.1.3.2	Waste Water Treatment System	14 days	Dec 19 '26	Jan 4 '27	2 days	No											
250	250	1.4.3.1.4	Fire Protection, Detection and Fire Fighting	14 days	Dec 11 '26	Dec 26 '26	5 days	No											
251	251	1.4.3.1.5	Ventilation and air conditioning system equipment	13 days	Dec 10 '26	Dec 24 '26	16 days	No											
252	252	1.4.3.1.6	Overhead Traveling Crane	13 days	Dec 10 '26	Dec 24 '26	36 days	No											
253	253	1.4.3.2	Electrical System Shipment	79 days	Sep 25 '26	Dec 25 '26	13 days	No											
254	254	1.4.3.2.1	Distribution Transformer	14 days	Dec 10 '26	Dec 25 '26	13 days	No											
255	255	1.4.3.2.2	AC Distribution Board	14 days	Dec 10 '26	Dec 25 '26	13 days	No											
256	256	1.4.3.2.3	Grounding and Lightning System	14 days	Sep 25 '26	Oct 10 '26	73 days	No											
257	257	1.4.3.2.4	Cable and Raceway System	14 days	Dec 10 '26	Dec 25 '26	8 days	No											
258	258	1.4.3.2.5	Lighting System and Small Power	14 days	Dec 10 '26	Dec 25 '26	8 days	No											
259	259	1.4.3.2.6	Fire Alarm System	14 days	Dec 10 '26	Dec 25 '26	8 days	No											
260	260	1.4.3.2.7	Communication System	14 days	Dec 10 '26	Dec 25 '26	8 days	No											
261	261	1.4.3.3	C&I Shipment	14 days	Dec 18 '26	Jan 2 '27	1 day	No											
262	262	1.4.4	Site Delivery	77 days	Oct 12 '26	Jan 8 '27	27 days	No											
263	263	1.4.4.1	Mechanical Site Delivery	46 days	Nov 17 '26	Jan 8 '27	27 days	No											
264	264	1.4.4.1.1	Waste Receiving System (Weighbridge)	4 days	Dec 26 '26	Dec 30 '26	10 days	No											
265	265	1.4.4.1.2	SRF Production System	8 days	Nov 17 '26	Nov 25 '26	30 days	No											
Project: SOLID RECOVERED FUEL Date: 25th June 2026 Revision: D (Owner)			Baseline Milestone	◆	Task Progress	▬	Finish Time only	┌	Baseline Split		Manual Abstract	▬							
			Baseline Summary	▬	Manual Task	▬	Schedule only	▬	Milestone	◆	Project Abstract	▬							
			Critical Task Progress	▬	Manual Split		Critical	▬	Manual Milestone	◆	Abstract Grouping	▬							
			Task	▬	Manual Progress	▬	Critical Split		Abstract Task Progress	▬									
			Split		Start Time only	┌	Baseline	▬	Abstract	▬									
			Page 5 of 10																

Project Master Schedule																							
ID	ID	WBS	Task Name	Duration	Start Time	Finish Time	Total Slack	Critical	6	Mar	Qtr 2, 2026			Qtr 3, 2026			Qtr 4, 2026			Qtr 1, 2027			Q
											Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
266	266	1.4.4.1.2.1	Grab Bucket System	8 days	Nov 17 '26	Nov 25 '26	30 days	No															
267	267	1.4.4.1.2.1.1	Stationary Grab Loader	8 days	Nov 17 '26	Nov 25 '26	30 days	No															
268	268	1.4.4.1.2.1.2	Feeding hopper	8 days	Nov 17 '26	Nov 25 '26	30 days	No															
269	269	1.4.4.1.2.2	Shredder (Pre-Shredder)	8 days	Nov 17 '26	Nov 25 '26	30 days	No															
270	270	1.4.4.1.2.3	Conveyor Equipment	8 days	Nov 17 '26	Nov 25 '26	30 days	No															
271	271	1.4.4.1.2.3.1	Chain Conveyor	8 days	Nov 17 '26	Nov 25 '26	30 days	No															
272	272	1.4.4.1.2.3.2	Belt Conveyor (Transfer conveyor)	8 days	Nov 17 '26	Nov 25 '26	30 days	No															
273	273	1.4.4.1.2.4	Magnetic Separator	8 days	Nov 17 '26	Nov 25 '26	30 days	No															
274	274	1.4.4.1.2.5	Trommel Screen	8 days	Nov 17 '26	Nov 25 '26	30 days	No															
275	275	1.4.4.1.2.6	Fully Automatic Hydraulic Baler	8 days	Nov 17 '26	Nov 25 '26	30 days	No															
276	276	1.4.4.1.2.7	Air Treatment System	8 days	Nov 17 '26	Nov 25 '26	30 days	No															
277	277	1.4.4.1.2.8	Electrical Control System	8 days	Nov 17 '26	Nov 25 '26	30 days	No															
278	278	1.4.4.1.3	Building water supply and drainage system	4 days	Jan 5 '27	Jan 8 '27	2 days	No															
279	279	1.4.4.1.3.1	Service Water Distribution System	4 days	Jan 5 '27	Jan 8 '27	2 days	No															
280	280	1.4.4.1.3.2	Waste Water Treatment System	4 days	Jan 5 '27	Jan 8 '27	2 days	No															
281	281	1.4.4.1.4	Fire Protection, Detection and Fire Fighting	4 days	Dec 28 '26	Dec 31 '26	5 days	No															
282	282	1.4.4.1.5	Ventilation and air conditioning system equipment	4 days	Dec 25 '26	Dec 29 '26	16 days	No															
283	283	1.4.4.1.6	Overhead Traveling Crane	4 days	Dec 25 '26	Dec 29 '26	36 days	No															
284	284	1.4.4.1.7	Diesel Oil Storage Tank	4 days	Dec 28 '26	Dec 31 '26	17 days	No															
285	285	1.4.4.2	Electrical System Site Delivery	69 days	Oct 12 '26	Dec 30 '26	13 days	No															
286	286	1.4.4.2.1	Distribution Transformer	4 days	Dec 26 '26	Dec 30 '26	13 days	No															
287	287	1.4.4.2.2	AC Distribution Board	4 days	Dec 26 '26	Dec 30 '26	13 days	No															
288	288	1.4.4.2.3	Grounding and Lightning System	4 days	Oct 12 '26	Oct 15 '26	73 days	No															
289	289	1.4.4.2.4	Cable and Raceway System	4 days	Dec 26 '26	Dec 30 '26	8 days	No															
290	290	1.4.4.2.5	Lighting System and Small Power	4 days	Dec 26 '26	Dec 30 '26	8 days	No															
291	291	1.4.4.2.6	Fire Alarm System	4 days	Dec 26 '26	Dec 30 '26	8 days	No															
292	292	1.4.4.2.7	Communication System	4 days	Dec 26 '26	Dec 30 '26	8 days	No															
293	293	1.4.4.3	C&I Site Delivery	4 days	Jan 4 '27	Jan 7 '27	1 day	No															
294	294	1.5	Construction	233 days	May 20 '26	Feb 15 '27	15 days	No															
295	295	1.5.1	Construction Permit	130 days	May 20 '26	Oct 17 '26	16 days	No															
296	296	1.5.1.1	SRF Main Building Permit	50 days	May 20 '26	Jul 16 '26	16 days	No															
297	297	1.5.1.2	Other Building Permit	80 days	Jul 17 '26	Oct 17 '26	16 days	No															
298	298	1.5.1.3	Diesel Oil Storage Tank Permit	45 days	Aug 22 '26	Oct 13 '26	35 days	No															
299	299	1.5.2	Subcontracting	40 days	Jun 27 '26	Aug 12 '26	0 days	Yes															
300	300	1.5.2.1	Civil, M&E	40 days	Jun 27 '26	Aug 12 '26	0 days	Yes															
301	301	1.5.2.1.1	RFP	6 days	Jun 27 '26	Jul 3 '26	0 days	Yes															
302	302	1.5.2.1.2	LOA/PO	20 days	Jul 4 '26	Jul 27 '26	0 days	Yes															
303	303	1.5.2.1.3	Manpower Mobilization	14 days	Jul 28 '26	Aug 12 '26	0 days	Yes															
304	304	1.5.3	Temporary Construction	55 days	Jun 27 '26	Aug 29 '26	14 days	No															
305	305	1.5.3.1	Temporary fence	26 days	Jun 27 '26	Jul 27 '26	14 days	No															
306	306	1.5.3.2	Site Leveling Work	26 days	Jun 27 '26	Jul 27 '26	14 days	No															
307	307	1.5.3.3	Temporary rebar fabrication area	15 days	Aug 13 '26	Aug 29 '26	15 days	No															
308	308	1.5.3.4	Temporary laydown area	15 days	Aug 13 '26	Aug 29 '26	15 days	No															
309	309	1.5.3.5	Equipment pre-assambly area	15 days	Aug 13 '26	Aug 29 '26	15 days	No															
310	310	1.5.3.6	Temporary internal road completion	15 days	Aug 13 '26	Aug 29 '26	15 days	No															
311	311	1.5.4	Civil work	150 days	Aug 13 '26	Feb 3 '27	0 days	Yes															
312	312	1.5.4.1	SRF Main Building	150 days	Aug 13 '26	Feb 3 '27	0 days	Yes															
313	313	1.5.4.1.1	Piling Work	60 days	Aug 13 '26	Oct 21 '26	0 days	Yes															
314	314	1.5.4.1.2	Foundation Excavation	50 days	Aug 31 '26	Oct 27 '26	0 days	Yes															
315	315	1.5.4.1.3	Foundation up to ground	60 days	Sep 17 '26	Nov 25 '26	0 days	Yes															
316	316	1.5.4.1.4	Super structure	60 days	Oct 22 '26	Dec 30 '26	0 days	Yes															
317	317	1.5.4.1.5	Rooftopping and balance work	60 days	Nov 26 '26	Feb 3 '27	0 days	Yes															
318	318	1.5.4.1.6	Architectures work	30 days	Dec 29 '26	Feb 1 '27	0 days	Yes															
Project: SOLID RECOVERED FUEL Date: 25th June 2026 Revision: D (Owner)			Baseline Milestone	◆	Task Progress	▬	Finish Time only	┌	Baseline Split	▬	Manual Abstract	▬											
			Baseline Summary	▬	Manual Task	▬	Schedule only	▬	Milestone	◆	Project Abstract	▬											
			Critical Task Progress	▬	Manual Split	▬	Critical	▬	Manual Milestone	◆	Abstract Grouping	▬											
			Task	▬	Manual Progress	▬	Critical Split	▬	Abstract Task Progress	▬													
			Split	▬	Start Time only	┌	Baseline	▬	Abstract	▬													
Page 6 of 10																							

Project Master Schedule																							
ID	ID	WBS	Task Name	Duration	Start Time	Finish Time	Total Slack	Critical	6	Mar	Qtr 2, 2026			Qtr 3, 2026			Qtr 4, 2026			Qtr 1, 2027			Q
											Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
319	319	1.5.4.2	SRF Auxiliary building	60 days	Oct 19 '26	Dec 26 '26	16 days	No															
320	320	1.5.4.2.1	Service Water and Fire Water Storage Tank Foundation	32 days	Oct 19 '26	Nov 24 '26	16 days	No															
321	321	1.5.4.2.1.1	Piling Work	5 days	Oct 19 '26	Oct 23 '26	16 days	No															
322	322	1.5.4.2.1.2	Foundation Excavation	5 days	Oct 24 '26	Oct 29 '26	32 days	No															
323	323	1.5.4.2.1.3	Foundation work	15 days	Oct 30 '26	Nov 16 '26	32 days	No															
324	324	1.5.4.2.1.4	Clearance for equipment installation	7 days	Nov 17 '26	Nov 24 '26	32 days	No															
325	325	1.5.4.2.2	Fire Water Pump Shelter	35 days	Oct 24 '26	Dec 3 '26	16 days	No															
326	326	1.5.4.2.2.1	Piling Work	5 days	Oct 24 '26	Oct 29 '26	16 days	No															
327	327	1.5.4.2.2.2	Foundation Excavation	3 days	Oct 30 '26	Nov 2 '26	54 days	No															
328	328	1.5.4.2.2.3	Foundation work	10 days	Nov 3 '26	Nov 13 '26	54 days	No															
329	329	1.5.4.2.2.4	Super structure	10 days	Nov 14 '26	Nov 25 '26	54 days	No															
330	330	1.5.4.2.2.5	Architectures work	7 days	Nov 26 '26	Dec 3 '26	54 days	No															
331	331	1.5.4.2.3	Transformer Foundation	30 days	Oct 30 '26	Dec 3 '26	16 days	No															
332	332	1.5.4.2.3.1	Piling Work	5 days	Oct 30 '26	Nov 4 '26	16 days	No															
333	333	1.5.4.2.3.2	Foundation Excavation	3 days	Nov 5 '26	Nov 7 '26	36 days	No															
334	334	1.5.4.2.3.3	Foundation work	15 days	Nov 9 '26	Nov 25 '26	36 days	No															
335	335	1.5.4.2.3.4	Clearance for equipment installation	7 days	Nov 26 '26	Dec 3 '26	36 days	No															
336	336	1.5.4.2.4	Diesel Tank Storage Foundation	32 days	Nov 5 '26	Dec 11 '26	16 days	No															
337	337	1.5.4.2.4.1	Piling Work	5 days	Nov 5 '26	Nov 10 '26	16 days	No															
338	338	1.5.4.2.4.2	Foundation Excavation	5 days	Nov 11 '26	Nov 16 '26	34 days	No															
339	339	1.5.4.2.4.3	Foundation work	15 days	Nov 17 '26	Dec 3 '26	34 days	No															
340	340	1.5.4.2.4.4	Clearance for equipment installation	7 days	Dec 4 '26	Dec 11 '26	34 days	No															
341	341	1.5.4.2.5	Storm Water Retention Pond	35 days	Nov 17 '26	Dec 26 '26	51 days	No															
342	342	1.5.4.2.5.1	Foundation Excavation	5 days	Nov 17 '26	Nov 21 '26	51 days	No															
343	343	1.5.4.2.5.2	Foundation work	15 days	Nov 23 '26	Dec 9 '26	51 days	No															
344	344	1.5.4.2.5.3	Clearance for equipment installatio	15 days	Dec 10 '26	Dec 26 '26	51 days	No															
345	345	1.5.4.2.6	Truck Weighing Scale Control Building	52 days	Oct 19 '26	Dec 17 '26	34 days	No															
346	346	1.5.4.2.6.1	Piling Work	7 days	Oct 19 '26	Oct 26 '26	34 days	No															
347	347	1.5.4.2.6.2	Foundation Excavation	5 days	Oct 27 '26	Oct 31 '26	54 days	No															
348	348	1.5.4.2.6.3	Foundation up to ground	10 days	Nov 2 '26	Nov 12 '26	54 days	No															
349	349	1.5.4.2.6.4	Super structure	20 days	Nov 13 '26	Dec 5 '26	54 days	No															
350	350	1.5.4.2.6.5	Architectures work	10 days	Dec 7 '26	Dec 17 '26	54 days	No															
351	351	1.5.4.2.7	Truck Weighing Scale Foundation	32 days	Oct 27 '26	Dec 2 '26	34 days	No															
352	352	1.5.4.2.7.1	Piling Work	5 days	Oct 27 '26	Oct 31 '26	34 days	No															
353	353	1.5.4.2.7.2	Foundation Excavation	5 days	Nov 2 '26	Nov 6 '26	34 days	No															
354	354	1.5.4.2.7.3	Foundation work	15 days	Nov 7 '26	Nov 24 '26	34 days	No															
355	355	1.5.4.2.7.4	Clearance for equipment installation	7 days	Nov 25 '26	Dec 2 '26	34 days	No															
356	356	1.5.4.2.8	Pipe Trench, Duct Bank, Lighting pole support Structural Details Drawing	20 days	Nov 26 '26	Dec 18 '26	20 days	No															
357	357	1.5.4.2.9	Drainage system and Sump pit Structural Details drawing	20 days	Nov 26 '26	Dec 18 '26	20 days	No															
358	358	1.5.4.3	SRF Other building	92 days	Oct 19 '26	Feb 2 '27	26 days	No															
359	359	1.5.4.3.1	Administration building	64 days	Oct 19 '26	Dec 31 '26	44 days	No															
360	360	1.5.4.3.1.1	Piling Work	7 days	Oct 19 '26	Oct 26 '26	44 days	No															
361	361	1.5.4.3.1.2	Foundation Excavation	7 days	Oct 27 '26	Nov 3 '26	44 days	No															
362	362	1.5.4.3.1.3	Foundation work	15 days	Nov 4 '26	Nov 20 '26	44 days	No															
363	363	1.5.4.3.1.4	Super structure	20 days	Nov 21 '26	Dec 14 '26	44 days	No															
364	364	1.5.4.3.1.5	Architectures work	15 days	Dec 15 '26	Dec 31 '26	44 days	No															
365	365	1.5.4.3.2	Warehouse & Maintenance Workshop Building	72 days	Nov 11 '26	Feb 2 '27	16 days	No															
366	366	1.5.4.3.2.1	Piling Work	10 days	Nov 11 '26	Nov 21 '26	16 days	No															
367	367	1.5.4.3.2.2	Foundation Excavation	7 days	Nov 23 '26	Nov 30 '26	16 days	No															
368	368	1.5.4.3.2.3	Foundation work	15 days	Dec 1 '26	Dec 17 '26	16 days	No															
369	369	1.5.4.3.2.4	Super structure	30 days	Dec 18 '26	Jan 21 '27	16 days	No															
370	370	1.5.4.3.2.5	Overhead Traveling Crane installation	5 days	Jan 22 '27	Jan 27 '27	16 days	No															
371	371	1.5.4.3.2.6	Architectures work	15 days	Jan 16 '27	Feb 2 '27	16 days	No															
Project: SOLID RECOVERED FUEL Date: 25th June 2026 Revision: D (Owner)			Baseline Milestone Baseline Summary Critical Task Progress Task Split ◇ Task Progress Manual Task Manual Split Manual Progress Start Time only Finish Time only Schedule only Critical Critical Split Baseline Baseline Split Milestone Manual Milestone Abstract Task Progress Abstract ◆ ◆ Manual Abstract Project Abstract Abstract Grouping																				
Page 7 of 10																							

Project Master Schedule																								
ID	ID	WBS	Task Name	Duration	Start Time	Finish Time	Total Slack	Critical	6	Mar	Qtr 2, 2026			Qtr 3, 2026			Qtr 4, 2026			Qtr 1, 2027			Q	
											Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	
372	372	1.5.4.3.3	Guard House	31 days	Oct 27 '26	Dec 1 '26	70 days	No																
373	373	1.5.4.3.3.1	Piling Work	1 day	Oct 27 '26	Oct 27 '26	70 days	No																
374	374	1.5.4.3.3.2	Foundation Excavation	1 day	Oct 28 '26	Oct 28 '26	70 days	No																
375	375	1.5.4.3.3.3	Foundation work	7 days	Oct 29 '26	Nov 5 '26	70 days	No																
376	376	1.5.4.3.3.4	Super structure	15 days	Nov 6 '26	Nov 23 '26	70 days	No																
377	377	1.5.4.3.3.5	Architectures work	7 days	Nov 24 '26	Dec 1 '26	70 days	No																
378	378	1.5.4.3.4	Road, Parking area, Paving area	90 days	Oct 19 '26	Jan 30 '27	28 days	No																
379	379	1.5.4.3.5	Boundary fence and Gate, Retaining wall	90 days	Oct 19 '26	Jan 30 '27	28 days	No																
380	380	1.5.5	Mechanical work	71 days	Nov 25 '26	Feb 15 '27	10 days	No																
381	381	1.5.5.1	Yard Pipe Installation (Inter-connecting)	30 days	Jan 9 '27	Feb 12 '27	2 days	No																
382	382	1.5.5.2	SRF Main Building	40 days	Dec 31 '26	Feb 15 '27	0 days	Yes																
383	383	1.5.5.2.1	Service Water Distribution System	25 days	Jan 9 '27	Feb 6 '27	7 days	No																
384	384	1.5.5.2.2	Waste Water Treatment System	25 days	Jan 9 '27	Feb 6 '27	7 days	No																
385	385	1.5.5.2.3	Fire Protection, Detection and Fire Fighting	25 days	Jan 4 '27	Feb 1 '27	3 days	No																
386	386	1.5.5.2.4	Ventilation and air conditioning system equipment	25 days	Jan 4 '27	Feb 1 '27	12 days	No																
387	387	1.5.5.2.5	SRF Production System	40 days	Dec 31 '26	Feb 15 '27	0 days	Yes																
388	388	1.5.5.2.5.1	Waste Receiving System (Weighbridge)	30 days	Dec 31 '26	Feb 3 '27	10 days	No																
389	389	1.5.5.2.5.2	Fuel preparation system	40 days	Dec 31 '26	Feb 15 '27	0 days	Yes																
390	390	1.5.5.2.5.2.1	Grab Bucket System	40 days	Dec 31 '26	Feb 15 '27	0 days	Yes																
391	391	1.5.5.2.5.2.1	Stationary Grab Loader	40 days	Dec 31 '26	Feb 15 '27	0 days	Yes																
392	392	1.5.5.2.5.2.1	Feeding hopper	40 days	Dec 31 '26	Feb 15 '27	0 days	Yes																
393	393	1.5.5.2.5.2.2	Shredder (Pre-Shredder)	40 days	Dec 31 '26	Feb 15 '27	0 days	Yes																
394	394	1.5.5.2.5.2.3	Conveyor Equipment	40 days	Dec 31 '26	Feb 15 '27	0 days	Yes																
395	395	1.5.5.2.5.2.3	Chain Conveyor	40 days	Dec 31 '26	Feb 15 '27	0 days	Yes																
396	396	1.5.5.2.5.2.3	Belt Conveyor (Transfer conveyor)	40 days	Dec 31 '26	Feb 15 '27	0 days	Yes																
397	397	1.5.5.2.5.2.4	Magnetic Separator	40 days	Dec 31 '26	Feb 15 '27	0 days	Yes																
398	398	1.5.5.2.5.2.5	Trommel Screen	40 days	Dec 31 '26	Feb 15 '27	0 days	Yes																
399	399	1.5.5.2.5.2.6	Fully Automatic Hydraulic Baler	40 days	Dec 31 '26	Feb 15 '27	0 days	Yes																
400	400	1.5.5.2.5.2.7	Air Treatment System	40 days	Dec 31 '26	Feb 15 '27	0 days	Yes																
401	401	1.5.5.2.5.2.8	Electrical Control System	40 days	Dec 31 '26	Feb 15 '27	0 days	Yes																
402	402	1.5.5.3	SRF Auxiliary building	62 days	Nov 25 '26	Feb 4 '27	17 days	No																
403	403	1.5.5.3.1	Truck Weighing Scale & Control Building	19 days	Dec 30 '26	Jan 20 '27	30 days	No																
404	404	1.5.5.3.1.1	Service Water Distribution System	10 days	Jan 9 '27	Jan 20 '27	30 days	No																
405	405	1.5.5.3.1.2	Waste Water Treatment System	10 days	Jan 9 '27	Jan 20 '27	30 days	No																
406	406	1.5.5.3.1.3	Fire Protection, Detection and Fire Fighting	10 days	Jan 1 '27	Jan 12 '27	37 days	No																
407	407	1.5.5.3.1.4	Ventilation and air conditioning system equipment	10 days	Dec 30 '26	Jan 9 '27	39 days	No																
408	408	1.5.5.3.2	Fire Water Pump Shelter	19 days	Dec 30 '26	Jan 20 '27	22 days	No																
409	409	1.5.5.3.2.1	Service Water Distribution System	10 days	Jan 9 '27	Jan 20 '27	30 days	No																
410	410	1.5.5.3.2.2	Waste Water Treatment System	10 days	Jan 9 '27	Jan 20 '27	30 days	No																
411	411	1.5.5.3.2.3	Fire Protection, Detection and Fire Fighting	10 days	Jan 1 '27	Jan 12 '27	20 days	No																
412	412	1.5.5.3.2.4	Ventilation and air conditioning system equipment	10 days	Dec 30 '26	Jan 9 '27	39 days	No																
413	413	1.5.5.3.3	Service Water and Fire Water Storage Tank (Field-Erection)	30 days	Nov 25 '26	Dec 29 '26	32 days	No																
414	414	1.5.5.3.4	Diesel Tank Installation	30 days	Jan 1 '27	Feb 4 '27	17 days	No																
415	415	1.5.5.4	SRF Other building	30 days	Dec 30 '26	Feb 2 '27	21 days	No																
416	416	1.5.5.4.1	Administration Building	24 days	Dec 30 '26	Jan 26 '27	27 days	No																
417	417	1.5.5.4.1.1	Service Water Distribution System	15 days	Jan 9 '27	Jan 26 '27	27 days	No																
418	418	1.5.5.4.1.2	Waste Water Treatment System	15 days	Jan 9 '27	Jan 26 '27	27 days	No																
419	419	1.5.5.4.1.3	Fire Protection, Detection and Fire Fighting	15 days	Jan 1 '27	Jan 18 '27	34 days	No																
420	420	1.5.5.4.1.4	Ventilation and air conditioning system equipment	15 days	Dec 30 '26	Jan 15 '27	36 days	No																
421	421	1.5.5.4.2	Warehouse & Maintenance Workshop Building	15 days	Jan 16 '27	Feb 2 '27	21 days	No																
422	422	1.5.5.4.2.1	Service Water Distribution System	15 days	Jan 16 '27	Feb 2 '27	21 days	No																
423	423	1.5.5.4.2.2	Waste Water Treatment System	15 days	Jan 16 '27	Feb 2 '27	21 days	No																
424	424	1.5.5.4.2.3	Fire Protection, Detection and Fire Fighting	15 days	Jan 16 '27	Feb 2 '27	21 days	No																
Project: SOLID RECOVERED FUEL Date: 25th June 2026 Revision: D (Owner)			Baseline Milestone Baseline Summary Critical Task Progress Task Split Task Progress Manual Task Manual Split Manual Progress Start Time only Finish Time only Schedule only Critical Critical Split Baseline Baseline Split Milestone Manual Milestone Abstract Task Progress Abstract Manual Abstract Project Abstract Abstract Grouping																					
Page 8 of 10																								

Project Master Schedule																											
ID	ID	WBS	Task Name	Duration	Start Time	Finish Time	Total Slack	Critical	6	Mar	Qtr 2, 2026			Qtr 3, 2026			Qtr 4, 2026			Qtr 1, 2027			Q				
											Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr				
425	425	1.5.5.4.2.4	Ventilation and air conditioning system equipment	15 days	Jan 16 '27	Feb 2 '27	21 days	No																			
426	426	1.5.5.4.3	Guard House	19 days	Dec 30 '26	Jan 20 '27	32 days	No																			
427	427	1.5.5.4.3.1	Service Water Distribution System	10 days	Jan 9 '27	Jan 20 '27	32 days	No																			
428	428	1.5.5.4.3.2	Wastewater System	10 days	Jan 9 '27	Jan 20 '27	32 days	No																			
429	429	1.5.5.4.3.3	Fire Protection, Detection and Fire Fighting	10 days	Jan 1 '27	Jan 12 '27	39 days	No																			
430	430	1.5.5.4.3.4	Ventilation and air conditioning system equipment	10 days	Dec 30 '26	Jan 9 '27	41 days	No																			
431	431	1.5.6	Electrical system	93 days	Oct 17 '26	Feb 2 '27	16 days	No																			
432	432	1.5.6.1	SRF Main Building	92 days	Oct 17 '26	Feb 1 '27	0 days	Yes																			
433	433	1.5.6.1.1	Outside Building	79 days	Oct 17 '26	Jan 16 '27	13 days	No																			
434	434	1.5.6.1.1.1	Electrical Equipment Installation (AC Distribution Board)	5 days	Dec 31 '26	Jan 5 '27	13 days	No																			
435	435	1.5.6.1.1.2	Grounding and Lightning System Installation	10 days	Oct 17 '26	Oct 28 '26	82 days	No																			
436	436	1.5.6.1.1.3	Cable and Raceway System	10 days	Jan 6 '27	Jan 16 '27	13 days	No																			
437	437	1.5.6.1.1.4	Electrical Lighting installation	15 days	Dec 31 '26	Jan 16 '27	13 days	No																			
438	438	1.5.6.1.1.5	Fire Alarm System installation	15 days	Dec 31 '26	Jan 16 '27	13 days	No																			
439	439	1.5.6.1.1.6	Communication System	15 days	Dec 31 '26	Jan 16 '27	13 days	No																			
440	440	1.5.6.1.2	Main Building	20 days	Jan 9 '27	Feb 1 '27	0 days	Yes																			
441	441	1.5.6.1.2.1	Grounding and Lightning System Installation	20 days	Jan 9 '27	Feb 1 '27	0 days	Yes																			
442	442	1.5.6.1.2.2	Cable and Raceway System	20 days	Jan 9 '27	Feb 1 '27	0 days	Yes																			
443	443	1.5.6.1.2.3	Lighting System and Small Power	20 days	Jan 9 '27	Feb 1 '27	0 days	Yes																			
444	444	1.5.6.1.2.4	Fire Alarm System	20 days	Jan 9 '27	Feb 1 '27	0 days	Yes																			
445	445	1.5.6.1.2.5	Communication System	20 days	Jan 9 '27	Feb 1 '27	0 days	Yes																			
446	446	1.5.6.2	SRF Auxiliary building	43 days	Nov 23 '26	Jan 11 '27	33 days	No																			
447	447	1.5.6.2.1	Truck Weighing Scale & Control Building	31 days	Dec 7 '26	Jan 11 '27	33 days	No																			
448	448	1.5.6.2.1.1	Grounding and Lightning System Installation	10 days	Dec 7 '26	Dec 17 '26	54 days	No																			
449	449	1.5.6.2.1.2	Cable and Raceway System	10 days	Dec 31 '26	Jan 11 '27	33 days	No																			
450	450	1.5.6.2.1.3	Lighting System and Small Power	10 days	Dec 31 '26	Jan 11 '27	33 days	No																			
451	451	1.5.6.2.1.4	Fire Alarm System	10 days	Dec 31 '26	Jan 11 '27	33 days	No																			
452	452	1.5.6.2.1.5	Communication System	10 days	Dec 31 '26	Jan 11 '27	33 days	No																			
453	453	1.5.6.2.2	Fire Water Pump Shelter	43 days	Nov 23 '26	Jan 11 '27	33 days	No																			
454	454	1.5.6.2.2.1	Grounding and Lightning System Installation	10 days	Nov 23 '26	Dec 3 '26	66 days	No																			
455	455	1.5.6.2.2.2	Cable and Raceway System	10 days	Dec 31 '26	Jan 11 '27	33 days	No																			
456	456	1.5.6.2.2.3	Lighting System and Small Power	10 days	Dec 31 '26	Jan 11 '27	33 days	No																			
457	457	1.5.6.2.2.4	Fire Alarm System	10 days	Dec 31 '26	Jan 11 '27	33 days	No																			
458	458	1.5.6.2.2.5	Communication System	10 days	Dec 31 '26	Jan 11 '27	33 days	No																			
459	459	1.5.6.2.3	Transformer Installation	5 days	Dec 31 '26	Jan 5 '27	13 days	No																			
460	460	1.5.6.3	SRF Other building	74 days	Nov 9 '26	Feb 2 '27	16 days	No																			
461	461	1.5.6.3.1	Administration Building	39 days	Dec 9 '26	Jan 22 '27	25 days	No																			
462	462	1.5.6.3.1.1	Grounding and Lightning System Installation	20 days	Dec 9 '26	Dec 31 '26	44 days	No																			
463	463	1.5.6.3.1.2	Cable and Raceway System	20 days	Dec 31 '26	Jan 22 '27	25 days	No																			
464	464	1.5.6.3.1.3	Lighting System and Small Power	20 days	Dec 31 '26	Jan 22 '27	25 days	No																			
465	465	1.5.6.3.1.4	Fire Alarm System	20 days	Dec 31 '26	Jan 22 '27	25 days	No																			
466	466	1.5.6.3.1.5	Communication System	20 days	Dec 31 '26	Jan 22 '27	25 days	No																			
467	467	1.5.6.3.2	Warehouse & Maintenance Workshop Building	20 days	Jan 11 '27	Feb 2 '27	16 days	No																			
468	468	1.5.6.3.2.1	Grounding and Lightning System Installation	20 days	Jan 11 '27	Feb 2 '27	16 days	No																			
469	469	1.5.6.3.2.2	Cable and Raceway System	20 days	Jan 11 '27	Feb 2 '27	16 days	No																			
470	470	1.5.6.3.2.3	Lighting System and Small Power	20 days	Jan 11 '27	Feb 2 '27	16 days	No																			
471	471	1.5.6.3.2.4	Fire Alarm System	20 days	Jan 11 '27	Feb 2 '27	16 days	No																			
472	472	1.5.6.3.2.5	Communication System	20 days	Jan 11 '27	Feb 2 '27	16 days	No																			
473	473	1.5.6.3.3	Guard House	65 days	Nov 9 '26	Jan 22 '27	25 days	No																			
474	474	1.5.6.3.3.1	Grounding and Lightning System Installation	20 days	Nov 9 '26	Dec 1 '26	70 days	No																			
475	475	1.5.6.3.3.2	Cable and Raceway System	20 days	Dec 31 '26	Jan 22 '27	25 days	No																			
476	476	1.5.6.3.3.3	Lighting System and Small Power	20 days	Dec 31 '26	Jan 22 '27	25 days	No																			
477	477	1.5.6.3.3.4	Fire Alarm System	20 days	Dec 31 '26	Jan 22 '27	25 days	No																			
Project: SOLID RECOVERED FUEL Date: 25th June 2026 Revision: D (Owner)			Baseline Milestone Baseline Summary Critical Task Progress Task Split Task Progress Manual Task Manual Split Manual Progress Start Time only Finish Time only Schedule only Critical Critical Split Baseline Baseline Split Milestone Manual Milestone Abstract Task Progress Abstract Manual Abstract Project Abstract Abstract Grouping																								
Page 9 of 10																											

Project Master Schedule																								
ID	ID	WBS	Task Name	Duration	Start Time	Finish Time	Total Slack	Critic	6	Qtr 2, 2026				Qtr 3, 2026			Qtr 4, 2026			Qtr 1, 2027				Q
										Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	Q
478	478	1.5.6.3.3.5	Communication System	20 days	Dec 31 '26	Jan 22 '27	25 days	No																
479	479	1.5.7	C&I	20 days	Jan 8 '27	Jan 30 '27	1 day	No																
480	480	1.6	Functional Testing and commissioning	37 days	Jan 21 '27	Mar 4 '27	0 days	Yes																
481	481	1.6.1	Firefighting system commissioning	7 days	Feb 2 '27	Feb 9 '27	3 days	No																
482	482	1.6.2	Electric and I&C	27 days	Jan 21 '27	Feb 20 '27	0 days	Yes																
483	483	1.6.2.1	SRF Main Building	20 days	Jan 21 '27	Feb 12 '27	0 days	Yes																
484	484	1.6.2.2	Grid power energization	2 days	Feb 13 '27	Feb 15 '27	0 days	Yes																
485	485	1.6.2.3	SRF Auxiliary building	5 days	Feb 16 '27	Feb 20 '27	3 days	No																
486	486	1.6.2.4	SRF Other building	5 days	Feb 16 '27	Feb 20 '27	5 days	No																
487	487	1.6.3	Mechanical (Incl. All System and Entire Plant Intelocking Test)	15 days	Feb 16 '27	Mar 4 '27	0 days	Yes																
488	488	1.6.3.1	SRF Main Building	15 days	Feb 16 '27	Mar 4 '27	0 days	Yes																
489	489	1.6.3.2	SRF Auxiliary building	7 days	Feb 22 '27	Mar 1 '27	3 days	No																
490	490	1.6.3.3	SRF Other building	5 days	Feb 22 '27	Feb 26 '27	5 days	No																
491	491	1.7	Commercial Operation Date (COD)	22 days	Mar 5 '27	Mar 30 '27	0 days	Yes																
492	492	1.7.1	Plant Tests	3 days	Mar 5 '27	Mar 8 '27	0 days	Yes																
493	493	1.7.2	Plant Emission Tests	3 days	Mar 9 '27	Mar 11 '27	0 days	Yes																
494	494	1.7.3	COD Application	16 days	Mar 12 '27	Mar 30 '27	0 days	Yes																
495	495	1.7.4	COD	0 days	Mar 30 '27	Mar 30 '27	0 days	Yes																
496	496	1.8	Provisional Acceptance Date (PAD)	61 days	Mar 31 '27	May 30 '27	0 days	Yes																
497	497	1.8.1	Reliability Guarantee Test	15 days	Mar 31 '27	Apr 14 '27	0 days	Yes																
498	498	1.8.2	Absolute Guarantee test	15 days	Apr 15 '27	Apr 29 '27	0 days	Yes																
499	499	1.8.3	PAD Application	31 days	Apr 30 '27	May 30 '27	0 days	Yes																
500	500	1.8.4	PAD	0 days	May 30 '27	May 30 '27	0 days	Yes																



Project: SOLID RECOVERED FUEL

Date: 25th June 2026

Revision: D (Owner)

Baseline Milestone

Baseline Summary

Critical Task Progress

Task

Split

Task Progress

Manual Task

Manual Split

Manual Progress

Start Time only

Finish Time only

Schedule only

Critical

Critical Split

Baseline

Baseline Split

Milestone

Manual Milestone

Abstract Task Progress

Abstract

Manual Abstract

Project Abstract

Abstract Grouping

Page 10 of 10
