

FOR APPROVAL

OWNER NAME



The Prao Power Co., Ltd.

OWNER'S ENGINEER NAME



Electricity Generating Authority of Thailand



Triangle Engineers (Thailand) Co., Ltd.

CONTRACTOR NAME



中国电力工程顾问集团有限公司
CHINA POWER ENGINEERING CONSULTING GROUP CO., LTD.


Doc No.

TPP-001-G-150-000-001

Document Name

Overall Project Schedule_Level 2

REV	REV Date	REV STA	DESD	CHKD	ARPD	Description
A	13 January 2026	FA	Lian Xiaoqing	Zhao Zeqing	Ding Xiangcheng	
B	03 May 2026	FA	Wang Meiqiang	Zhao Zeqing	Ding Xiangcheng	

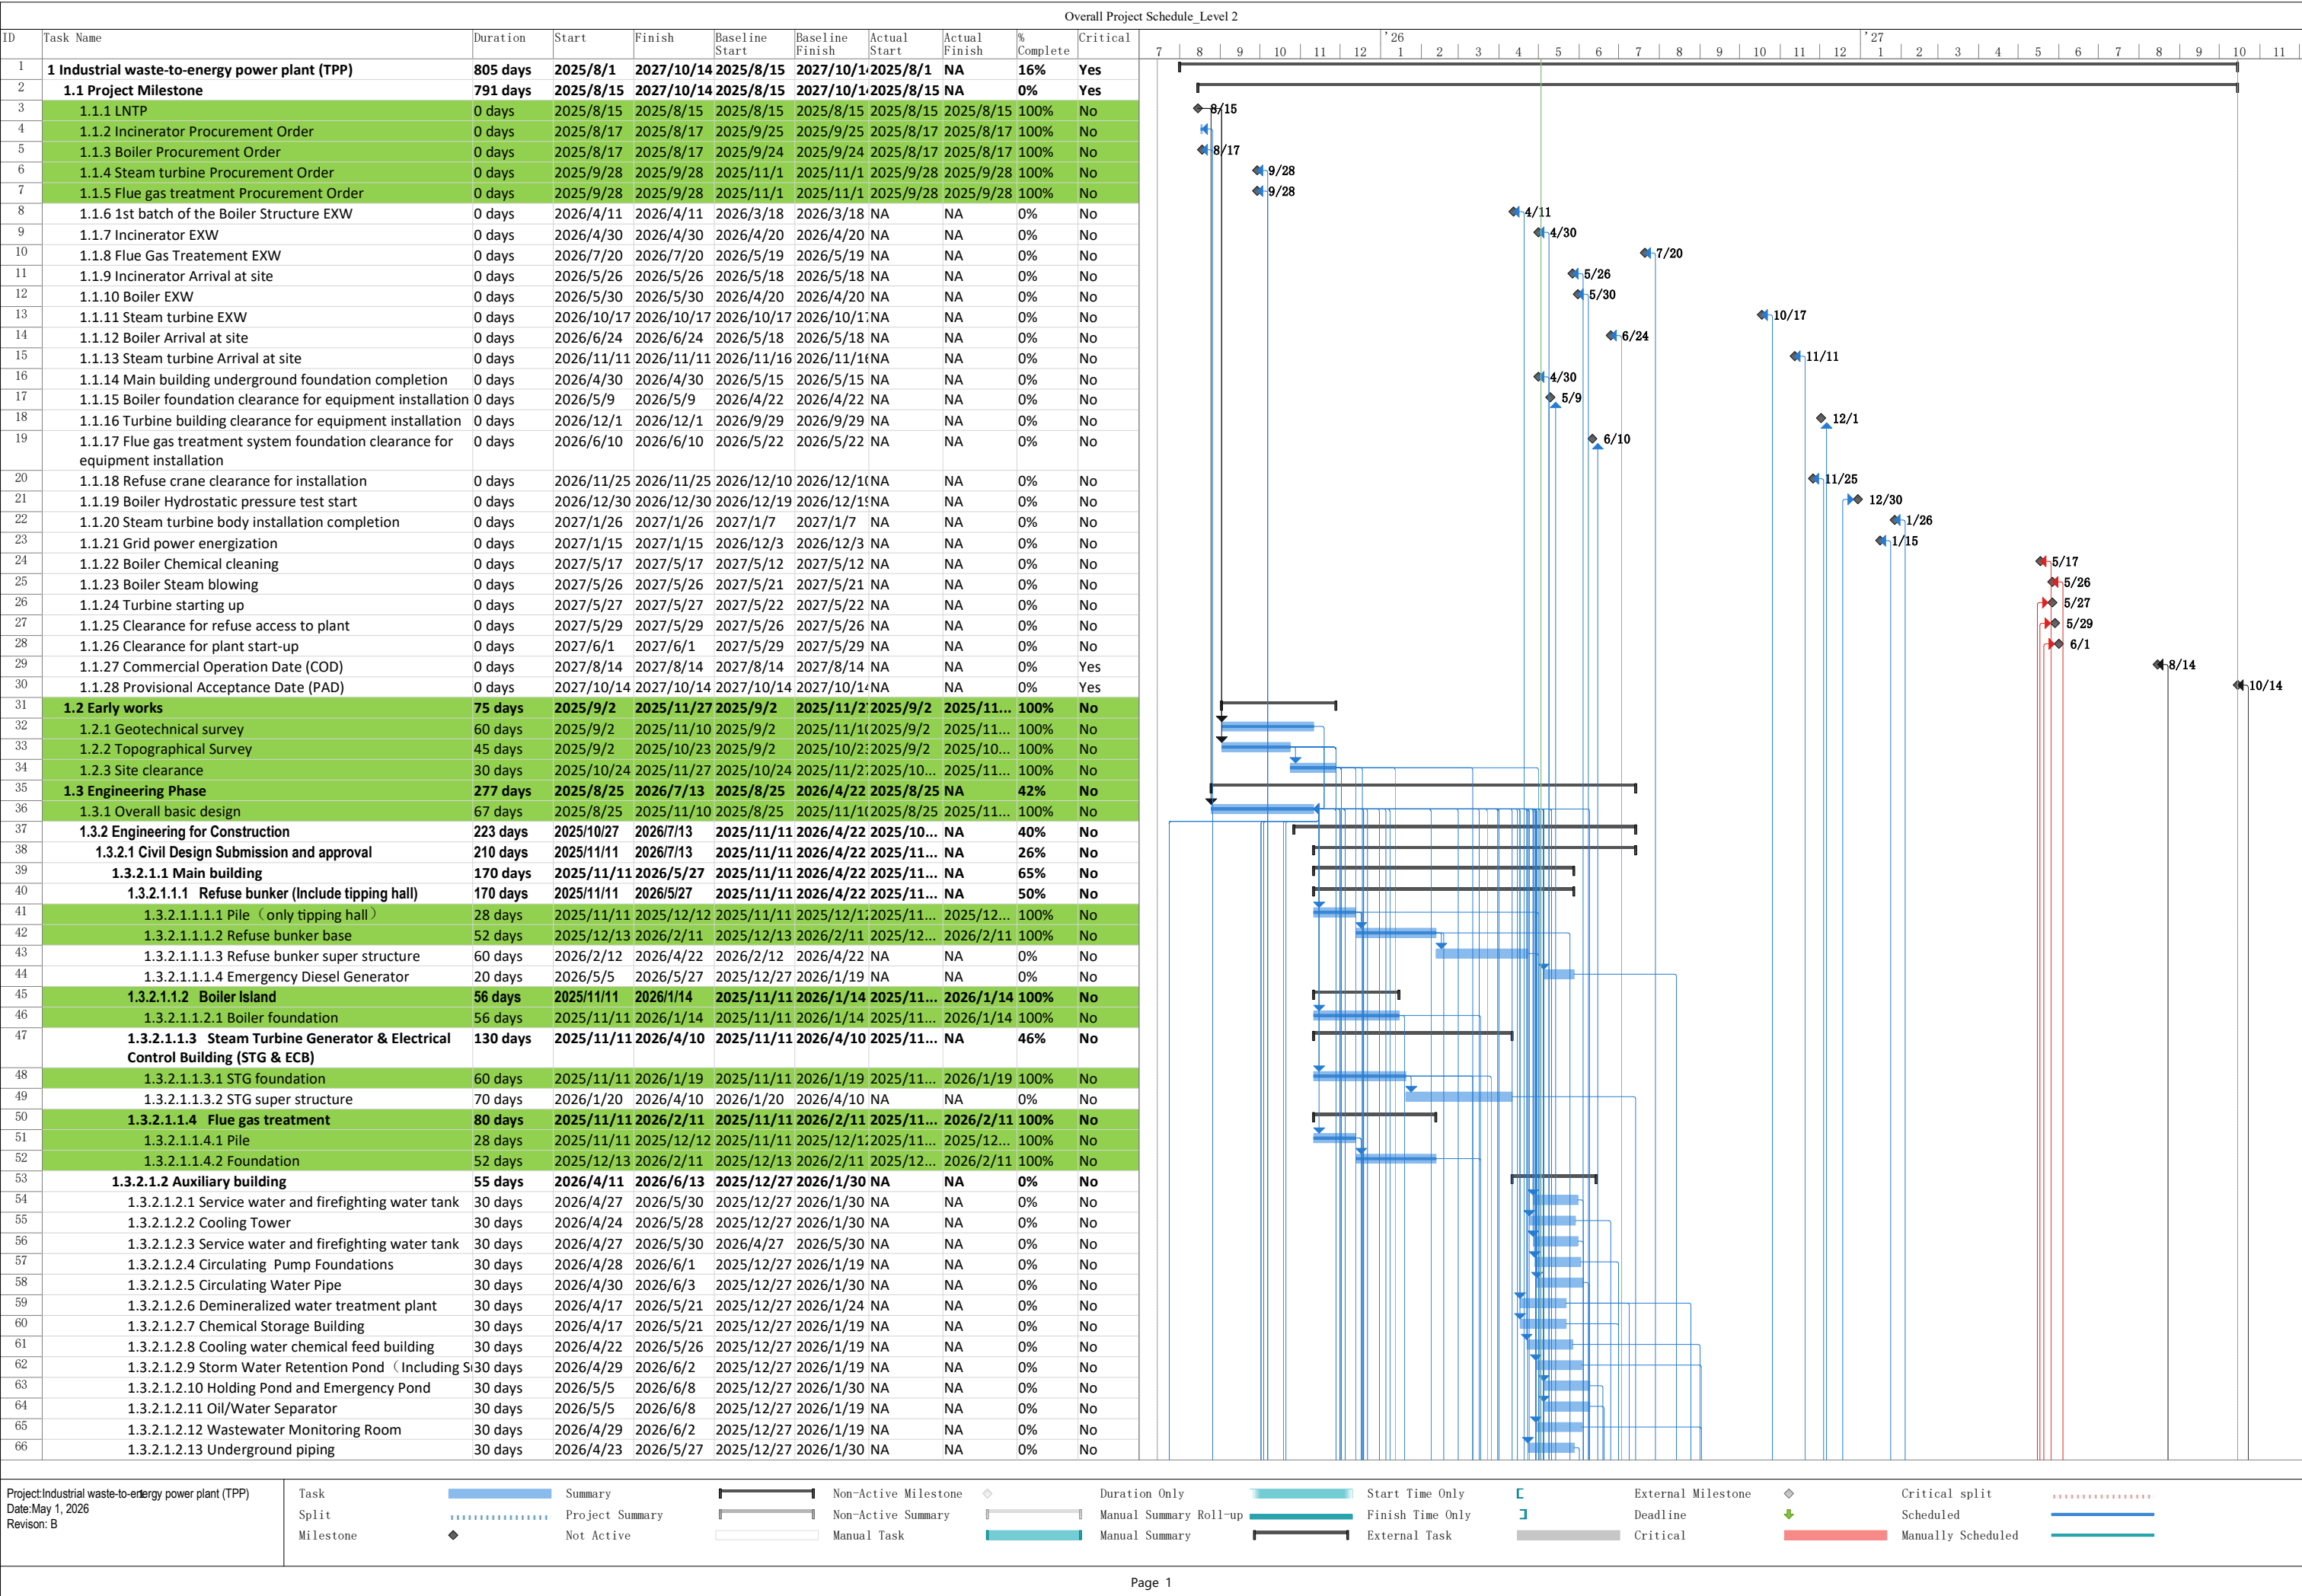

Overall Project Schedule_Level 2																																										
ID	Task Name	Duration	Start	Finish	Baseline Start	Baseline Finish	Actual Start	Actual Finish	% Complete	Critical	7	8	9	10	11	12	'26	1	2	3	4	5	6	7	8	9	10	11	12	'27	1	2	3	4	5	6	7	8	9	10	11	
67	1.3.2.1.2.14 Fire water pump shelter	30 days	2026/4/29	2026/6/2	2025/12/27	2026/1/19	NA	NA	0%	No																																
68	1.3.2.1.2.15 Chimney foundation	30 days	2026/5/5	2026/6/8	2025/12/27	2026/1/30	NA	NA	0%	No																																
69	1.3.2.1.2.16 CEMS control room	30 days	2026/5/11	2026/6/13	2025/12/27	2026/1/30	NA	NA	0%	No																																
70	1.3.2.1.2.17 Diesel oil tank and diesel oil pump founda	30 days	2026/4/29	2026/6/2	2025/12/27	2026/1/19	NA	NA	0%	No																																
71	1.3.2.1.2.18 Unit Auxiliary Transformer and Step-up Transformer Foundation	30 days	2026/5/11	2026/6/13	2025/12/27	2026/1/19	NA	NA	0%	No																																
72	1.3.2.1.2.19 Emergency Diesel Generator	30 days	2026/5/2	2026/6/5	2025/12/27	2026/1/19	NA	NA	0%	No																																
73	1.3.2.1.2.20 Final Inspection pit	30 days	2026/4/24	2026/5/28	2025/12/27	2026/1/19	NA	NA	0%	No																																
74	1.3.2.1.2.21 Bottom Ash Conveyer	20 days	2026/4/11	2026/5/4	2025/12/27	2026/1/19	NA	NA	0%	No																																
75	1.3.2.1.2.22 Fly Ash Silo	30 days	2026/5/5	2026/6/8	2025/12/27	2026/1/19	NA	NA	0%	No																																
76	1.3.2.1.3 Orther building	160 days	2026/1/8	2026/7/13	2026/1/8	2026/2/17	2026/1/8	NA	27%	No																																
77	1.3.2.1.3.1 Administration building	35 days	2026/5/5	2026/6/13	2026/1/8	2026/2/17	NA	NA	0%	No																																
78	1.3.2.1.3.2 Warehouse and Maintenance Workshop(V	30 days	2026/4/29	2026/6/2	2026/1/8	2026/2/11	NA	NA	0%	No																																
79	1.3.2.1.3.3 Truck Weighing Scale & Control Building	20 days	2026/5/5	2026/5/27	2026/1/8	2026/1/30	NA	NA	0%	No																																
80	1.3.2.1.3.4 Guard House	20 days	2026/4/23	2026/5/15	2026/1/8	2026/1/30	NA	NA	0%	No																																
81	1.3.2.1.3.5 Plant internal road	30 days	2026/1/8	2026/2/11	2026/1/8	2026/2/11	2026/1/8	2026/2/11	100%	No																																
82	1.3.2.1.3.6 Plant Virescence	30 days	2026/6/9	2026/7/13	2026/1/8	2026/2/11	NA	NA	0%	No																																
83	1.3.2.1.3.7 Site Grading (Backfilling)	30 days	2026/1/8	2026/2/11	2026/1/8	2026/2/11	2026/1/8	2026/2/11	100%	No																																
84	1.3.2.1.3.8 Parking area	30 days	2026/5/5	2026/6/8	2026/1/8	2026/2/11	NA	NA	0%	No																																
85	1.3.2.2 Mechanical Design Submission and approval	84 days	2026/5/18	2026/5/18	2026/2/16	2026/2/23	2026/2/10	NA	0%	No																																
86	1.3.2.2.1 Boiler Auxiliary system	60 days	2026/2/10	2026/4/20	2025/12/16	2026/2/23	2026/2/10	NA	0%	No																																
87	1.3.2.2.1.1 Primary fan system (Including Motor System	60 days	2026/2/10	2026/4/20	2025/12/16	2026/2/23	2026/2/10	NA	0%	No																																
88	1.3.2.2.1.2 Secondary draft fan system (Including Motor Sys	60 days	2026/2/10	2026/4/20	2025/12/16	2026/2/23	2026/2/10	NA	0%	No																																
89	1.3.2.2.1.3 Induced Draft fan system (Including Motor	60 days	2026/2/10	2026/4/20	2025/12/16	2026/2/23	2026/2/10	NA	0%	No																																
90	1.3.2.2.1.4 Flue gas system	60 days	2026/2/10	2026/4/20	2025/12/16	2026/2/23	2026/2/10	NA	0%	No																																
91	1.3.2.2.1.5 Flue gas recirculation fan system installatio	60 days	2026/2/10	2026/4/20	2025/12/16	2026/2/23	2026/2/10	NA	0%	No																																
92	1.3.2.2.1.6 Furnace cooling fan system (Including Mot	60 days	2026/2/10	2026/4/20	2025/12/16	2026/2/23	2026/2/10	NA	0%	No																																
93	1.3.2.2.2 Steam turbine Auxiliary system	84 days	2026/2/10	2026/5/18	2025/12/16	2026/2/23	2026/2/10	NA	0%	No																																
94	1.3.2.2.2.1 Vacuum pumping system	60 days	2026/2/20	2026/4/30	2025/12/16	2026/2/23	2026/2/20	NA	0%	No																																

Overall Project Schedule_Level 2																																								
ID	Task Name	Duration	Start	Finish	Baseline Start	Baseline Finish	Actual Start	Actual Finish	% Complete	Critical	7	8	9	10	11	12	'26 1	2	3	4	5	6	7	8	9	10	11	12	'27 1	2	3	4	5	6	7	8	9	10	11	
133	1.4.1.7 Compressed air system	135 days	2025/10/10	2026/3/16	2025/11/11	2026/1/19	2025/10...	2026/3/16	100%	No																														
134	1.4.1.8 Boiler Auxiliary system	6 days	2025/12/7	2025/12/14	2026/2/24	2026/3/12	2025/12/7	2025/12...	100%	No																														
135	1.4.1.8.1 Primary fan (Including Motor System)	6 days	2025/12/7	2025/12/14	2026/2/24	2026/3/12	2025/12/7	2025/12...	100%	No																														
136	1.4.1.8.2 Secondary fan (Including Motor System)	6 days	2025/12/7	2025/12/14	2026/2/24	2026/3/12	2025/12/7	2025/12...	100%	No																														
137	1.4.1.8.3 Induced Draft fan (Including Motor System)	6 days	2025/12/7	2025/12/14	2026/2/24	2026/3/12	2025/12/7	2025/12...	100%	No																														
138	1.4.1.8.4 Flue gas recirculation fan (Including Motor Syst	6 days	2025/12/7	2025/12/14	2026/2/24	2026/3/12	2025/12/7	2025/12...	100%	No																														
139	1.4.1.8.5 Furnace cooling fan system (Including Motor S	6 days	2025/12/7	2025/12/14	2026/2/24	2026/3/12	2025/12/7	2025/12...	100%	No																														
140	1.4.1.9 STG Auxiliary Systems	36 days	2025/12/14	2026/1/25	2026/2/24	2026/3/24	2025/12...	2026/1/25	100%	No																														
141	1.4.1.10 Electric system	138 days	2025/12/22	2026/5/30	2026/1/22	2026/3/27	2025/12...	NA	14%	No																														
142	1.4.1.10.1 Step-up Transformer	52 days	2026/1/11	2026/3/12	2026/2/4	2026/2/20	2026/1/11	2026/3/12	100%	No																														
143	1.4.1.10.2 Generator outlet cabinet	31 days	2026/3/11	2026/4/15	2026/2/5	2026/3/5	NA	NA	0%	No																														
144	1.4.1.10.3 22 kV switchgear and distribution system	28 days	2026/3/14	2026/4/15	2026/2/5	2026/3/5	NA	NA	0%	No																														
145	1.4.1.10.4 11kV Switchgear	28 days	2026/3/14	2026/4/15	2026/2/5	2026/3/5	NA	NA	0%	No																														
146	1.4.1.10.5 11kV VFD	29 days	2026/3/13	2026/4/15	2026/2/6	2026/3/12	NA	NA	0%	No																														
147	1.4.1.10.6 Auxiliary transformer	41 days	2026/3/14	2026/4/30	2026/2/5	2026/2/21	NA	NA	0%	No																														
148	1.4.1.10.7 Emergency Diesel Generator	26 days	2026/3/17	2026/4/15	2026/2/19	2026/3/25	NA	NA</																																

Overall Project Schedule_Level 2																																									
ID	Task Name	Duration	Start	Finish	Baseline Start	Baseline Finish	Actual Start	Actual Finish	% Complete	Critical	7	8	9	10	11	12	'26	1	2	3	4	5	6	7	8	9	10	11	12	'27	1	2	3	4	5	6	7	8	9	10	11
200	1.4.3.14.11 LV Switchgear/Distribution board	105 days	2026/5/1	2026/8/31	2026/3/19	2026/8/5	NA	NA	0%	No																															
201	1.4.3.14.12 Cable and raceway system (EE)	105 days	2026/6/1	2026/9/30	2026/3/28	2026/8/14	NA	NA	0%	No																															
202	1.4.3.14.13 Grounding and Lightning Protection System	180 days	2026/1/5	2026/8/1	2026/3/5	2026/7/22	NA	NA	0%	No																															
203	1.4.3.14.14 Lighting and Small Power	150 days	2026/1/12	2026/7/4	2026/2/20	2026/7/9	NA	NA	0%	No																															
204	1.4.3.14.15 Communication system (telephone, paging, intercom)	115 days	2026/6/1	2026/10/12	2026/3/19	2026/7/13	NA	NA	0%	No																															
205	1.4.3.15 C&I system	175 days	2026/4/11	2026/10/31	2026/3/25	2026/8/17	NA	NA	0%	No																															
206	1.4.3.15.1 DCS (Include Boiler Control System)	175 days	2026/4/11	2026/10/31	2026/3/31	2026/8/17	NA	NA	0%	No																															
207	1.4.3.15.2 CEMS	144 days	2026/4/11	2026/9/25	2026/3/25	2026/8/11	NA	NA	0%	No																															
208	1.4.3.15.3 CCTV system	105 days	2026/6/1	2026/9/30	2026/3/25	2026/6/25	NA	NA	0%	No																															
209	1.4.3.15.4 Fire Alarm and detection system	105 days	2026/6/1	2026/9/30	2026/3/31	2026/5/4	NA	NA	0%	No																															
210	1.4.3.15.5 Instrument and Analyzer	105 days	2026/6/1	2026/9/30	2026/3/31	2026/7/13	NA	NA	0%	No																															
211	1.4.3.15.6 Instrument Enclosure,Rack and Stanchion	105 days	2026/6/1	2026/9/30	2026/3/31	2026/7/13	NA	NA	0%	No																															
212	1.4.3.15.7 Cable and raceway system (C&I)	105 days	2026/5/16	2026/9/15	2026/3/28	2026/8/14	NA	NA	0%	No																															
213	1.4.4 Shipment	254 days	2026/1/11	2026/11/3	2026/1/13	2026/11/7	2026/1/11	NA	4%	No																															
214	1.4.4.1 Incinerator equipment (Include Boiler Control System)	15 days		2026/5/18	2026/4/21	2026/5/9	NA	NA	0%	No																															

Overall Project Schedule_Level 2																																									
ID	Task Name	Duration	Start	Finish	Baseline Start	Baseline Finish	Actual Start	Actual Finish	% Complete	Critical	7	8	9	10	11	12	' 26	1	2	3	4	5	6	7	8	9	10	11	12	' 27	1	2	3	4	5	6	7	8	9	10	11
266	1.4.5.14.4 11kV Switchgear	10 days	2026/10/1	2026/10/12	2026/8/17	2026/8/27	NA	NA	0%	No																															
267	1.4.5.14.5 11kV VFD	10 days	2026/9/26	2026/10/7	2026/8/24	2026/9/3	NA	NA	0%	No																															
268	1.4.5.14.6 Auxiliary transformer	10 days	2026/9/30	2026/10/10	2026/8/28	2026/9/8	NA	NA	0%	No																															
269	1.4.5.14.7 Emergency Diesel Generator	10 days	2026/9/5	2026/9/16	2026/8/1	2026/8/12	NA	NA	0%	No																															
270	1.4.5.14.8 Batteries/DC/UPS	7 days	2026/10/12	2026/10/19	2026/7/31	2026/8/7	NA	NA	0%	No																															
271	1.4.5.14.9 Relay and protection panel	10 days	2026/9/28	2026/10/8	2026/8/25	2026/9/4	NA	NA	0%	No																															
272	1.4.5.14.10 Revenue meter and synchronization	10 days	2026/10/7	2026/10/17	2026/8/29	2026/9/9	NA	NA	0%	No																															
273	1.4.5.14.11 LV Switchgear/Distribution board	10 days	2026/9/24	2026/10/5	2026/8/29	2026/9/9	NA	NA	0%	No																															
274	1.4.5.14.12 Cable and raceway system (EE)	10 days	2026/10/19	2026/10/29	2026/9/2	2026/9/12	NA	NA	0%	No																															
275	1.4.5.14.13 Grounding and Lightning Protection System	10 days	2026/8/3	2026/8/13	2026/7/23	2026/8/3	NA	NA	0%	No																															
276	1.4.5.14.14 Lighting and Small Power	10 days	2026/7/6	2026/7/16	2026/7/10	2026/7/21	NA	NA	0%	No																															
277	1.4.5.14.15 Communication system (telephone, paging, i	10 days	2026/10/13	2026/10/23	2026/7/14	2026/7/24	NA	NA	0%	No																															
278	1.4.5.15 C&I	46 days	2026/9/26	2026/11/18	2026/5/5	2026/9/12	NA	NA	0%	No																															
279	1.4.5.15.1 DCS (Include Boiler Control System)	15 days	2026/11/2	2026/11/18	2026/8/18	2026/9/3	NA	NA	0%	No																															
280	1.4.5.15.2 CCTV system	10 days	2026/10/30	2026/11/10	2026/7/25	2026/8/5	NA	NA	0%	No																															
281	1.4.5.15.3 Fire Alarm and detection system	5 days	2026/10/1	2026/10/6	2026/5/5	2026/5/9	NA	NA	0%	No																															
282	1.4.5.15.4 CEMS	20 days	2026/9/26	2026/10/19	2026/8/12	2026/9/3	NA	NA	0%	No																															
283	1.4.5.15.5 Instrument and Analyzer	20 days	2026/10/19	2026/11/10	2026/7/31	2026/8/22	NA	NA	0%	No																															
284	1.4.5.15.6 Instrument Enclosure,Rack and Stanchion	20 days	2026/10/19	2026/11/10	2026/7/31	2026/8/22	NA	NA	0%	No																															
285	1.4.5.15.7 Cable and raceway system (C&I)	10 days	2026/10/19	2026/10/29	2026/9/2	2026/9/12	NA	NA	0%	No																															
286	1.5 Construction	520 days	2025/10/10	2027/6/8	2025/10/10	2027/4/16	2025/10...	NA	10%	No																															
287	1.5.1 Temporary Construction	73 days	2025/11/28	2026/2/20	2025/11/28	2026/2/20	2025/11...	2026/2/20	100%	No																															
288	1.5.1.1 Temporary site office	56 days	2025/11/28	2026/1/31	2025/11/28	2026/1/31	2025/11...	2026/1/31	100%	No																															
289	1.5.1.2 Temporary fence	30 days	2025/11/28	2026/1/1	2025/11/28	2026/1/1	2025/11...	2026/1/1	100%	No																															
290	1.5.1.3 Temporary rebar fabrication area	45 days	2025/11/28	2026/1/19	2025/11/28	2026/1/19	2025/11...	2026/1/19	100%	No																															
291	1.5.1.4 Temporary laydown area	45 days	2025/11/28	2026/1/19	2025/11/28	2026/1/19	2025/11...	2026/1/19	100%	No																															
292	1.5.1.5 Equipment pre-assembly area	30 days	2025/11/28	2026/1/1	2025/11/28	2026/1/1	2025/11...	2026/1/1	100%	No																															
293	1.5.1.6 Temporary internal road completion (Main worksh	73 days	2025/11/28	2026/2/20	2025/11/28	2026/2/20	2025/11...	2026/2/20	100%	No																															
294	1.5.1.7 Temporary internal road completion (Balance area)	60 days	2025/11/28	2026/2/5	2025/11/28	2026/2/5	2025/11...	2026/2/5	100%	No																															
295	1.5.2 Permit	253 days	2025/10/10	2026/7/31	2025/10/10	2026/6/30	2025/10...	NA	24%	No																															
296	1.5.2.1 Construction permit (Client to obtain) - Lot 1	60 days	2025/10/10	2025/12/18	2025/10/10	2025/12/18	2025/10...	2025/12...	100%	No																															
297	1.5.2.2 Construction permit (Client to obtain) - Lot 2	130 days	2025/12/19	2026/5/19	2025/12/19	2026/3/31	NA	NA	0%	No																															
298	1.5.2.3 Construction permit (Client to obtain) - Lot 3	63 days	2026/5/20	2026/7/31	2026/4/1	2026/6/30	NA	NA	0%	No																															
299	1.5.3 Civil work	465 days	2025/12/13	2027/6/8	2025/12/13	2027/4/1	2025/12...	NA	9%	No																															
300	1.5.3.1 Main building work	433 days	2025/12/13	2027/5/1	2025/12/13	2027/3/3	2025/12...	NA	19%	No																															
301	1.5.3.1.1 Testing Pile	114 days	2026/5/1	2026/9/10	2025/12/13	2026/1/27	NA	NA	0%	No																															
302	1.5.3.1.1.1 Piling Work-Testing Pile	100 days	2026/5/1	2026/8/25	2025/12/13	2025/12/3	NA	NA	0%	No																															
303	1.5.3.1.1.2 Pile Inspection-Testing Pile	14 days	2026/8/26	2026/9/10	2025/12/31	2026/1/27	NA	NA	0%	No																															
304	1.5.3.1.2 Refuse Bunker	324 days	2025/12/18	2026/12/30	2025/12/13	2027/1/14	2025/12...	NA	17%	No																															
305	1.5.3.1.2.1 Foundation Excavation- Refuse Bunker	54 days	2025/12/18	2026/2/18	2025/12/13	2026/1/24	2025/12...	2026/2/18	100%	No																															
306	1.5.3.1.2.2 Bottom basement casting- Refuse Bunker	25.6 days	2026/2/18	2026/3/22	2026/2/12	2026/3/2	2026/2/18	2026/3/22	100%	No																															
307	1.5.3.1.2.3 Foundation up to ground (Including the surrounding rooms、Underground grounding	34 days	2026/3/23	2026/4/30	2026/3/3	2026/5/15	2026/3/23	NA	90%	No																															
308	1.5.3.1.2.4 Super structure up to 7.65m elevation (Refuse feeder platform) (Including the surrounding	45 days	2026/5/1	2026/6/22	2026/5/16	2026/7/7	NA	NA	0%	No																															
309	1.5.3.1.2.5 Super structure up to 18m elevation (Refuse chute platform) (Including the surrounding	45 days	2026/6/23	2026/8/13	2026/7/8	2026/8/28	NA	NA	0%	No																															
310	1.5.3.1.2.6 Super structure up to 25.55m elevation (Refuse crane rail)- Refuse Bunker	35 days	2026/8/14	2026/9/23	2026/8/29	2026/10/8	NA	NA	0%	No																															
311	1.5.3.1.2.7 Completion of refuse bunker up to 35.55m elevation (Rooftop)- Refuse Bunker	45 days	2026/9/24	2026/11/14	2026/10/9	2026/11/3	NA	NA	0%	No																															

Overall Project Schedule_Level 2																																										
ID	Task Name	Duration	Start	Finish	Baseline Start	Baseline Finish	Actual Start	Actual Finish	% Complete	Critical																																
324	1.5.3.1.3.4 Super structure up to 13m- Tripping Hall	87 days	2026/7/3	2026/10/12	2026/5/16	2026/8/25	NA	NA	0%	No	7	8	9	10	11	12	'26	1	2	3	4	5	6	7	8	9	10	11	12	'27	1	2	3	4	5	6	7	8	9	10	11	
325	1.5.3.1.3.5 Rooftopping and balance work- Tripping Hall	26 days	2026/10/13	2026/11/11	2026/8/26	2026/9/24	NA	NA	0%	No																																
326	1.5.3.1.3.6 Architectures work- Tripping Hall	30 days	2026/10/8	2026/11/11	2026/8/21	2026/9/24	NA	NA	0%	No																																
327	1.5.3.1.4 Boiler Island	152 days	2026/1/12	2026/7/7	2026/1/15	2026/6/19	2026/1/12	NA	32%	No																																
328	1.5.3.1.4.1 Foundation Excavation- Boiler Island	58 days	2026/1/12	2026/3/19	2026/1/15	2026/1/30	2026/1/12	2026/3/19	100%	No																																
329	1.5.3.1.4.2 Boiler foundation - Boiler Island	40 days	2026/3/18	2026/5/4	2026/1/31	2026/3/30	2026/3/18	NA	88%	No																																
330	1.5.3.1.4.3 Clearance for boiler installation- Boiler Island	5 days	2026/5/5	2026/5/9	2026/3/31	2026/4/22	NA	NA	0%	No																																
331	1.5.3.1.4.4 Auxiliary Equipment Foundation (Boiler)	50 days	2026/5/11	2026/7/7	2026/4/23	2026/6/19	NA	NA	0%	No																																
332	1.5.3.1.4.4.1 Primary Air fan (PA) foundation upto clearance for equipment installation	30 days	2026/5/11	2026/6/13	2026/4/23	2026/5/27	NA	NA	0%	No																																
333	1.5.3.1.4.4.2 Secondary air fan (SA) foundation upto clearance for equipment installation	30 days	2026/5/11	2026/6/13	2026/4/23	2026/5/27	NA	NA	0%	No																																
334	1.5.3.1.4.4.3 Induced Draft fan (ID) foundation upto clearance for equipment installation	45 days	2026/5/11	2026/7/1	2026/4/23	2026/6/13	NA	NA	0%	No																																
335	1.5.3.1.4.4.4 Flue gas recirculation fan system foundation upto clearance for equipment	35 days	2026/5/11	2026/6/19	2026/4/23	2026/6/2	NA	NA	0%	No																																
336	1.5.3.1.4.4.5 Furnace cooling fan system foundation upto clearance for equipment	50 days	2026/5/11	2026/7/7	2026/4/23	2026/6/19	NA	NA	0%	No																																
337	1.5.3.1.5 Flue gas treatment	154 days	2025/12/13	2026/6/10	2025/12/13	2026/5/22	2025/12/13	NA	83%	No																																
338	1.5.3.1.5.1 Piling Work(Including Pile test)- Flue Gas Treatment Equipment Foundation (No Pile)	26 days	2025/12/13	2026/1/12	2025/12/13	2026/1/12	2025/12/13	2026/1/12	100%	No																																
339	1.5.3.1.5.2 Foundation Excavation- Flue Gas Treatment Equipment Foundation	58 days	2026/1/12	2026/3/19	2026/1/13	2026/1/23	2026/1/12	2026/																																		

Overall Project Schedule_Level 2																																																
ID	Task Name	Duration	Start	Finish	Baseline Start	Baseline Finish	Actual Start	Actual Finish	% Complete	Critical													'26													'27												
377	1.5.3.2.4.1 Underground circulating water pipe const	60 days	2026/6/4	2026/8/12	2026/1/31	2026/4/10	NA	NA	0%	No	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11									
378	1.5.3.2.4.1.1 Underground circulating water pipe construction （Including Cathodic protection）	60 days	2026/6/4	2026/8/12	2026/1/31	2026/4/10	NA	NA	0%	No																																						
379	1.5.3.2.4.2 Other underground piping work and cable	55 days	2026/5/28	2026/7/30	2026/1/31	2026/6/15	NA	NA	0%	No																																						
380	1.5.3.2.4.2.1 Underground piping work and cable duct - Main workshop & STG area	50 days	2026/5/28	2026/7/24	2026/1/31	2026/5/15	NA	NA	0%	No																																						
381	1.5.3.2.4.2.2 Underground piping work and cable du	5 days	2026/7/25	2026/7/30	2026/5/16	2026/6/15	NA	NA	0%	No																																						
382	1.5.3.2.5 Demineralized water treatment plant	118 days	2026/7/9	2026/11/23	2026/4/1	2026/8/15	NA	NA	0%	No																																						
383	1.5.3.2.5.1 Foundation Work （Including Underground grounding system）-Demineralized	40 days	2026/7/9	2026/8/24	2026/4/1	2026/5/16	NA	NA	0%	No																																						
384	1.5.3.2.5.2 Super structure-Demineralized water treat	50 days	2026/8/25	2026/10/21	2026/5/18	2026/7/14	NA	NA	0%	No																																						
385	1.5.3.2.5.3 Architectures work-Demineralized water tr	28 days	2026/10/22	2026/11/23	2026/7/15	2026/8/15	NA	NA	0%	No																																						
386	1.5.3.2.6 Demineralized water storage tank foundation	47 days	2026/8/25	2026/10/17	2026/5/18	2026/7/10	NA	NA	0%	No																																						
387	1.5.3.2.6.1 Foundation Excavation-Demineralized water storage tank foundation	4 days	2026/8/25	2026/8/28	2026/5/18	2026/5/21	NA	NA	0%	No																																						
388	1.5.3.2.6.2 Foundation work-Demineralized water storage tank foundation	15 days	2026/8/29	2026/9/15	2026/5/22	2026/6/8	NA	NA	0%	No																																						
389	1.5.3.2.6.3 Clearance for equipment installation-Demineralized water storage tank	28 days	2026/9/16	2026/10/17	2026/6/9	2026/7/10	NA	NA	0%	No																																						
390	1.5.3.2.7 Chemical Storage Building	70 days	2026/7/1	2026/9/19	2026/5/13	2026/8/1	NA	NA	0%	No																																						
391	1.5.3.2.7.1 Foundation Work （Including Underground grounding system）-Chemical Storage	30 days	2026/7/1	2026/8/4	2026/5/13	2026/6/16	NA	NA	0%	No																																						
392	1.5.3.2.7.2 Super structure-Chemical Storage Building	20 days	2026/8/5	2026/8/27	2026/6/17	2026/7/9	NA	NA	0%	No																																						
393	1.5.3.2.7.3 Architectures work-Chemical Storage Build	20 days	2026/8/28	2026/9/19	2026/7/10	2026/8/1	NA	NA	0%	No																																						
394	1.5.3.2.8 Cooling water chemical feed building	87 days	2026/9/1	2026/12/10	2026/7/31	2026/11/9	NA	NA	0%	No																																						
395	1.5.3.2.8.1 Foundation Work （Including Underground grounding system）-Cooling water	30 days	2026/9/1	2026/10/5	2026/7/31	2026/9/3	NA	NA	0%	No																																						
396	1.5.3.2.8.2 Super structure-Cooling water chemical fee	20 days	2026/10/6	2026/10/28	2026/9/4	2026/9/26	NA	NA	0%	No																																						
397	1.5.3.2.8.3 Architectures work-Cooling water chemical	37 days	2026/10/29	2026/12/10	2026/9/28	2026/11/9	NA	NA	0%	No																																						
398	1.5.3.2.9 Storm Water Retention Pond （Including Sum	124 days	2026/9/2	2027/1/23	2026/8/1	2026/12/2	NA	NA	0%	No																																						
399	1.5.3.2.10 Holding Pond and Emergency Pond	151 days	2026/6/19	2026/12/11	2026/5/1	2026/10/2	NA	NA	0%	No																																						
400	1.5.3.2.10.1 Foundation Excavation- Holding Pond and	10 days	2026/6/19	2026/6/30	2026/5/1	2026/5/12	NA	NA	0%	No																																						
401	1.5.3.2.10.2 Foundation slab- Holding Pond and Emerg	45 days	2026/7/1	2026/8/21	2026/5/13	2026/7/3	NA	NA	0%	No																																						
402	1.5.3.2.10.3 Pond wall- Holding Pond and Emergency f	45 days	2026/8/22	2026/10/13	2026/7/4	2026/8/25	NA	NA	0%	No																																						
403	1.5.3.2.10.4 Top slab- Holding Pond and Emergency Pc	51 days	2026/10/14	2026/12/11	2026/8/26	2026/10/2	NA	NA	0%	No																																						
404	1.5.3.2.10.5 Oil/Water Separator- Holding Pond and Ei	150 days	2026/6/20	2026/12/11	2026/5/2	2026/10/2	NA	NA	0%	No																																						
405	1.5.3.2.11 Wastewater Monitoring Room (WMR)	70 days	2026/9/2	2026/11/21	2026/8/1	2026/10/2	NA	NA	0%	No																																						
406	1.5.3.2.11.1 Foundation Work （Including Underground grounding system）-WMR	10 days	2026/9/2	2026/9/12	2026/8/1	2026/8/12	NA	NA	0%	No																																						
407	1.5.3.2.11.2 Super structure-WMR	35 days	2026/9/14	2026/10/23	2026/8/13	2026/9/22	NA	NA	0%	No																																						
408	1.5.3.2.11.3 Architectures work-WMR	25 days	2026/10/24	2026/11/21	2026/9/23	2026/10/2	NA	NA	0%	No																																						
409	1.5.3.2.11.4 Final Inspection pit-WMR	28 days	2026/10/21	2026/11/21	2026/9/19	2026/10/2	NA	NA	0%	No																																						
410	1.5.3.2.12 Fire water pump shelter	80 days	2026/6/3	2026/9/3	2026/1/20	2026/4/22	NA	NA	0%	No																																						
411	1.5.3.2.12.1 Foundation Work （Including Underground grounding system）- Fire Water Pump	50 days	2026/6/3	2026/7/30	2026/1/20	2026/3/18	NA	NA	0%	No																																						
412	1.5.3.2.12.2 Super structure- Fire Water Pump Shelter	30 days	2026/7/31	2026/9/3	2026/3/19	2026/4/22	NA	NA	0%	No																																						
413	1.5.3.2.13 Chimney foundation (Stack)	101 days	2026/6/9	2026/10/3	2026/1/31	2026/10/9	NA	NA	0%	No																																						
414	1.5.3.2.13.1 Piling - Chimney	30 days	2026/6/9	2026/7/13	2026/1/31	2026/4/17	NA	NA	0%	No																																						
415	1.5.3.2.13.2 Foundation basement casting- Chimney f	26 days	2026/7/14	2026/8/12	2026/4/18	2026/5/22	NA	NA	0%	No																																						
416	1.5.3.2.13.3 Foundation casting- Chimney foundation	30 days	2026/8/13	2026/9/16	2026/5/23	2026/7/31	NA	NA	0%	No																																						
417	1.5.3.2.13.4 Clearance for installation- Chimney found	15 days	2026/9/17	2026/10/3	2026/8/1	2026/10/9	NA	NA	0%	No																																						
418	1.5.3.2.14 Diesel oil tank and diesel oil pump foundation and clearance for equipment installation	53 days	2026/8/14	2026/10/14	2026/8/29	2026/10/2	NA	NA	0%	No																																						
419	1.5.3.2.15 CEMS control room	70 days	2026/7/14	2026/10/2	2026/4/18	2026/7/8	NA	NA	0%	No																																						
420	1.5.3.2.15.1 Foundation Work （Including Underground grounding system）-CEMS control	30 days	2026/7/14	2026/8/17	2026/4/18	2026/5/22	NA	NA	0%	No																																						
421	1.5.3.2.15.2 Super structure-CEMS control room	20 days	2026/8/18	2026/9/9	2026/5/23	2026/6/15	NA	NA	0%	No																																						
422	1.5.3.2.15.3 Architectures work-CEMS control room	20 days	2026/9/10	2026/10/2	2026/6/16	2026/7/8	NA	NA	0%	No																																						
423	1.5.3.2.16 Transformer Foundation	56 days	2026/8/5	2026/10/8	2026/6/17	2026/8/20	NA	NA	0%	No																																						
424	1.5.3.2.16.1 Foundation Excavation- Transformer Fou	21 days	2026/8/5	2026/8/28	2026/6/17	2026/7/10	NA	NA	0%	No																																						
425	1.5.3.2.16.2 Foundation work- Transformer Foundatic	25 days	2026/8/29	2026/9/26	2026/7/11	2026/8/8	NA	NA	0%	No																																						
426	1.5.3.2.16.3 Clearance for equipment installation- Tra	10 days	2026/9/28	2026/10/8	2026/8/10	2026/8/20	NA	NA	0%	No																																						
427	1.5.3.2.17 Bottom Ash Conveyer Foundation	20 days	2026/5/5	2026/5/27	2026/3/31	2026/5/4	NA	NA	0%	No																																						
428	1.5.3.2.18 Fly Ash Silo Foundation	30 days	2026/6/9	2026/7/13	2026/5/5	2026/6/8	NA	NA	0%	No																																						
429	1.5.3.2.19 Pipe Rack Foundation and Installation (Incl.Pipe bridge and Pipe Support)	52 days	2026/11/23	2027/1/21	2026/9/15	2026/11/1	NA	NA	0%	No																		</																				

Overall Project Schedule_Level 2																																									
ID	Task Name	Duration	Start	Finish	Baseline Start	Baseline Finish	Actual Start	Actual Finish	% Complete	Critical	7	8	9	10	11	12	' 26	1	2	3	4	5	6	7	8	9	10	11	' 27	1	2	3	4	5	6	7	8	9	10	11	
432	1.5.3.3.1.1 Foundation Work (Including Underground grounding system) - Administration	50 days	2026/9/2	2026/10/29	2026/8/1	2026/9/28	NA	NA	0%	No																															
433	1.5.3.3.1.2 Super structure- Administration Building	52 days	2026/10/30	2026/12/29	2026/9/29	2026/11/2	NA	NA	0%	No																															
434	1.5.3.3.1.3 Architectures work (Include decoration, Septic tank) - Administration Building	52 days	2026/12/30	2027/2/27	2026/11/28	2027/1/27	NA	NA	0%	No																															
435	1.5.3.3.2 Warehouse and Maintenance Workshop(WH & Maintenance Workshop)	180 days	2026/9/2	2027/3/30	2026/8/13	2027/4/1	NA	NA	0%	No																															
436	1.5.3.3.2.1 Foundation Work (Including Underground grounding system) - WH & WS	30 days	2026/9/2	2026/10/6	2026/8/13	2026/9/16	NA	NA	0%	No																															
437	1.5.3.3.2.2 Super structure - WH & WS	45 days	2026/10/7	2026/11/27	2026/9/17	2026/11/7	NA	NA	0%	No																															
438	1.5.3.3.2.3 Overhead Crane clearance for equipment installation	45 days	2026/11/28	2027/1/19	2026/11/9	2026/12/3	NA	NA	0%	No																															
439	1.5.3.3.2.4 Architectures work (Including Septic tank)	60 days	2027/1/20	2027/3/30	2026/12/31	2027/3/10	NA	NA	0%	No																															
440	1.5.3.3.3 Truck Weighing Scale & Control Building	121 days	2026/9/2	2027/1/20	2026/8/1	2026/12/1	NA	NA	0%	No																															
441	1.5.3.3.3.1 Foundation Work (Including Weighbridge foundation, Underground grounding system) -Truck Weighing Scale & Control Building	30 days	2026/9/2	2026/10/6	2026/8/1	2026/9/4	NA	NA	0%	No																															
442	1.5.3.3.3.2 Weighbridge installation-Truck Weighing Scale & Control Building	30 days	2026/10/7	2026/11/10	2026/9/5	2026/10/9	NA	NA	0%	No																															
443	1.5.3.3.3.3 Super structure-Truck Weighing Scale & Control Building	40 days	2026/10/7	2026/11/21	2026/9/5	2026/10/2	NA	NA	0%	No																															
444	1.5.3.3.3.4 Architectures work-Truck Weighing Scale & Control Building	51 days	2026/11/23	2027/1/20	2026/10/22	2026/12/1	NA	NA	0%	No																															
445	1.5.3.3.4 Guard House	49 days	2026/9/2	2026/10/28	2026/8/1	2026/9/26	NA	NA	0%	No																															
446	1.5.3.3.4.1 Foundation Work (Including Underground grounding system) - Guard House	10 days	2026/9/2	2026/9/12	2026/8/1	2026/8/12	NA	NA	0%	No																															
447	1.5.3.3.4.2 Super structure- Guard House	17 days	2026/9/14	2026/10/2	2026/8/13	2026/9/1	NA	NA	0%	No																															
448	1.5.3.3.4.3 Architectures work (Including Septic tank)	22 days	2026/10/3	2026/10/28	2026/9/2	2026/9/26	NA	NA	0%	No																															
449	1.5.3.3.5 Plant internal road	45 days	2027/2/12	2027/4/30	2026/2/12	2026/4/4	2027/2/12	NA	48%	No																															
450	1.5.3.3.6 Plant Virescence	60 days	2027/3/31	2027/6/8	2026/2/12	2026/4/22	NA	NA	0%	No																															
451	1.5.3.3.7 Site Grading (Backfilling)	30 days	2027/2/12	2027/3/18	2026/2/12	2026/8/5	2027/2/12	NA	35%	No																															
452	1.5.3.3.8 Road Lighting	30 days	2027/5/1	2027/6/4	2026/4/6	2026/5/9	NA	NA	0%	No																															
453	1.5.3.3.9 Parking area foundation	20 days	2027/5/1	2027/5/24	2026/8/6	2026/9/26	NA	NA	0%	No																															
454	1.5.4 Mechanical Work	302 days	2026/5/11	2027/4/27	2026/4/23	2027/4/16	NA	NA	0%	No																															
455	1.5.4.1 Main equipment installation	302 days	2026/5/11	2027/4/27	2026/4/23	2027/4/16	NA	NA	0%	No																															
456	1.5.4.1.1 Incinerator installation	120 days	2026/5/11	2026/9/26	2026/4/23	2026/10/1	NA	NA	0%	No																															
457	1.5.4.1.1.1 Grate steel structure (Supplied by boiler supplier)	20 days	2026/5/11	2026/6/2	2026/4/23	2026/5/25	NA	NA	0%	No																															
458	1.5.4.1.1.2 Bottom ash remover-Incinerator	5 days	2026/6/3	2026/6/8	2026/5/26	2026/5/30	NA	NA	0%	No																															
459	1.5.4.1.1.3 Bottom ash conveyor-Incinerator	5 days	2026/6/9	2026/6/13	2026/6/1	2026/6/5	NA	NA	0%	No																															
460	1.5.4.1.1.4 Incinerator ash hopper-Incinerator	5 days	2026/6/15	2026/6/19	2026/6/6	2026/6/11	NA	NA	0%	No																															
461	1.5.4.1.1.5 Grate installation-Incinerator	18 days	2026/6/20	2026/7/10	2026/6/12	2026/7/2	NA	NA	0%	No																															
462	1.5.4.1.1.6 Feeder installation-Incinerator	5 days	2026/7/11	2026/7/16	2026/7/8	2026/7/13	NA	NA	0%	No																															
463	1.5.4.1.1.7 Chute installation-Incinerator	3 days	2026/8/14	2026/8/17	2026/8/29	2026/9/1	NA	NA	0%	No																															
464	1.5.4.1.1.8 Fuel hopper installation-Incinerator	5 days	2026/8/18	2026/8/22	2026/9/2	2026/9/7	NA	NA	0%	No																															
465	1.5.4.1.1.9 Hydrostatic oil station-Incinerator	30 days	2026/8/24	2026/9/26	2026/9/8	2026/10/1	NA	NA	0%	No																															
466	1.5.4.1.2 Boiler installation	240 days	2026/7/11	2027/4/16	2026/7/3	2027/4/16	NA	NA	0%	No																															
467	1.5.4.1.2.1 Boiler steel structure-Boiler	24 days	2026/7/11	2026/8/7	2026/7/3	2026/7/25	NA	NA	0%	No																															
468	1.5.4.1.2.2 Board girder and Drum lifting-Boiler	5 days	2026/8/8	2026/8/13	2026/7/27	2026/7/29	NA	NA	0%	No																															
469	1.5.4.1.2.3 Water wall installation-Boiler	20 days	2026/8/14	2026/9/5	2026/7/30	2026/8/21	NA	NA	0%	No																															
470	1.5.4.1.2.4 Superheater-Boiler	25 days	2026/9/7	2026/10/5	2026/8/22	2026/9/18	NA	NA	0%	No																															
471	1.5.4.1.2.5 Economizer-Boiler	24 days	2026/10/6	2026/11/2	2026/9/19	2026/10/1	NA	NA	0%	No																															
472	1.5.4.1.2.6 Heating surface sealing-Boiler	45 days	2026/11/3	2026/12/24	2026/10/17	2026/12/8	NA	NA	0%	No																															
473	1.5.4.1.2.7 Main body pipeline-Boiler	40 days	2026/11/3	2026/12/18	2026/10/17	2026/12/8	NA	NA	0%	No																															
474	1.5.4.1.2.8 Boiler ash hopper-Boiler	10 days	2026/11/3	2026/11/13	2026/10/17	2026/10/2	NA	NA	0%	No																															
475	1.5.4.1.2.9 Boiler ash conveyor-Boiler	10 days	2026/11/14	2026/11/25	2026/10/29	2026/11/9	NA	NA	0%	No																															
476	1.5.4.1.2.10 Tail flue gas duct-Boiler	10 days	2026/11/3	2026/11/13	2026/10/17	2026/10/2	NA	NA	0%	No																															
477	1.5.4.1.2.11 Temporary pipeline (For Hydrostatic test)	9 days	2026/12/19	2026/12/29	2026/12/9	2026/12/1	NA	NA	0%	No																															
478	1.5.4.1.2.12 Hydrostatic test-Boiler	3 days	2026/12/30	2027/1/1	2026/12/19	2026/12/2	NA	NA	0%	No																															
479	1.5.4.1.2.13 Fire brick-Boiler	45 days	2027/1/2	2027/2/23	2026/12/23	2027/2/12	NA	NA	0%	No																															
480	1.5.4.1.2.14 Insulation-Boiler	45 days	2027/2/24	2027/																																					

Overall Project Schedule_Level 2																																							
ID	Task Name	Duration	Start	Finish	Baseline Start	Baseline Finish	Actual Start	Actual Finish	% Complete	Critical	7	8	9	10	11	12	' 26 1	2	3	4	5	6	7	8	9	10	11	12	' 27 1	2	3	4	5	6	7	8	9	10	11
494	1.5.4.1.4.2 Bag filler- Flue Gas Treatment	40 days	2026/8/15	2026/9/30	2026/6/15	2026/7/30	NA	NA	0%	No																													
495	1.5.4.1.4.3 Lime slurry preparation and supply system- Flue Gas Treatment	45 days	2026/10/1	2026/11/21	2026/7/31	2026/9/21	NA	NA	0%	No																													
496	1.5.4.1.4.4 Dry injection system- Flue Gas Treatment	30 days	2026/10/1	2026/11/4	2026/7/31	2026/9/3	NA	NA	0%	No																													
497	1.5.4.1.4.5 Activated carbon injection system- Flue Gas Treatment	20 days	2026/10/1	2026/10/23	2026/7/31	2026/8/22	NA	NA	0%	No																													
498	1.5.4.1.4.6 Fly ash conveying and storage system- Flue Gas Treatment	30 days	2026/11/26	2026/12/30	2026/11/10	2026/12/1	NA	NA	0%	No																													
499	1.5.4.1.4.7 SNCR installation- Flue Gas Treatment	30 days	2026/10/1	2026/11/4	2026/10/9	2026/11/1	NA	NA	0%	No																													
500	1.5.4.1.4.8 Flue gas treatment system piping- Flue Gas Treatment	40 days	2026/12/31	2027/2/15	2026/12/15	2027/2/10	NA	NA	0%	No																													
501	1.5.4.1.4.9 Insulation- Flue Gas Treatment	50 days	2027/2/16	2027/4/14	2027/2/11	2027/4/16	NA	NA	0%	No																													
502	1.5.4.2 Auxiliary equipment & system installation	205 days	2026/8/6	2027/4/1	2026/6/25	2027/2/1	NA	NA	0%	No																													
503	1.5.4.2.1 Service and firefighting water tank installation	60 days	2026/9/10	2026/11/18	2026/6/25	2026/9/2	NA	NA	0%	No																													
504	1.5.4.2.2 Cooling Water System	120 days	2026/9/22	2027/2/8	2026/8/4	2026/12/2	NA	NA	0%	No																													
505	1.5.4.2.2.1 Cooling Tower, Circulating cooling water pump incl.Motor Installation - Cooling Water System	60 days	2026/9/22	2026/11/30	2026/8/4	2026/10/1	NA	NA	0%	No																													
506	1.5.4.2.2.2 Piping Installation (Incl. Painting & Insulation) - Cooling Water System	60 days	2026/12/1	2027/2/8	2026/10/13	2026/12/2	NA	NA	0%	No																													
507	1.5.4.2.3 Cooling water chemical feed system	45 days	2026/12/11	2027/2/1	2026/11/10	2026/12/3	NA	NA	0%	No																													
508	1.5.4.2.3.1 Mechanical Installation - Cooling Water Chemical Feed System	5 days	2026/12/11	2026/12/16	2026/11/10	2026/11/1	NA	NA	0%	No																													
509	1.5.4.2.3.2 Piping Installation (Incl. Painting & Insulation) - Cooling Water Chemical Feed System	40 days	2026/12/17	2027/2/1	2026/11/16	2026/12/3	NA	NA	0%	No																													
510	1.5.4.2.4 Demin Water Distribution System	60 days	2026/11/24	2027/2/1	2026/8/17	2026/10/2	NA	NA	0%	No																													
511	1.5.4.2.4.1 Mechanical Installation - Demin Water Distribution System	10 days	2026/11/24	2026/12/4	2026/8/17	2026/8/27	NA	NA	0%	No																													
512	1.5.4.2.4.2 Piping Installation (Incl. Painting & Insulation) - Demin Water Distribution System	50 days	2026/12/5	2027/2/1	2026/8/28	2026/10/2	NA	NA	0%	No																													
513	1.5.4.2.5 Compressed air system	30 days	2026/9/15	2026/10/19	2026/9/22	2026/10/2	NA	NA	0%	No																													
514	1.5.4.2.5.1 Mechanical Installation - Compressed Air System	5 days	2026/9/15	2026/9/19	2026/9/22	2026/9/26	NA	NA	0%	No																													
515	1.5.4.2.5.2 Piping Installation (Incl. Painting & Insulation) - Compressed Air System	25 days	2026/9/21	2026/10/19	2026/9/28	2026/10/2	NA	NA	0%	No																													
516	1.5.4.2.6 Water and Steam sampling and analysis system	30 days	2026/10/24	2026/11/27	2026/11/9	2026/12/1	NA	NA	0%	No																													
517	1.5.4.2.6.1 Mechanical Installation - Water and Steam Sampling and Analysis System	5 days	2026/10/24	2026/10/29	2026/11/9	2026/11/1	NA	NA	0%	No																													
518	1.5.4.2.6.2 Piping Installation (Incl. Painting & Insulation) - Water and Steam Sampling and Analysis	25 days	2026/10/30	2026/11/27	2026/11/14	2026/12/1	NA	NA	0%	No																													
519	1.5.4.2.7 Steel Chimney installation	20 days	2026/10/5	2026/10/27	2026/10/10	2026/11/2	NA	NA	0%	No																													
520	1.5.4.2.8 Diesel oil tank and diesel oil pump installation	60 days	2026/10/15	2026/12/23	2026/10/30	2027/1/7	NA	NA	0%	No																													
521	1.5.4.2.9 Boiler Auxiliary system	60 days	2026/8/6	2026/10/14	2026/8/17	2026/10/2	NA	NA	0%	No																													
522	1.5.4.2.9.1 Primary fan system (Including Motor System)	60 days	2026/8/6	2026/10/14	2026/8/17	2026/10/2	NA	NA	0%	No																													
523	1.5.4.2.9.1.1 fan Installation-Primary fan system	10 days	2026/8/6	2026/8/17	2026/8/17	2026/8/27	NA	NA	0%	No																													
524	1.5.4.2.9.1.2 Piping Installation-Primary fan system	50 days	2026/8/18	2026/10/14	2026/8/28	2026/10/2	NA	NA	0%	No																													
525	1.5.4.2.9.2 Secondary fan system (Including Motor System)	60 days	2026/8/6	2026/10/14	2026/8/17	2026/10/2	NA	NA	0%	No																													
526	1.5.4.2.9.2.1 fan Installation-Secondary fan system	10 days	2026/8/6	2026/8/17	2026/8/17	2026/8/27	NA	NA	0%	No																													
527	1.5.4.2.9.2.2 Piping Installation-Secondary fan system	50 days	2026/8/18	2026/10/14	2026/8/28	2026/10/2	NA	NA	0%	No																													
528	1.5.4.2.9.3 Induced Draft fan system (Including Motor)	60 days	2026/8/6	2026/10/14	2026/8/17	2026/10/2	NA	NA	0%	No																													
529	1.5.4.2.9.3.1 fan Installation-Induced Draft fan system	10 days	2026/8/6	2026/8/17	2026/8/17	2026/8/27	NA	NA	0%	No																													
530	1.5.4.2.9.3.2 Piping Installation-Induced Draft fan system	50 days	2026/8/18	2026/10/14	2026/8/28	2026/10/2	NA	NA	0%	No																													
531	1.5.4.2.9.4 Flue gas recirculation fan system installation	60 days	2026/8/6	2026/10/14	2026/8/17	2026/10/2	NA	NA	0%	No																													
532	1.5.4.2.9.4.1 fan Installation-Flue gas recirculation	10 days	2026/8/6	2026/8/17	2026/8/17	2026/8/27	NA	NA	0%	No																													
533	1.5.4.2.9.4.2 Piping Installation-Flue gas recirculation	50 days	2026/8/18	2026/10/14	2026/8/28	2026/10/2	NA	NA	0%	No																													
534	1.5.4.2.9.5 Furnace cooling fan system (Including Motor)	60 days	2026/8/6	2026/10/14	2026/8/17	2026/10/2	NA	NA	0%	No																													
535	1.5.4.2.9.5.1 fan Installation-Furnace cooling fan system	10 days	2026/8/6	2026/8/17	2026/8/17	2026/8/27	NA	NA	0%	No																													
536	1.5.4.2.9.5.2 Piping Installation-Furnace cooling fan system	50 days	2026/8/18	2026/10/14	2026/8/28	2026/10/2	NA	NA	0%	No																													
537	1.5.4.2.9.6 Insulation	60 days	2026/8/6	2026/10/14	2026/8/17	2026/10/2	NA	NA	0%	No																													
538	1.5.4.2.10 STG Auxiliary systems	60 days	2027/1/22	2027/4/1	2026/11/24	2027/2/1	NA	NA	0%	Yes																													
539	1.5.4.2.10.1 Vacuum pumping system	30 days	2027/1/22	2027/2/25	2026/11/24	2026/12/2	NA	NA	0%	No																													
540	1.5.4.2.10.1.1 Mechanical Installation - Vacuum Purification	5 days	2027/1/22	2027/1/27	2026/11/24	2026/11/2	NA	NA	0%	No																													
541	1.5.4.2.10.1.2 Piping Installation (Incl. Painting & Insulation) - Vacuum Pumping System	25 days	2027/1/28	2027/2/25	2026/11/30	2026/12/2	NA	NA	0%	No																													
542	1.5.4.2.10.2 Condensate water system	45 days	2027/1/22	2027/3/15	2026/11/24	2027/1/14	NA	NA	0%	No																													
543	1.5.4.2.10.2.1 Mechanical Installation - Condensate Water System	5 days	2027/1/22	2027/1/27	2026/11/24	2026/11/2	NA	NA																															

Overall Project Schedule_Level 2																																									
ID	Task Name	Duration	Start	Finish	Baseline Start	Baseline Finish	Actual Start	Actual Finish	% Complete	Critical	7	8	9	10	11	12	' 26	1	2	3	4	5	6	7	8	9	10	11	' 27	1	2	3	4	5	6	7	8	9	10	11	
551	1.5.4.2.10.6.1 Mechanical Installation - Turbine Extr	10 days	2027/1/22	2027/2/2	2026/11/24	2026/12/4	NA	NA	0%	Yes																															
552	1.5.4.2.10.6.2 Piping Installation (Incl. Painting & Insulation) - Turbine Extraction Steam System	50 days	2027/2/3	2027/4/1	2026/12/5	2027/2/1	NA	NA	0%	Yes																															
553	1.5.4.2.10.7 Insulation	60 days	2027/1/22	2027/4/1	2026/11/24	2027/2/1	NA	NA	0%	Yes																															
554	1.5.5 Electrical Work	152 days	2026/7/17	2027/1/9	2026/7/22	2026/11/2	NA	NA	0%	No																															
555	1.5.5.1 22kV system	20 days	2026/11/3	2026/11/25	2026/8/28	2026/9/18	NA	NA	0%	No																															
556	1.5.5.1.1 11kV/22kV Transformer installation	10 days	2026/11/14	2026/11/25	2026/9/8	2026/9/18	NA	NA	0%	No																															
557	1.5.5.1.2 22kV Swithgear and Distribution system	10 days	2026/11/3	2026/11/13	2026/8/28	2026/9/8	NA	NA	0%	No																															
558	1.5.5.2 Relay and protection system	21 days	2026/11/3	2026/11/26	2026/8/26	2026/10/2	NA	NA	0%	No																															
559	1.5.5.2.1 Relay and protection panel	20 days	2026/11/4	2026/11/26	2026/9/5	2026/9/28	NA	NA	0%	No																															
560	1.5.5.2.2 Revenue meter and synchronization	20 days	2026/11/4	2026/11/26	2026/9/10	2026/10/2	NA	NA	0%	No																															
561	1.5.5.2.3 Battery system	10 days	2026/11/3	2026/11/13	2026/8/26	2026/9/5	NA	NA	0%	No																															
562	1.5.5.2.4 DC, UPS system	10 days	2026/11/4	2026/11/14	2026/8/27	2026/9/7	NA	NA	0%	No																															
563	1.5.5.2.5 Communication system (telephone, paging, int	20 days	2026/11/4	2026/11/26	2026/8/27	2026/9/18	NA	NA	0%	No																															
564	1.5.5.3 11kV system	20 days	2026/11/3	2026/11/25	2026/8/28	2026/9/26	NA	NA	0%	No																															
565	1.5.5.3.1 Generator outlet cabinet	20 days	2026/11/3	2026/11/25	2026/8/28	2026/9/19	NA	NA	0%	No																															
566	1.5.5.3.2 11kV Switchgear	20 days	2026/11/3	2026/11/25	2026/8/28	2026/9/19	NA	NA	0%	No																															
567	1.5.5.3.3 11kV VFD	20 days	2026/11/3	2026/11/25	2026/9/4	2026/9/26	NA	NA	0%	No																															
568	1.5.5.4 400V system	59 days	2026/9/18	2026/11/25	2026/9/9	2026/10/1	NA	NA	0%	No																															
569	1.5.5.4.1 11kV/400V Transformer installation	5 days	2026/10/12	2026/10/16	2026/9/9	2026/9/14	NA	NA	0%	No																															
570	1.5.5.4.2 Low voltage cabinet installation	20 days	2026/11/3	2026/11/25	2026/9/10	2026/10/2	NA	NA	0%	No																															
571	1.5.5.4.3 LV frequency converter cabinet	10 days	2026/11/3	2026/11/13	2026/9/10	2026/9/21	NA	NA	0%	No																															
572	1.5.5.4.4 Emergency Diesel Generator	10 days	2026/9/18	2026/9/29	2026/10/3	2026/10/1	NA	NA	0%	No																															
573	1.5.5.5 Cable and raceway system installation	55 days	2026/11/2	2027/1/4	2026/9/14	2026/11/1	NA	NA	0%	No																															
574	1.5.5.6 Cable laying and wiring (Electric system)	45 days	2026/11/13	2027/1/4	2026/9/25	2026/11/1	NA	NA	0%	No																															
575	1.5.5.7 Cable laying and wiring (Mechanical equipment power supply system)	50 days	2026/11/13	2027/1/9	2026/9/25	2026/11/2	NA	NA	0%	No																															
576	1.5.5.8 Grounding and Lightning Protection System	45 days	2026/8/14	2026/10/5	2026/8/4	2026/9/24	NA	NA	0%	No																															
577	1.5.5.9 Lighting and Small Power	30 days	2026/7/17	2026/8/20	2026/7/22	2026/8/25	NA	NA	0%	No																															
578	1.5.6 C&I Work	141 days	2026/10/7	2027/3/19	2026/6/16	2027/1/11	NA	NA	0%	No																															
579	1.5.6.1 DCS system installation	45 days	2026/11/28	2027/1/19	2026/10/1	2026/11/2	NA	NA	0%	No																															
580	1.5.6.2 CCTV system	111 days	2026/11/11	2027/3/19	2026/8/6	2026/12/1	NA	NA	0%	No																															
581	1.5.6.3 Fire fighting and fire alarm system	100 days	2026/10/7	2027/1/30	2026/6/16	2026/12/7	NA	NA	0%	No																															
582	1.5.6.4 CEMS system and Emission Panel at entrance gate	60 days	2026/10/28	2027/1/5	2026/11/3	2027/1/11	NA	NA	0%	No																															
583	1.5.6.5 HVAC syetem (Control room and electric distributio	32 days	2026/11/3	2026/12/9	2026/8/26	2026/10/1	NA	NA	0%	No																															
584	1.5.6.6 Source component installation	60 days	2026/11/11	2027/1/19	2026/8/24	2026/10/3	NA	NA	0%	No																															
585	1.5.6.7 Instrument equipment installation	60 days	2026/11/11	2027/1/19	2026/8/24	2026/10/3	NA	NA	0%	No																															
586	1.5.6.8 Cable and raceway system installation	40 days	2026/11/2	2026/12/17	2026/9/14	2026/10/2	NA	NA	0%	No																															
587	1.5.6.9 Cable laying and wiring	50 days	2026/11/13	2027/1/9	2026/9/25	2026/11/2	NA	NA	0%	No																															
588	1.6 Testing/Commissioning	275 days	2026/11/28	2027/10/14	2026/10/3	2027/10/1	NA	NA	0%	Yes																															
589	1.6.1 System testing and commissioning	171 days	2026/11/28	2027/6/15	2026/10/3	2027/6/19	NA	NA	0%	Yes																															
590	1.6.1.1 Wastewater treatment system	10 days	2027/1/25	2027/2/4	2026/12/24	2027/1/4	NA	NA	0%	No																															
591	1.6.1.2 Testing and commissioning for electrical system	7 days	2027/1/5	2027/1/12	2026/11/23	2026/11/3	NA	NA	0%	No																															
592	1.6.1.3 HVAC syetem (Control room and electric distributio	15 days	2026/12/10	2026/12/26	2026/10/3	2026/10/2	NA	NA	0%	No																															
593	1.6.1.4 Back energized power	3 days	2027/1/13	2027/1/15	2026/12/1	2026/12/3	NA	NA	0%	No																															
594	1.6.1.5 Cooling tower commissioning	7 days	2027/1/16	2027/1/23	2026/12/4	2026/12/1	NA	NA	0%	No																															
595	1.6.1.6 Cooling water system flushing and commissioning	10 days	2027/2/9	2027/2/19	2027/1/5	2027/1/15	NA	NA	0%	No																															
596	1.6.1.7 Cooling water chemical feed system commissioning	6 days	2027/2/2	2027/2/8	2027/1/1	2027/1/7	NA	NA	0%	No																															
597	1.6.1.8 Compressed air system	20 days	2027/2/20	2027/3/15	2027/1/16	2027/2/8	NA	NA	0%	No																															
598	1.6.1.9 Producing qualified water	12 days	2027/3/16	2027/3/29	2027/2/9	2027/2/22	NA	NA	0%	No																															
599	1.6.1.10 Test and commissioning DCS	85 days	2027/1/20	2027/4/28	2026/12/4	2027/3/12	NA	NA	0%	No																															
600	1.6.1.11 CEMS system commissioning and testing																																								

